

**SIEMENS INDUSTRY, INC.**  
**SMART INFRASTRUCTURE**

**Valve Submittal - Water**

|                  |              |                      |                     |              |          |
|------------------|--------------|----------------------|---------------------|--------------|----------|
| <b>LOCATION:</b> | NEW YORK, NY | <b>PROJECT NAME:</b> | 7TS 29-31 SNOWFLAKE | <b>DATE:</b> | 07/22/26 |
| <b>JOB NO:</b>   | 44OP-420147  |                      |                     | <b>PAGE:</b> | 1        |
| <b>ENGR:</b>     | PP           |                      |                     | <b>REV:</b>  |          |

|                                                                                                           |                                                                                      |
|-----------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------|
| <b>GENERAL NOTES:</b>                                                                                     | <b>UNITS:</b>                                                                        |
| 1. All valves 2-1/2" and larger have flanged ends, 2" and smaller have screwed ends.                      | Steam inlet pressure, actual pressure drop, and shut off pressure indicated in PSIG. |
| 2. All control valves and wells shall be installed by the mechanical contractor.                          |                                                                                      |
| 3. Standard abbreviations used on control valves are:                                                     |                                                                                      |
| <b>BODY TYPES:</b> 3W - Three way; 2W - Two way; A - Angle; N.C. - Normally Closed; N.O. - Normally Open; | <b>ACTUATOR TYPES:</b> SR - Spring Return; NSR - No Spring Return                    |
| NOC - Ball Valve can be N.O. or N.C.; BF - Butterfly Valve; DS - Double Seated;                           | CR - Capacitor Driven Return; DA - Double Acting                                     |

| Valve ID/<br>Location | Qty | Product Number | Valve Size | Body Type | Body Style | Actual Cv | Actuator Type | Design P. Drop (psi) | Required Flow (gpm) | Min (gpm) | Max (gpm) | Preset (gpm) | Steam Inlet | Press Drop (psi) | Valve Spec Sheet | Shut Off | ANSI Class | Comment |
|-----------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|
|-----------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|

| Mechanical System: AC |   |            |      |    |      |        |       | WATER COOLED AC (MECH)    |        |     |     |              |  |  |  |
|-----------------------|---|------------|------|----|------|--------|-------|---------------------------|--------|-----|-----|--------------|--|--|--|
| V-1                   | 1 | 172E-10321 | 1.25 | 2W | Ball | 100.00 | NC-SR | -----ISOLATION VALVE----- | 154038 | 200 | 250 | CRAC-29-1IVR |  |  |  |
| V-2                   | 1 | 172E-10321 | 1.25 | 2W | Ball | 100.00 | NC-SR | -----ISOLATION VALVE----- | 154038 | 200 | 250 | CRAC-29-1IVS |  |  |  |
| V-3                   | 1 | 172E-10321 | 1.25 | 2W | Ball | 100.00 | NC-SR | -----ISOLATION VALVE----- | 154038 | 200 | 250 | CRAC-30-1IVR |  |  |  |
| V-4                   | 1 | 172E-10321 | 1.25 | 2W | Ball | 100.00 | NC-SR | -----ISOLATION VALVE----- | 154038 | 200 | 250 | CRAC-30-1IVS |  |  |  |
| V-5                   | 1 | 172E-10321 | 1.25 | 2W | Ball | 100.00 | NC-SR | -----ISOLATION VALVE----- | 154038 | 200 | 250 | CRAC-31-1IVR |  |  |  |
| V-6                   | 1 | 172E-10321 | 1.25 | 2W | Ball | 100.00 | NC-SR | -----ISOLATION VALVE----- | 154038 | 200 | 250 | CRAC-31-1IVS |  |  |  |

|                               |   |           |      |    |       |      |       |   |                              |     |     |     |    |        |         |     |     |              |
|-------------------------------|---|-----------|------|----|-------|------|-------|---|------------------------------|-----|-----|-----|----|--------|---------|-----|-----|--------------|
| <b>Mechanical System: FPB</b> |   |           |      |    |       |      |       |   | <b>FAN POWERED BOX W/HWR</b> |     |     |     |    |        |         |     |     |              |
| V-1                           | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                         | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-3 HCV |
| V-2                           | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                         | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-29-5 HCV |
| V-3                           | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                         | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-6 HCV |
| V-4                           | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                         | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-8 HCV |
| V-5                           | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                         | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-10HCV |
| V-6                           | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                         | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-29-11HCV |

NOTES: All control valves and wells shall be installed by the heating contractor.

**SIEMENS INDUSTRY, INC.**  
**SMART INFRASTRUCTURE**

**Valve Submittal - Water**

|                  |              |                      |                     |              |          |
|------------------|--------------|----------------------|---------------------|--------------|----------|
| <b>LOCATION:</b> | NEW YORK, NY | <b>PROJECT NAME:</b> | 7TS 29-31 SNOWFLAKE | <b>DATE:</b> | 07/22/26 |
| <b>JOB NO:</b>   | 44OP-420147  |                      |                     | <b>PAGE:</b> | 2        |
| <b>ENGR:</b>     | PP           |                      |                     | <b>REV:</b>  |          |

**GENERAL NOTES:**

1. All valves 2-1/2" and larger have flanged ends, 2" and smaller have screwed ends.
2. All control valves and wells shall be installed by the mechanical contractor.
3. Standard abbreviations used on control valves are:

**BODY TYPES:** 3W - Three way; 2W - Two way; A - Angle; N.C. - Normally Closed; N.O. - Normally Open;  
NOC - Ball Valve can be N.O. or N.C.; BF - Butterfly Valve; DS - Double Seated;

**UNITS:**

Steam inlet pressure, actual pressure drop, and shut off pressure indicated in PSIG.

**ACTUATOR TYPES:** SR - Spring Return; NSR - No Spring Return  
CR - Capacitor Driven Return; DA - Double Acting

| Valve ID/<br>Location | Qty | Product Number | Valve Size | Body Type | Body Style | Actual Cv | Actuator Type | Design P. Drop (psi) | Required Flow (gpm) | Min (gpm) | Max (gpm) | Preset (gpm) | Steam Inlet | Press Drop (psi) | Valve Spec Sheet | Shut Off | ANSI Class | Comment |
|-----------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|
|-----------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|

**Mechanical System: FPB**

**FAN POWERED BOX W/HWR**

|      |   |           |      |    |       |      |       |   |      |     |     |     |    |        |         |     |     |              |
|------|---|-----------|------|----|-------|------|-------|---|------|-----|-----|-----|----|--------|---------|-----|-----|--------------|
| V-7  | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-14HCV |
| V-8  | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-15HCV |
| V-9  | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-16HCV |
| V-10 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-17HCV |
| V-11 | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70 | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-29-18HCV |
| V-12 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-21HCV |
| V-13 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-23HCV |
| V-14 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-25HCV |
| V-15 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-27HCV |
| V-16 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-29-29HCV |
| V-17 | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70 | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-29-30HCV |
| V-18 | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70 | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-29-31HCV |

NOTES: All control valves and wells shall be installed by the heating contractor.

**SIEMENS INDUSTRY, INC.**  
**SMART INFRASTRUCTURE**

**Valve Submittal - Water**

|                  |              |                      |                     |              |          |
|------------------|--------------|----------------------|---------------------|--------------|----------|
| <b>LOCATION:</b> | NEW YORK, NY | <b>PROJECT NAME:</b> | 7TS 29-31 SNOWFLAKE | <b>DATE:</b> | 07/22/26 |
| <b>JOB NO:</b>   | 44OP-420147  |                      |                     | <b>PAGE:</b> | 3        |
| <b>ENGR:</b>     | PP           |                      |                     | <b>REV:</b>  |          |

**GENERAL NOTES:**

1. All valves 2-1/2" and larger have flanged ends, 2" and smaller have screwed ends.
2. All control valves and wells shall be installed by the mechanical contractor.
3. Standard abbreviations used on control valves are:

**BODY TYPES:** 3W - Three way; 2W - Two way; A - Angle; N.C. - Normally Closed; N.O. - Normally Open;  
NOC - Ball Valve can be N.O. or N.C.; BF - Butterfly Valve; DS - Double Seated;

**UNITS:**

Steam inlet pressure, actual pressure drop, and shut off pressure indicated in PSIG.

**ACTUATOR TYPES:** SR - Spring Return; NSR - No Spring Return  
CR - Capacitor Driven Return; DA - Double Acting

| Valve ID/<br>Location | Qty | Product Number | Valve Size | Body Type | Body Style | Actual Cv | Actuator Type | Design P. Drop (psi) | Required Flow (gpm) | Min (gpm) | Max (gpm) | Preset (gpm) | Steam Inlet | Press Drop (psi) | Valve Spec Sheet | Shut Off | ANSI Class | Comment |
|-----------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|
|-----------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|

| Mechanical System: FPB |   |           |      |    |       |      |       |   | FAN POWERED BOX W/HWR |     |     |     |    |        |         |     |     |              |
|------------------------|---|-----------|------|----|-------|------|-------|---|-----------------------|-----|-----|-----|----|--------|---------|-----|-----|--------------|
| V-19                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-1 HCV |
| V-20                   | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                  | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-30-4 HCV |
| V-21                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-7 HCV |
| V-22                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-8 HCV |
| V-23                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-10HCV |
| V-24                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-11HCV |
| V-25                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-12HCV |
| V-26                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-17HCV |
| V-27                   | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                  | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-30-18HCV |
| V-28                   | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                  | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-30-20HCV |
| V-29                   | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                  | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-30-21HCV |
| V-30                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-23HCV |

NOTES: All control valves and wells shall be installed by the heating contractor.

**SIEMENS INDUSTRY, INC.**  
**SMART INFRASTRUCTURE**

**Valve Submittal - Water**

|                  |              |                      |                     |              |          |
|------------------|--------------|----------------------|---------------------|--------------|----------|
| <b>LOCATION:</b> | NEW YORK, NY | <b>PROJECT NAME:</b> | 7TS 29-31 SNOWFLAKE | <b>DATE:</b> | 07/22/26 |
| <b>JOB NO:</b>   | 44OP-420147  |                      |                     | <b>PAGE:</b> | 4        |
| <b>ENGR:</b>     | PP           |                      |                     | <b>REV:</b>  |          |

**GENERAL NOTES:**

1. All valves 2-1/2" and larger have flanged ends, 2" and smaller have screwed ends.
2. All control valves and wells shall be installed by the mechanical contractor.
3. Standard abbreviations used on control valves are:

**BODY TYPES:** 3W - Three way; 2W - Two way; A - Angle; N.C. - Normally Closed; N.O. - Normally Open;  
 NOC - Ball Valve can be N.O. or N.C.; BF - Butterfly Valve; DS - Double Seated;

**UNITS:**

Steam inlet pressure, actual pressure drop, and shut off pressure indicated in PSIG.

**ACTUATOR TYPES:** SR - Spring Return; NSR - No Spring Return  
 CR - Capacitor Driven Return; DA - Double Acting

| Valve ID/<br>Location | Qty | Product Number | Valve Size | Body Type | Body Style | Actual Cv | Actuator Type | Design P. Drop (psi) | Required Flow (gpm) | Min (gpm) | Max (gpm) | Preset (gpm) | Steam Inlet | Press Drop (psi) | Valve Spec Sheet | Shut Off | ANSI Class | Comment |
|-----------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|
|-----------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|

| Mechanical System: FPB |   |           |      |    |       |      |       |   | FAN POWERED BOX W/HWR |     |     |     |    |        |         |     |     |              |
|------------------------|---|-----------|------|----|-------|------|-------|---|-----------------------|-----|-----|-----|----|--------|---------|-----|-----|--------------|
| V-31                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-25HCV |
| V-32                   | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                  | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-30-26HCV |
| V-33                   | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                  | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-30-28HCV |
| V-34                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-29HCV |
| V-35                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-30HCV |
| V-36                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-30-31HCV |
| V-37                   | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                  | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-1 HCV |
| V-38                   | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                  | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-2 HCV |
| V-39                   | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20                  | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-4 HCV |
| V-40                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-31-6 HCV |
| V-41                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-31-7 HCV |
| V-42                   | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70                  | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-31-8 HCV |

NOTES: All control valves and wells shall be installed by the heating contractor.

**SIEMENS INDUSTRY, INC.**  
**SMART INFRASTRUCTURE**

**Valve Submittal - Water**

|                  |              |                      |                     |              |          |
|------------------|--------------|----------------------|---------------------|--------------|----------|
| <b>LOCATION:</b> | NEW YORK, NY | <b>PROJECT NAME:</b> | 7TS 29-31 SNOWFLAKE | <b>DATE:</b> | 07/22/26 |
| <b>JOB NO:</b>   | 44OP-420147  |                      |                     | <b>PAGE:</b> | 5        |
| <b>ENGR:</b>     | PP           |                      |                     | <b>REV:</b>  |          |

**GENERAL NOTES:**

1. All valves 2-1/2" and larger have flanged ends, 2" and smaller have screwed ends.
2. All control valves and wells shall be installed by the mechanical contractor.
3. Standard abbreviations used on control valves are:

**BODY TYPES:** 3W - Three way; 2W - Two way; A - Angle; N.C. - Normally Closed; N.O. - Normally Open;  
 NOC - Ball Valve can be N.O. or N.C.; BF - Butterfly Valve; DS - Double Seated;

**UNITS:**

Steam inlet pressure, actual pressure drop, and shut off pressure indicated in PSIG.

**ACTUATOR TYPES:** SR - Spring Return; NSR - No Spring Return  
 CR - Capacitor Driven Return; DA - Double Acting

| Valve ID/<br>Location | Qty | Product Number | Valve Size | Body Type | Body Style | Actual Cv | Actuator Type | Design P. Drop (psi) | Required Flow (gpm) | Min (gpm) | Max (gpm) | Preset (gpm) | Steam Inlet | Press Drop (psi) | Valve Spec Sheet | Shut Off | ANSI Class | Comment |
|-----------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|
|-----------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|

**Mechanical System: FPB**

**FAN POWERED BOX W/HWR**

|      |   |           |      |    |       |      |       |   |      |     |     |     |    |        |         |     |     |              |
|------|---|-----------|------|----|-------|------|-------|---|------|-----|-----|-----|----|--------|---------|-----|-----|--------------|
| V-43 | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70 | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-31-10HCV |
| V-44 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-11HCV |
| V-45 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-12HCV |
| V-46 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-13HCV |
| V-47 | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70 | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-31-14HCV |
| V-48 | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70 | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-31-15HCV |
| V-49 | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70 | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-31-16HCV |
| V-50 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-17HCV |
| V-51 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-18HCV |
| V-52 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-21HCV |
| V-53 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-22HCV |
| V-54 | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70 | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-31-26HCV |

NOTES: All control valves and wells shall be installed by the heating contractor.

**SIEMENS INDUSTRY, INC.**  
**SMART INFRASTRUCTURE**

**Valve Submittal - Water**

|                  |              |                      |                     |              |          |
|------------------|--------------|----------------------|---------------------|--------------|----------|
| <b>LOCATION:</b> | NEW YORK, NY | <b>PROJECT NAME:</b> | 7TS 29-31 SNOWFLAKE | <b>DATE:</b> | 07/22/26 |
| <b>JOB NO:</b>   | 44OP-420147  |                      |                     | <b>PAGE:</b> | 6        |
| <b>ENGR:</b>     | PP           |                      |                     | <b>REV:</b>  |          |

**GENERAL NOTES:**

1. All valves 2-1/2" and larger have flanged ends, 2" and smaller have screwed ends.
2. All control valves and wells shall be installed by the mechanical contractor.
3. Standard abbreviations used on control valves are:

**BODY TYPES:** 3W - Three way; 2W - Two way; A - Angle; N.C. - Normally Closed; N.O. - Normally Open;  
 NOC - Ball Valve can be N.O. or N.C.; BF - Butterfly Valve; DS - Double Seated;

**UNITS:**

Steam inlet pressure, actual pressure drop, and shut off pressure indicated in PSIG.

**ACTUATOR TYPES:** SR - Spring Return; NSR - No Spring Return  
 CR - Capacitor Driven Return; DA - Double Acting

| Valve ID/ Location | Qty | Product Number | Valve Size | Body Type | Body Style | Actual Cv | Actuator Type | Design P. Drop (psi) | Required Flow (gpm) | Min (gpm) | Max (gpm) | Preset (gpm) | Steam Inlet | Press Drop (psi) | Valve Spec Sheet | Shut Off | ANSI Class | Comment |
|--------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|
|--------------------|-----|----------------|------------|-----------|------------|-----------|---------------|----------------------|---------------------|-----------|-----------|--------------|-------------|------------------|------------------|----------|------------|---------|


**Mechanical System: FPB**

**FAN POWERED BOX W/HWR**

|      |   |           |      |    |       |      |       |   |      |     |     |     |    |        |         |     |     |              |
|------|---|-----------|------|----|-------|------|-------|---|------|-----|-----|-----|----|--------|---------|-----|-----|--------------|
| V-55 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-29HCV |
| V-56 | 1 | 262-02034 | 0.50 | 2W | Globe | 1.00 | NO-SR | 3 | 1.20 | N/A | N/A | N/A | -- | 1.44   | 154 010 | 120 | 250 | FPB-31-30HCV |
| V-57 | 1 | 262-02030 | 0.50 | 2W | Globe | 0.40 | NO-SR | 3 | 0.70 | N/A | N/A | N/A | -- | 3.0625 | 154 010 | 120 | 250 | FPB-31-31HCV |

NOTES: All control valves and wells shall be installed by the heating contractor.

CRAC UNIT  
REFERENCE : M-529, M-530 & M-531  
LOCATION: SEE SCHEDULE  
SERVES: SEE SCHEDULE

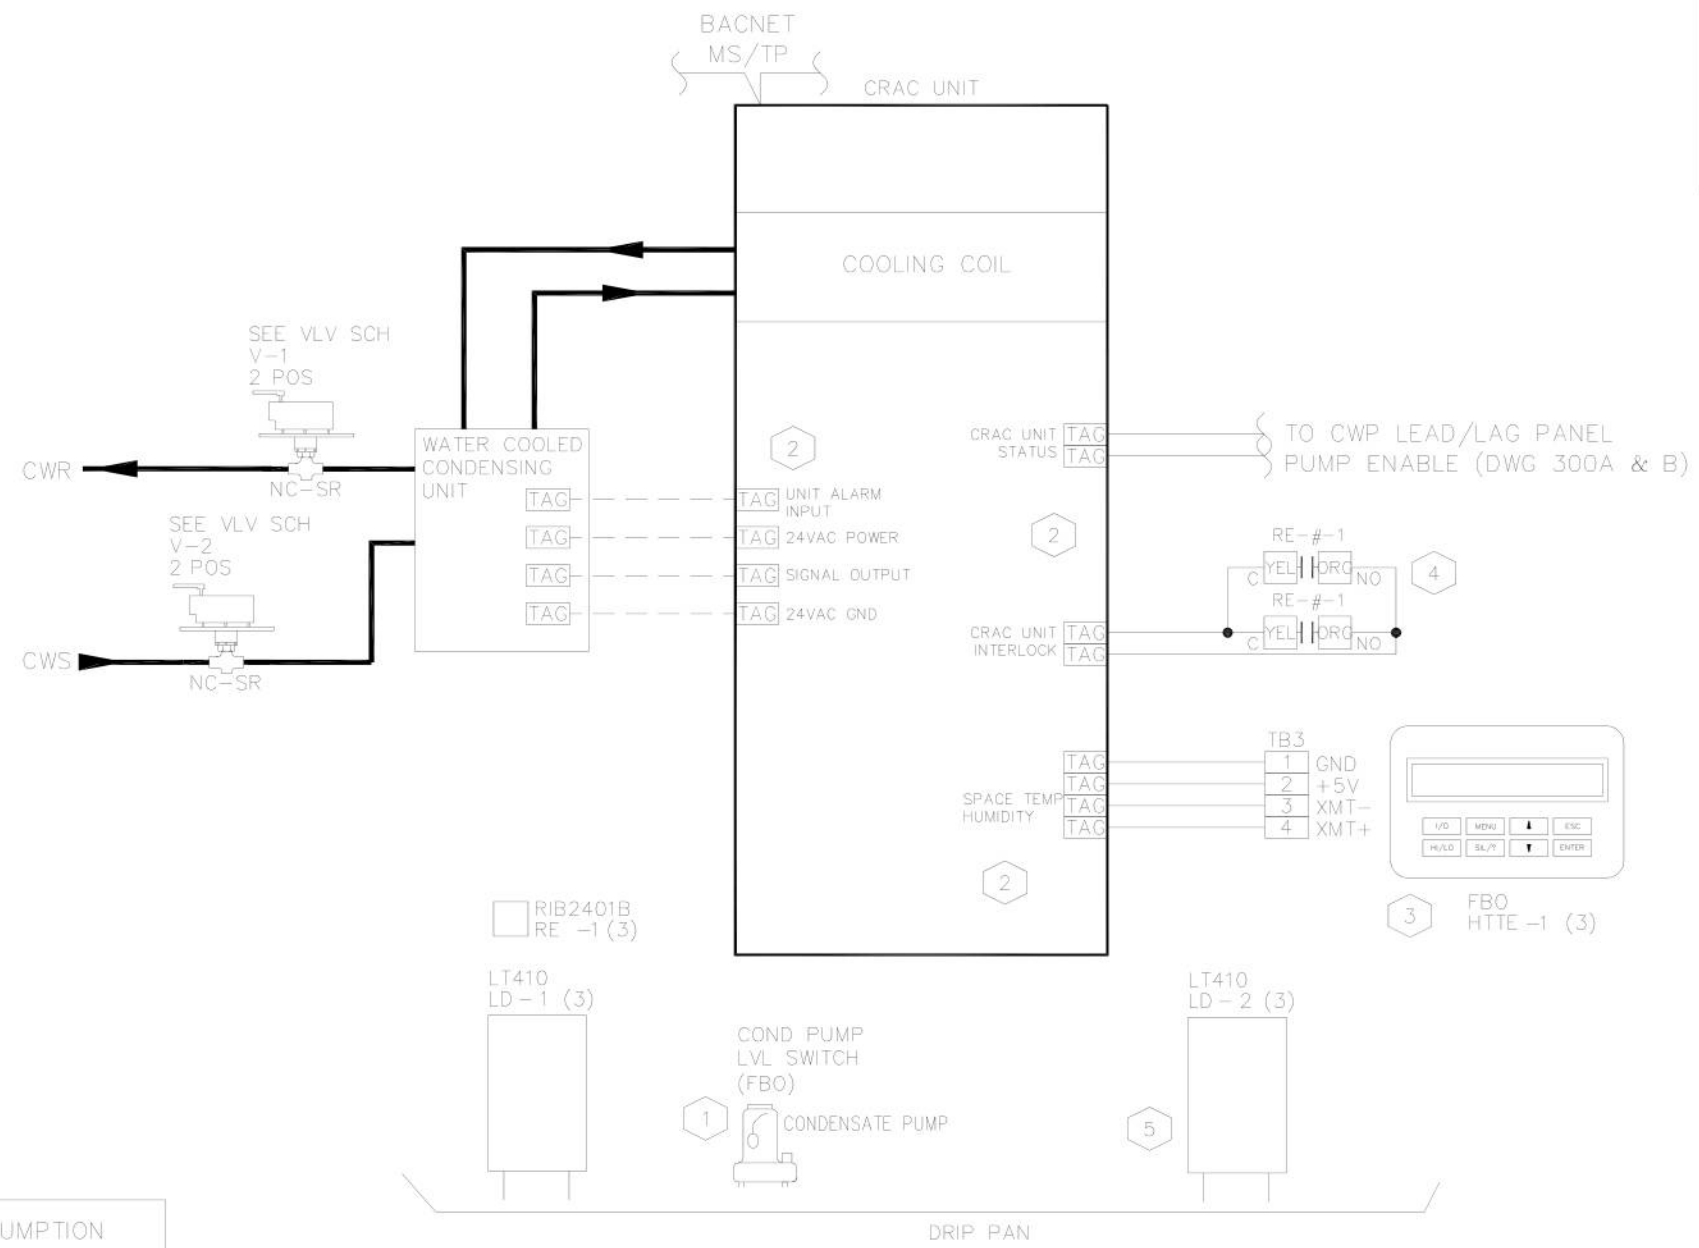

PANEL MOUNTED DEVICES

TR100VA004  
XFMR -1 (3)

- INSTALLATION NOTES:
- 1 CONDENSATE PUMP FACTORY PROVIDED AND FACTORY INSTALLED.
  - 2 TERMINATIONS TO BE FIELD COORDINATED.
  - 3 SPACE TEMPERATURE/HUMIDITY SENSOR PROVIDED BY UNIT MANUFACTURER.
  - 4 REFER SCHEDULE FOR THE RELAY CONTACTS.
  - 5 LD-2 LEAK DETECTOR WILL BE CONNECTED TO AUTO DIALER. REFER 503A FOR WIRING DETAILS.

| CRAC UNIT SCHEDULE |                  |  |
|--------------------|------------------|--|
| TAG                | LOCATION &SERVES |  |
| CRAC-29-1          | IDF 29.35        |  |
| WCCU-29-1          |                  |  |
| CRAC-30-1          | IDF 30.29        |  |
| WCCU-30-1          |                  |  |
| CRAC-31-1          | IDF 31.44        |  |
| WCCU-30-1          |                  |  |

| AC UNIT   | RELAY CONTACT |
|-----------|---------------|
| WCCU-29-1 | RE-3-1        |
| WCCU-29-1 | RE-8-1        |
| WCCU-29-1 | RE-13-1       |

| AC UNIT   | RELAY CONTACT |
|-----------|---------------|
| WCCU-29-1 | RE-5-1        |
| WCCU-29-1 | RE-10-1       |
| WCCU-29-1 | RE-15-1       |

| VA CONSUMPTION |        |    |
|----------------|--------|----|
| S NO           | DEVICE | VA |
| 1              | V-1,2  | 10 |
| 2              | LD-1   | 3  |
| TOTAL          |        | 13 |

### REVISION HISTORY

|    |           |    |                        |
|----|-----------|----|------------------------|
| R0 | 7/22/2026 | PP | SUBMITTAL FOR APPROVAL |
|----|-----------|----|------------------------|

**SIEMENS**

SIEMENS INDUSTRY, INC.  
SMART INFRASTRUCTURE

412 MT KEMBLE AVE  
SUITE 200S  
MORRISTOWN  
NJ-07960 USA  
PHONE: (973)575-6300  
FAX: (973)575-7968

7TS 29-31 SNOWFLAKE  
NEW YORK, NY

|          |         |            |                 |                |
|----------|---------|------------|-----------------|----------------|
| ENGINEER | DRAFTER | CHECKED BY | INITIAL RELEASE | LAST EDIT DATE |
| PP       | PP      | SN         | 07/22/26        | 07/22/26       |

WATER COOLED AC (MECH)

440P-420147  
0

100

© COPYRIGHT 1994-26 SIEMENS INDUSTRY, INC. All Rights Reserved

C:\JOBS\440P-420147\MDT\AC.DWG



| Control Device        | Qty | Product Number | Manufacturer       | Document Number | Description                              |
|-----------------------|-----|----------------|--------------------|-----------------|------------------------------------------|
| Field Mounted Devices |     |                |                    |                 |                                          |
| LD 1-2                | 6   | LT410          | LIEBERT            | N/A             | POINT LEAK DETECTOR SENSOR               |
| RE 1                  | 3   | RIB2401B       | FUNCTIONAL DEVICES | 1208cut021      | 20A SPDT 24VAC/DC/120VAC                 |
| V                     |     |                |                    |                 | SEE VALVE SUBMITTAL                      |
| Panel Mounted Devices |     |                |                    |                 |                                          |
| XFMR 1                | 3   | TR100VA004     | FUNCTIONAL         | TR100VA004      | Xfrmr 100VA,120/240/277/480-24V,dual hub |

CONTINUOUSLY. REFER TO THE CONDENSER WATER PUMP SEQUENCE OF OPERATION FOR ADDITIONAL REQUIREMENTS. ALL AC UNITS WILL BE PROVIDED WITH A CONDENSATE PUMP WITH OVERFLOW ALARM CONTACTS WIRED TO ALARM THE LANDLORD BMS AND TENANT ALARM SYSTEM.

WATER COOLED AIR CONDITIONING UNITS – SEQUENCE OF OPERATIONS:

- a) AIR CONDITIONING UNITS SERVING IDF OR FIBER CLOSETS WILL OPERATE 24 HOURS A DAY, SEVEN DAYS PER WEEK IN TIMED SCHEDULE.
- b) AIR CONDITIONING UNITS SERVING GENERAL OFFICE SPACE WILL BE STARTED/STOPPED NORMALLY BY AN ADJUSTABLE PRESET TIMED SCHEDULE AS DETERMINED BY OWNER (E.G. 8:00 AM TO 6:00 PM).
- c) UNITS WILL BE AUTOMATICALLY STARTED AND STOPPED VIA AN INDIVIDUAL DIGITALLY PROGRAMMABLE COOLING THERMOSTAT WITH SEVEN-DAY TIME CLOCK CONTROL AND LOCKING COVER LOCATED WITHIN THE SERVED SPACE.THE TIME SCHEDULE TO BE DETERMINED BY OWNER. THERMOSTATS TO INCLUDE TIMED OVERRIDE CAPABILITY TO OVERRIDE THE CLOCK SETTING IN THREE (3) HOUR INCREMENTS (ADJUSTABLE). THERMOSTATS TO INCLUDE MULTIPLE STAGES AS REQUIRED BY EQUIPMENT CONTROLLED. THERMOSTAT WILL BE SIMILAR TO HONEYWELL TB8220 PREMIUM THERMOSTAT.
- d) THERMOSTAT WILL HAVE LOCAL SETPOINT AND ACTUAL SPACE TEMPERATURE READOUTS AND WILL HAVE A SETPOINT OF 75°F ADJ. THE AC UNIT CONTROLS WILL CYCLE AND MODULATE THE REFRIGERATION COMPONENTS TO MAINTAIN THE SPACE TEMPERATURE SETPOINT.
- e) THE THERMOSTAT WILL ALLOW THE UNITS FAN TO RUN CONTINUOUSLY WHILE IN OPERATION.
- f) UNIT WILL MODULATE WATER REGULATING VALVE AS REQUIRED TO MAINTAIN REFRIGERANT PRESSURES.
- g) PROVIDE NORMALLY CLOSED MOTORIZED ISOLATION VALVES ON THE CONDENSER WATER SUPPLY AND RETURN PIPING LINES.
- h) MOTORIZED ISOLATION VALVES WILL OPEN UPON AC UNIT ACTIVATION AND CLOSE WHEN THE UNIT IS NOT OPERATING. VALVES WILL OPEN DAILY FOR 4 HOURS (ADJUSTABLE) TO FLOW WATER THROUGH THE CONDENSER COIL REGARDLESS OF UNIT OPERATION.
- i) THE RESPECTIVE CONDENSATE PUMP FOR EACH AIR CONDITIONING UNIT WILL BE ENERGIZED AT ALL TIMES REGARDLESS OF THE AIR CONDITIONING UNIT’S OPERATION. WHEN THE CONDENSATE PUMPS SAFETY FLOAT SWITCH IS ENGAGED, AN ALARM SIGNAL WILL SOUND AT THE LANDLORD BMS. IF THE ALARM IS NOT RESET WITHIN 5 MINUTES (ADJUSTABLE), THE AIR CONDITIONING UNIT WILL BE DE-ENERGIZED AND THE ISOLATION VALVES CLOSED.
- j) LEAK DETECTION WILL BE PROVIDED IN THE AUXILIARY DRAIN PAN FOR EACH UNIT. WHEN THE LOCAL LEAK DETECTOR SENSES MOISTURE IN THE AUXILIARY DRAIN PAN, AN ALARM SIGNAL WILL SOUND AT THE LANDLORD BMS. IF THE ALARM IS NOT RESET WITHIN 5 MINUTES (ADJUSTABLE), THE AIR CONDITIONING UNIT WILL BE DE-ENERGIZED AND THE ISOLATION VALVES CLOSED.
- k) PROVIDE A FLOW SWITCH FOR EACH AIR CONDITIONING UNIT. THE FLOW SWITCH WILL SENSE THE MINIMUM CONDENSER WATER FLOW NECESSARY FOR OPERATING THE UNIT. UPON REACHING THE MINIMUM FLOW SETPOINT, THE FLOW SWITCH SENSOR WILL ENGAGE A CONTACT AND ALLOW THE UNIT TO OPERATE. IF THE FLOW RATE IS BELOW THE MINIMUM SETPOINT, THE CONTACT WILL OPEN AND PREVENT THE UNIT FROM RUNNING.
- l) UPON A CALL TO ACTIVATE ANY AC UNIT, THE RESPECTIVE CONDENSER WATER PUMP WILL START AND RUN

REVISION HISTORY

|    |           |    |                        |
|----|-----------|----|------------------------|
| RO | 7/22/2026 | PP | SUBMITTAL FOR APPROVAL |
|    |           |    |                        |

SIEMENS

SIEMENS INDUSTRY, INC.  
SMART INFRASTRUCTURE

412 MT KEMBLE AVE  
SUITE 200S  
MORRISTOWN  
NJ-07960 USA  
PHONE: (973)575-6300  
FAX: (973)575-7968

7TS 29-31 SNOWFLAKE  
NEW YORK, NY

|          |         |            |                 |                |
|----------|---------|------------|-----------------|----------------|
| ENGINEER | DRAFTER | CHECKED BY | INITIAL RELEASE | LAST EDIT DATE |
| PP       | PP      | SN         | 07/22/26        | 07/22/26       |

WATER COOLED AC (BOM&SEQ)

440P-420147  
0

100B

CONDENSER WATER PUMPS  
LOCATION & SERVES: SEE SCHEDULE

LEAD LAG PUMP CONTROLLER


- ☐ RIBU1C  
RE -1 (3)
- ☐ RIBU1C  
RE -2 (3)
- ☐ RIBU1C  
RE -5 (3)
- ☐ RIBU1C  
RE -3 (3)
- ☐ RIBU1C  
RE -4 (3)

DRAWING NOTES:

- 1 LEAK DETECTOR PROVIDED BY SIEMENS.
- 2 VFD MOUNTED IN CEILING NEAR PUMP SET.
- 3 REFER BELOW SCHEDULE FOR NEAREST DXR'S.

| CWP SCHEDULE |                   |           |
|--------------|-------------------|-----------|
| UNIT TAG     | LOCATION          | SERVES    |
| CWP-29-1,2   | OPEN OFFICE 29.17 | CRAC-29-1 |
| CWP-30-1,2   | DISH ROOM 30.13   | CRAC-30-1 |
| CWP-31-1,2   | STORAGE 31.15     | CRAC-31-1 |

| TAG      | FLOOR | NEAREST DXR | DEVICE     |
|----------|-------|-------------|------------|
| CWP-29-1 | 29    | FPB-29-15   | LD-1       |
| CWP-29-1 | 29    | FPB-29-16   | FS-1 ALARM |
| CWP-29-2 | 29    | FPB-29-17   | LD-2       |
| CWP-29-2 | 29    | FPB-29-18   | FS-2 ALARM |
| CWP-30-1 | 30    | FPB-30-16   | LD-1       |
| CWP-30-1 | 30    | FPB-30-19   | FS-1 ALARM |
| CWP-30-2 | 30    | FPB-30-20   | LD-2       |
| CWP-30-2 | 30    | FPB-30-21   | FS-2 ALARM |
| CWP-31-1 | 31    | FPB-31-10   | LD-1       |
| CWP-31-1 | 31    | FPB-31-11   | FS-1 ALARM |
| CWP-31-2 | 31    | FPB-31-12   | LD-2       |
| CWP-31-2 | 31    | FPB-31-14   | FS-2 ALARM |

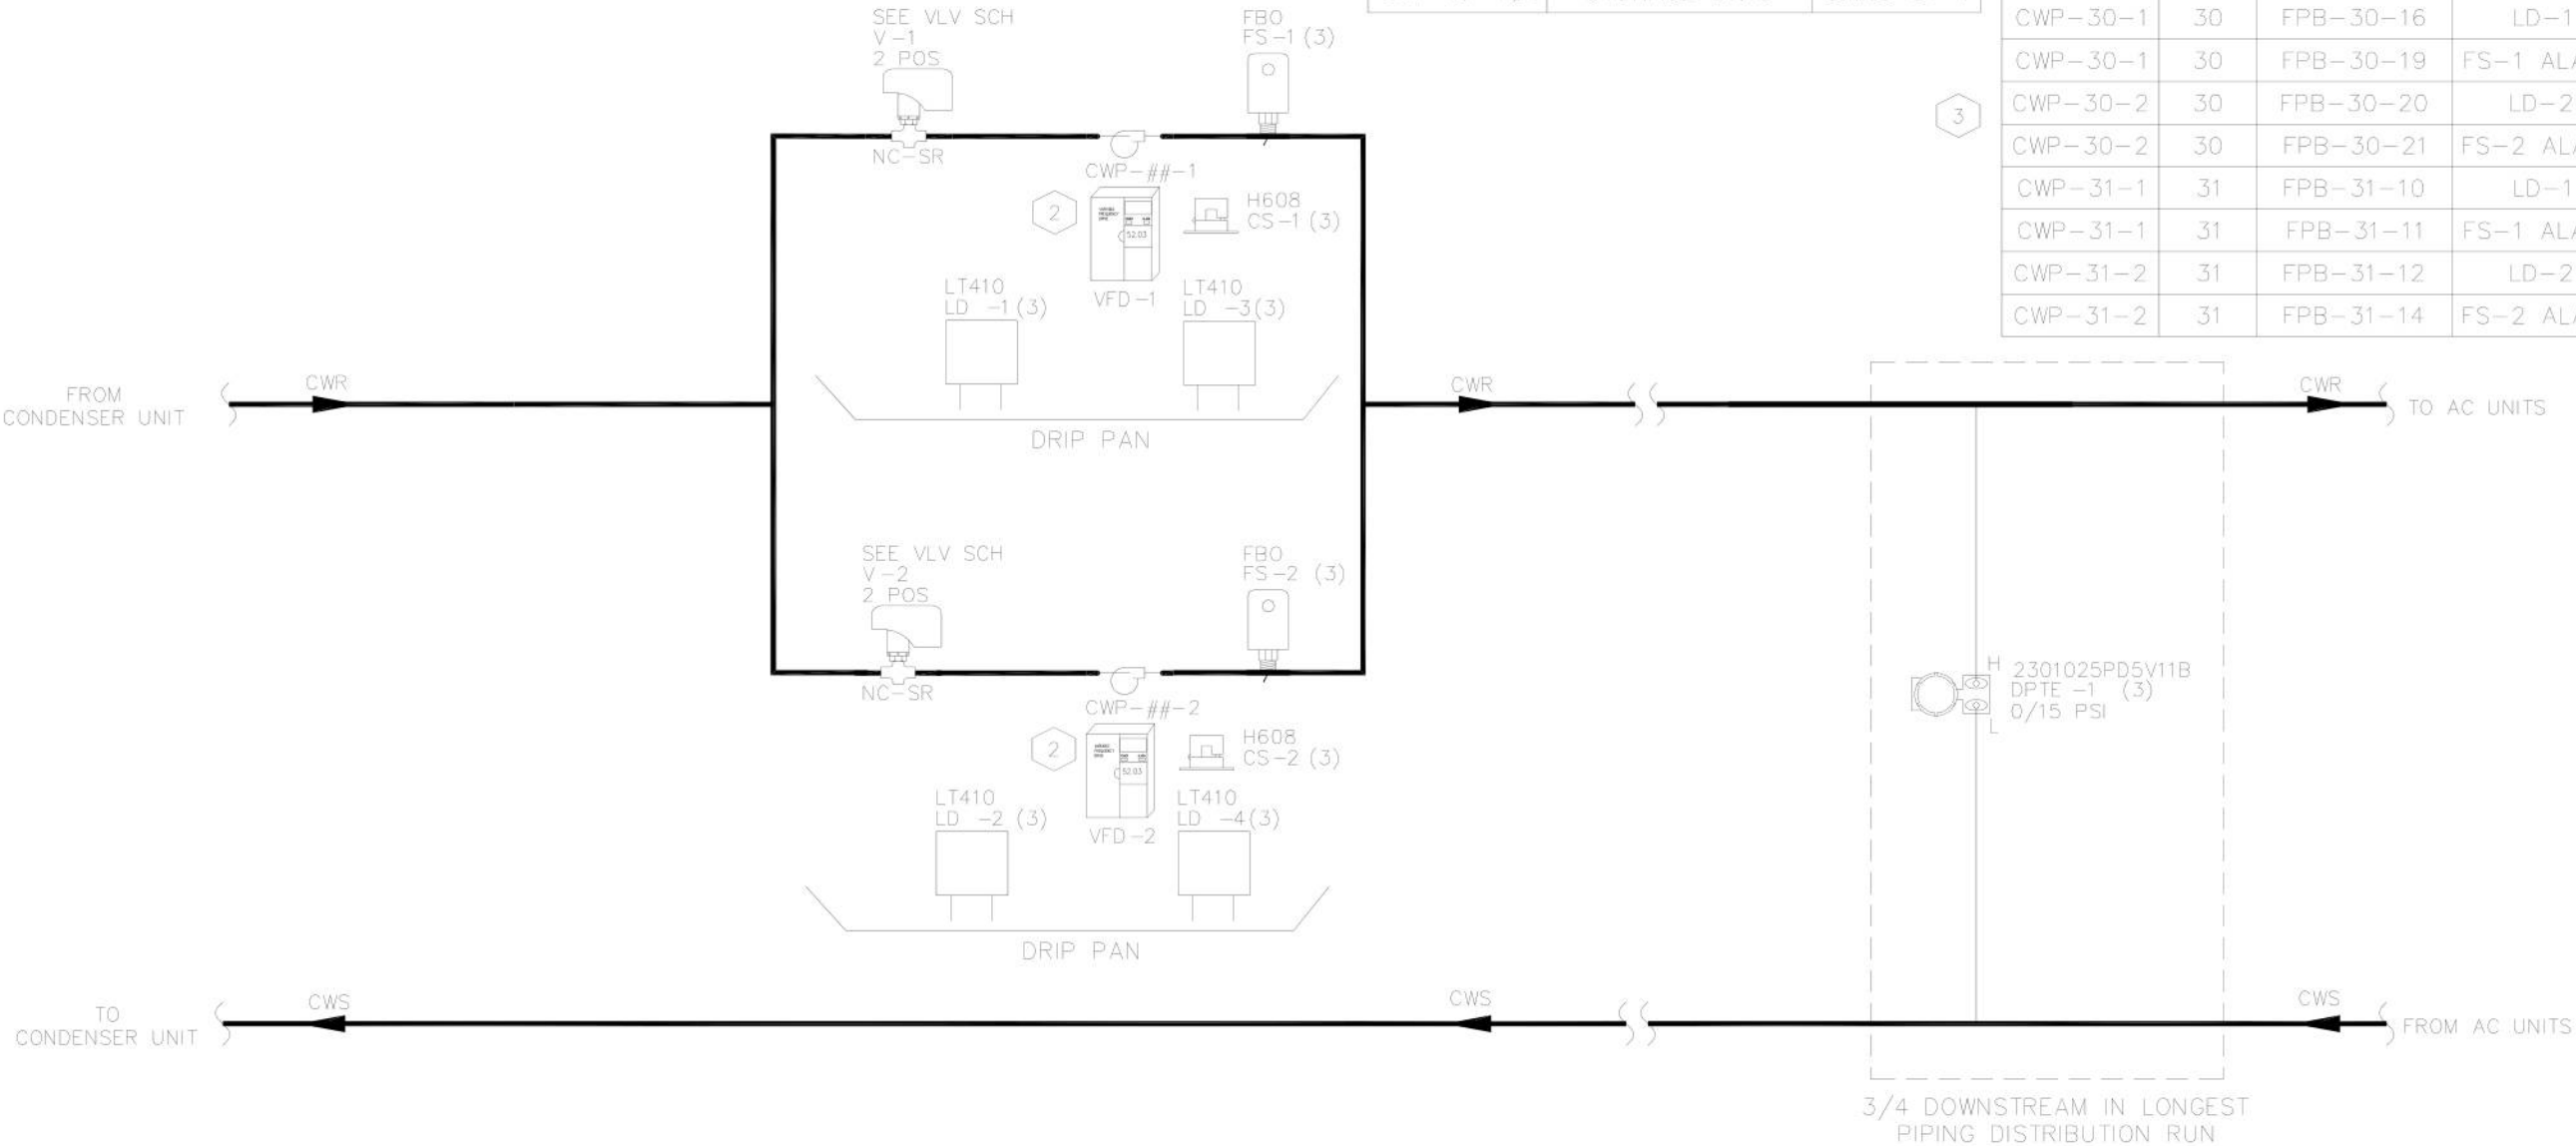

REVISION HISTORY

|    |           |    |                        |
|----|-----------|----|------------------------|
| RO | 7/22/2026 | PP | SUBMITTAL FOR APPROVAL |
|----|-----------|----|------------------------|

SIEMENS

SIEMENS INDUSTRY, INC.  
SMART INFRASTRUCTURE

412 MT KEMBLE AVE  
SUITE 200S  
MORRISTOWN  
NJ-07960 USA  
PHONE: (973)575-6300  
FAX: (973)575-7968

7TS 29-31 SNOWFLAKE  
NEW YORK, NY

|          |         |            |                 |                |
|----------|---------|------------|-----------------|----------------|
| ENGINEER | DRAFTER | CHECKED BY | INITIAL RELEASE | LAST EDIT DATE |
| PP       | PP      | SN         | 07/22/26        | 07/22/26       |

CONDENSER WATER PUMPS(MECH)

440P-420147  
0

300

| REVISION HISTORY       |           |    |
|------------------------|-----------|----|
| R0                     | 7/22/2026 | PP |
| SUBMITTAL FOR APPROVAL |           |    |

SIEMENS

SIEMENS INDUSTRY, INC.  
SMART INFRASTRUCTURE

412 MT KEMBLE AVE  
SUITE 200S  
MORRISTOWN  
NJ-07960 USA  
PHONE: (973)575-6300  
FAX: (973)575-7968

7TS 29-31 SNOWFLAKE  
NEW YORK, NY

440P-420147  
0

300A

ENGINEER

DRAFTER

CHECKED BY

INITIAL RELEASE

LAST EDIT DATE

PP


PP

SN

07/22/26

07/22/26

CONDENSER WATER PUMPS(ELEC-1)

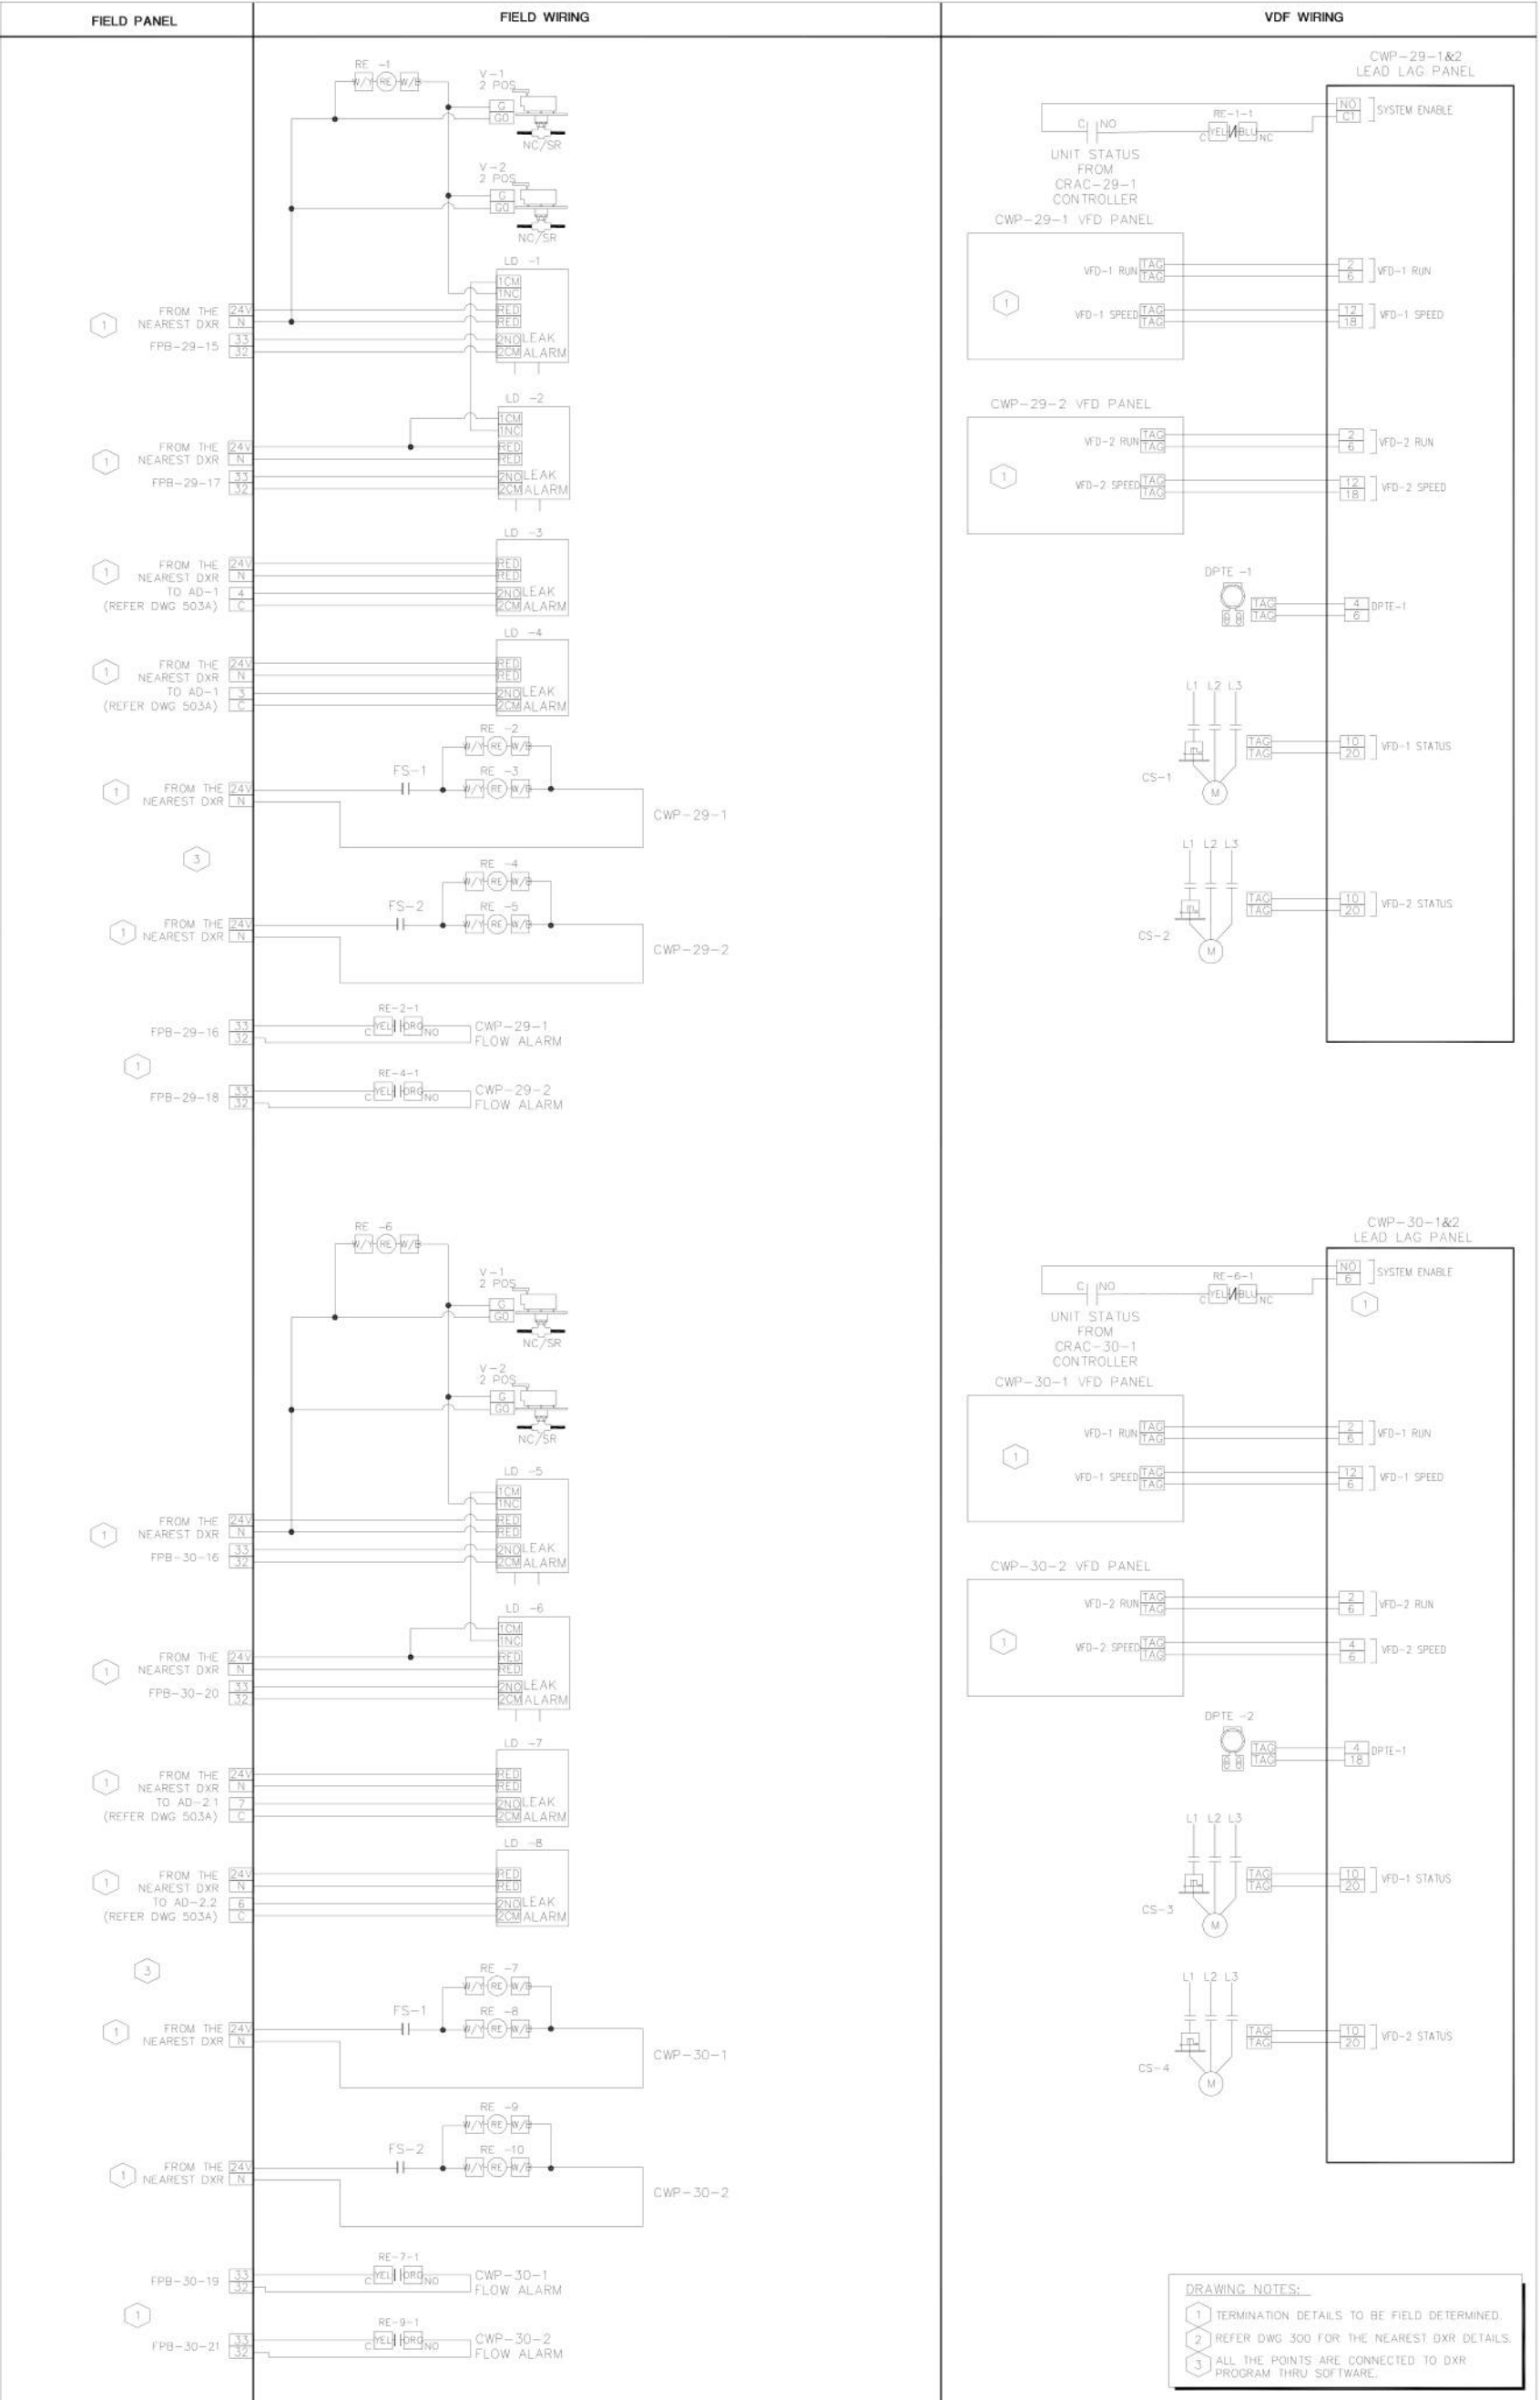

**SIEMENS**  
412 MT KEMBLE AVE  
SUITE 200S  
MORRISTOWN  
NJ-07960 USA  
PHONE: (973)575-6300  
FAX: (973)575-7968  
SIEMENS INDUSTRY, INC.  
SMART INFRASTRUCTURE

| FIELD PANEL | FIELD WIRING                                                                                                                                                                                                                                                                                            | VDF WIRING                                                                                                                                                                             |
|-------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|             |                                                                                                                                                                                                                                                                                                         |                                                                                                                                                                                        |
|             | <p>FROM THE NEAREST DXR<br/>FPB-31-10</p> <p>FROM THE NEAREST DXR<br/>FPB-31-12</p> <p>FROM THE NEAREST DXR<br/>TO AD-3<br/>(REFER DWG 503A)</p> <p>FROM THE NEAREST DXR<br/>TO AD-3<br/>(REFER DWG 503A)</p> <p>FROM THE NEAREST DXR</p> <p>FROM THE NEAREST DXR</p> <p>FPB-31-11</p> <p>FPB-31-14</p> | <p>UNIT STATUS<br/>FROM<br/>CRAC-31-1<br/>CONTROLLER</p> <p>VFD-1 RUN</p> <p>VFD-1 SPEED</p> <p>VFD-2 RUN</p> <p>VFD-2 SPEED</p> <p>DPTE-1</p> <p>VFD-1 STATUS</p> <p>VFD-2 STATUS</p> |

**DRAWING NOTES:**

1. TERMINATION DETAILS TO BE FIELD DETERMINED.
2. REFER DWG 300 FOR THE NEAREST DXR DETAILS.
3. ALL THE POINTS ARE CONNECTED TO DXR PROGRAM THRU SOFTWARE.

| Control Device        | Qty | Product Number | Manufacturer       | Document Number | Description                            |
|-----------------------|-----|----------------|--------------------|-----------------|----------------------------------------|
| Field Mounted Devices |     |                |                    |                 |                                        |
| CS 1-2                | 6   | H608           | VERIS              | 1006cut016      | CUR SW SPLTCOR-ADJ SETPT W/LED         |
| DPTE 1                | 3   | 2301025PD5V11B | SETRA SYST         | N/A             | DP TRAN,WET,25PSI,4-20MA,W/ 5VALVE MAN |
| LD 1-4                | 12  | LT410          | LIEBERT            | N/A             | POINT LEAK DETECTOR SENSOR             |
| RE 1-5                | 15  | RIBU1C         | FUNCTIONAL DEVICES | 1208cut013      | RIB 120VAC 24VAC/DC SPDT               |
| V                     |     |                |                    |                 | SEE VALVE SUBMITTAL                    |

CONDENSER WATER PUMPS – SEQUENCE OF OPERATION:

- a) CIRCULATING PUMP OPERATION SHALL BE INTERLOCKED WITH THE AC UNITS. UPON ACTIVATION OF ANY UNIT, THE LEAD CIRCULATING PUMP SHALL START AND RUN CONTINUOUSLY. THE PUMPS SHALL BE PROVIDED WITH AN AUTOMATIC RESTART AFTER A POWER OUTAGE.
- b) PROVIDE FOR LEAD/LAG SEQUENCING IN ORDER TO HAVE ONE PUMP RUNNING AND THE OTHER AS STAND-BY. PUMPS SHALL BE CYCLED ON A 150 HOUR OPERATING SCHEDULE (ADJUSTABLE) FOR EVEN WEAR.
- c) A FLOW SENSOR (ON DISCHARGE OF EACH PUMP) SHALL PROVE FLOW BEFORE STARTING ANY AIR CONDITIONING UNITS. A LOSS OF FLOW AS INDICATED BY THE FLOW SENSOR ON THE RUNNING PUMP SHALL SWITCH OPERATION TO THE STAND-BY PUMP AND ANNUNCIATE AN AUDIO/VISUAL ALARM LOCALLY.
- d) PROVIDE A LEAK DETECTOR AT THE AUXILIARY DRAIN PAN OF EACH PUMP. LEAK DETECTION SHALL ANNUNCIATE AN AUDIO/VISUAL ALARM LOCALLY AND THROUGH THE LANDLORD BMS. IF MOISTURE IS DETECTED IN THE PAN OF THE OPERATING PUMP, THE PUMP SHALL STOP, AND THE STAND-BY PUMP SHALL START.
- e) SYSTEM DIFFERENTIAL PRESSURE WILL BE MAINTAINED BY VARIABLE SPEED DRIVES PROVIDED FOR EACH PUMP. THE PUMP SPEED SHALL MODULATE AS REQUIRED TO MAINTAIN A SYSTEM DIFFERENTIAL PRESSURE SETPOINT (ADJUSTABLE) AS SENSED BY A PIPE MOUNTED DIFFERENTIAL PRESSURE SENSOR. DIFFERENTIAL PRESSURE SENSOR TO BE MOUNTED 3/4 DOWNSTREAM IN THE LONGEST PIPING DISTRIBUTION RUN.
- f) PROVIDE CONDENSER WATER PUMP SYSTEM WITH A 24 HOUR, 7 DAY TIMER TO INSURE PUMP OPERATION NOT LESS THAN 1 HOUR EVERY 4 HOURS.

REVISION HISTORY

|    |           |    |                        |
|----|-----------|----|------------------------|
| R0 | 7/22/2026 | PP | SUBMITTAL FOR APPROVAL |
|    |           |    |                        |

SIEMENS

SIEMENS INDUSTRY, INC.  
SMART INFRASTRUCTURE

412 MT KEMBLE AVE  
SUITE 200S  
MORRISTOWN  
NJ-07960 USA  
PHONE: (973)575-6300  
FAX: (973)575-7968

7TS 29-31 SNOWFLAKE  
NEW YORK, NY

|          |         |            |                 |                |
|----------|---------|------------|-----------------|----------------|
| ENGINEER | DRAFTER | CHECKED BY | INITIAL RELEASE | LAST EDIT DATE |
| PP       | PP      | SN         | 07/22/26        | 07/22/26       |

CONDENSER WATER PUMPS(BOM&SEQ)

440P-420147  
0

300C
