


ERU-1 / ERU-2 / ERU-3 Greenheck RVE-85-52D - duct sensor field wiring, one unit (typical of 3)

Northern Wolves AC | IPA Church, 310A S. Oyster Bay Rd, Syosset NY | ref. Greenheck submittal wiring diagrams G31 (p.15) and Y07 (p.18)

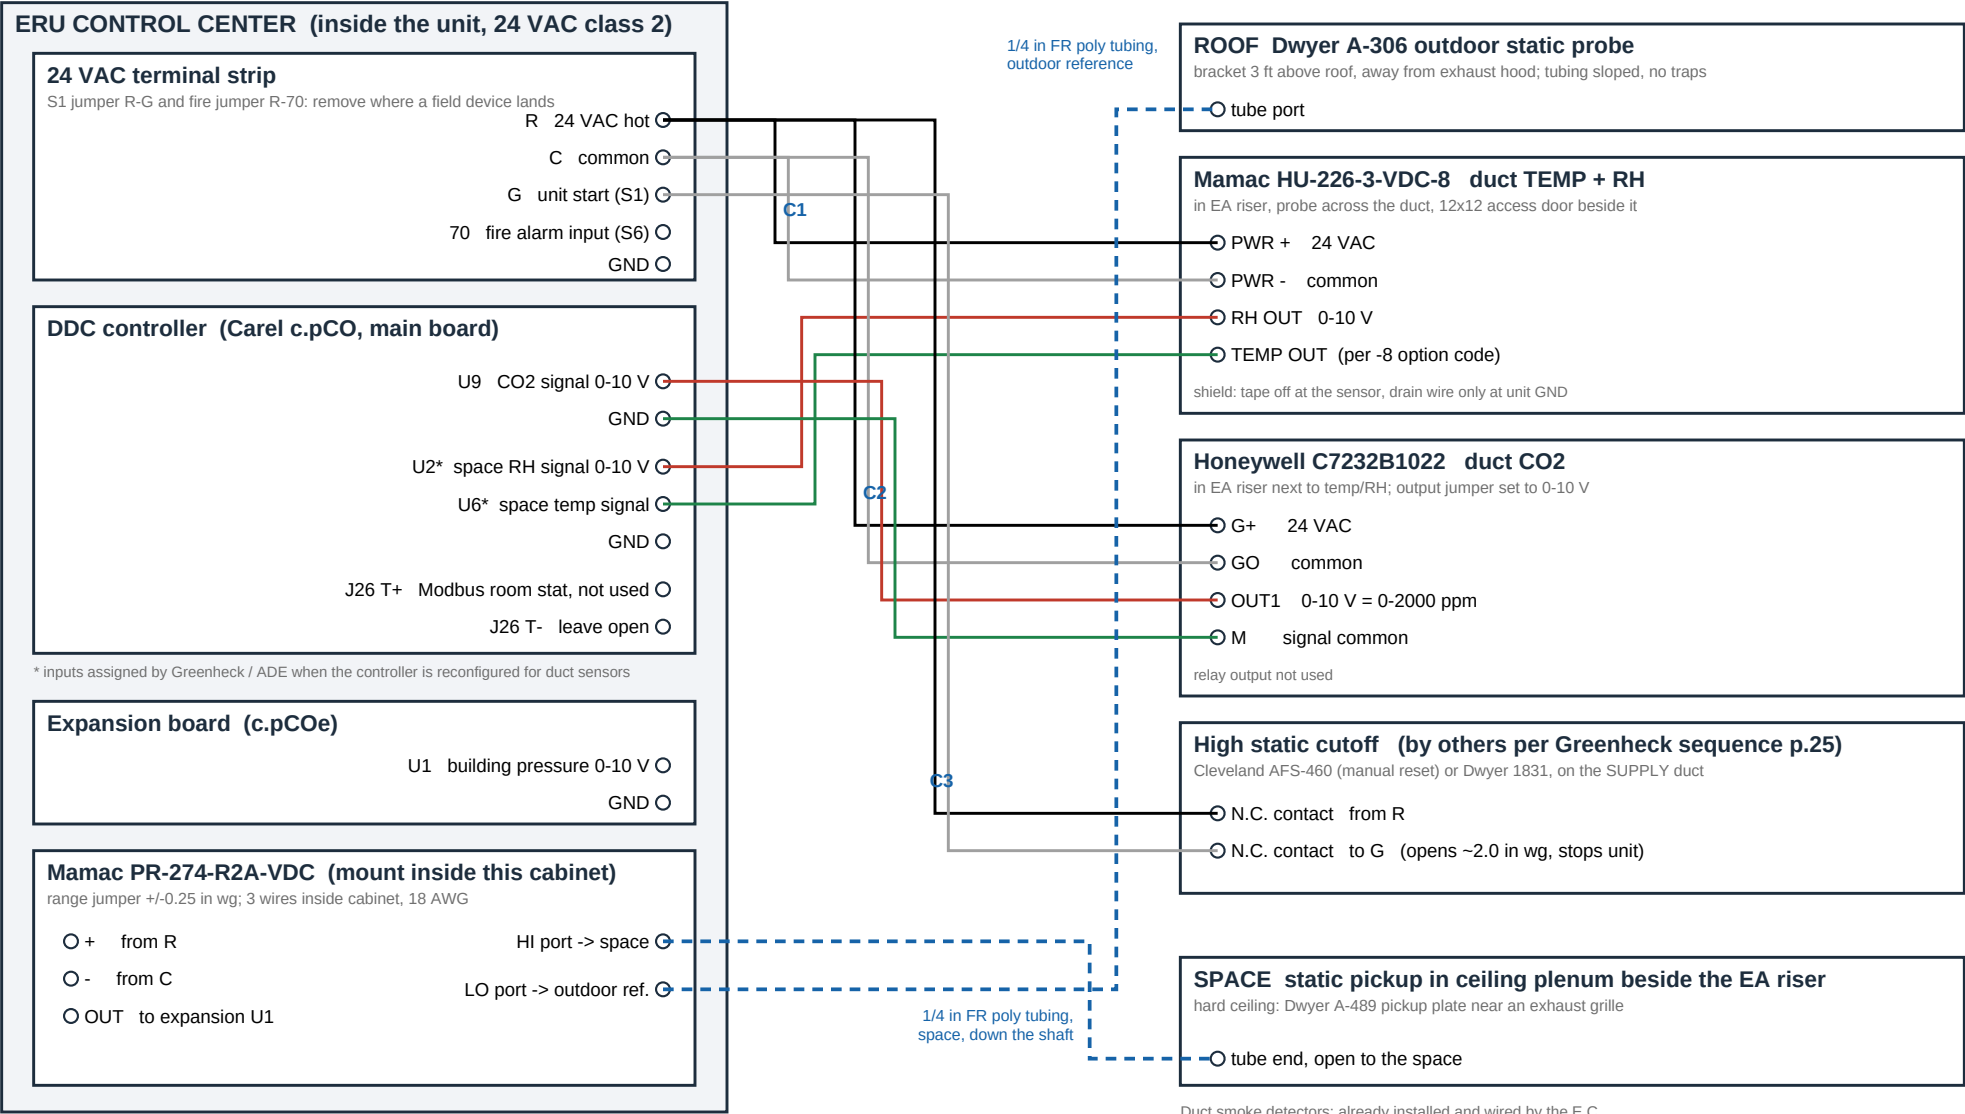

Same cable for C1-C3: 18/4 stranded, overall shield + drain, plenum rated (CMP). Unused conductors are spares, tape off.
Shield drain on controller GND at the unit only; cut and tape at the device. Never in a conduit with 208 V. Runs 20-60 ft.
Route: unit base control knockout -> inside the curb -> down the duct shaft along the EA riser. No roof / wall penetrations.
Remote display: Greenheck 6-wire RJ12 cable (150 ft), no splices. BACnet MS/TP if a BMS is added: 22 AWG shielded pair.
After wiring, ADE / Greenheck reconfigure the controller: duct sensors on U2*/U6*, CO2 on U9, building pressure on exp. U1.


Duct smoke detectors: already installed and wired by the E.C.
If their contacts are to stop the unit, E.C. lands them on R-70 (fire input S6).

Cable	Device	BLK	WHT	RED	GRN	Length
C1	duct temp/RH Mamac HU-226	R -> PWR+	C -> PWR-	RH OUT -> U2*	TEMP OUT -> U6*	20-60 ft
C2	duct CO2 Honeywell C7232B	R -> G+	C -> GO	OUT1 -> U9	M -> GND	20-60 ft
C3	high static cutoff switch	R -> N.C.	N.C. -> G	spare	spare	< 20 ft

Wire colors are the usual 18/4 jacket set; if the spool differs, keep the same order: 24 V hot, common, signal 1, signal 2.

ERU-1 / ERU-2 / ERU-3 - duct sensor placement detail (section at the roof curb, not to scale)

Northern Wolves AC | IPA Church, Syosset NY | unit arrangement per Greenheck overview drawing (OA inlet at end, SA discharge and EA intake through the bottom)

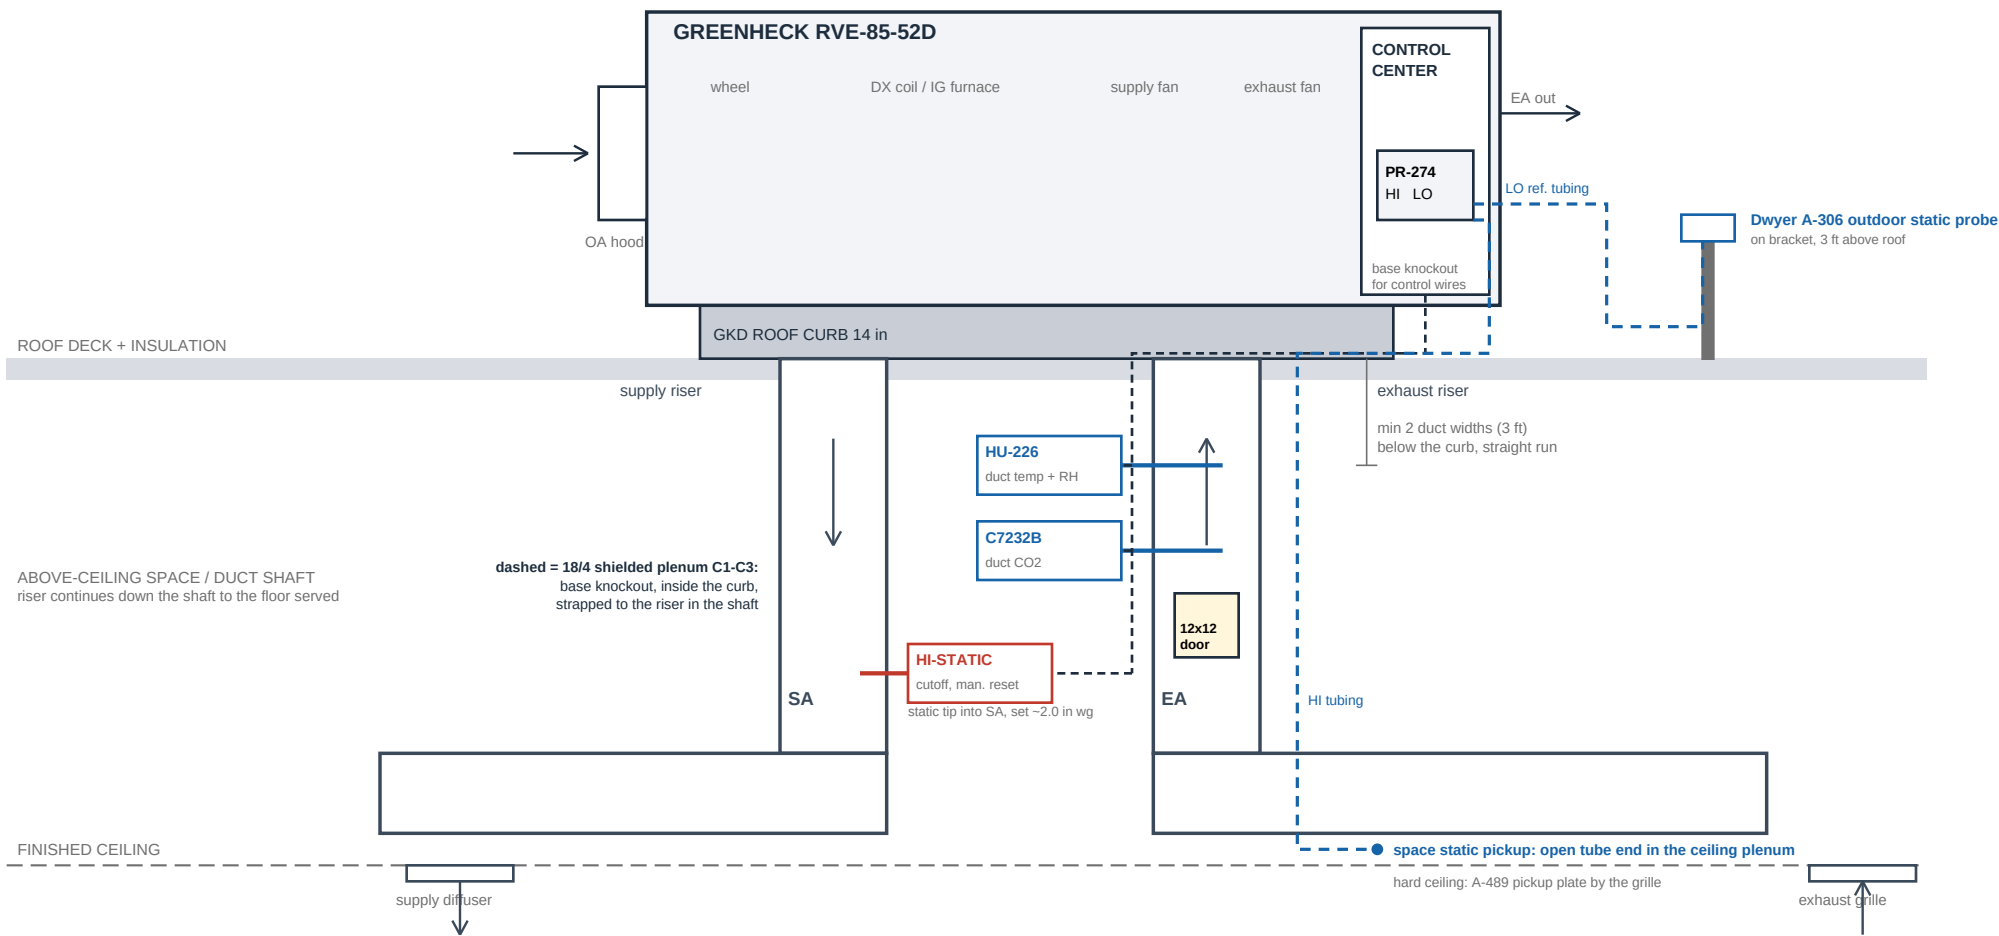

FLOOR OF THE SERVED SPACE (ERU-1, ERU-2: basement; ERU-3: first / second floor)

PLACEMENT NOTES

1. Temp/RH and CO2 sensors on the exhaust riser, first straight section reachable from inside the building: ERU-3 at the 2nd floor ceiling (grid 8.7-9.2), ERU-1 / ERU-2 at the top of the shaft under the roof deck.
2. Probes across the duct centerline through a gasketed hole; sensor housings outside the insulation; 12x12 access door within 2 ft. Nothing inside the curb or on the roof section of the duct.
3. High static cutoff on the supply riser 3-4 ft below the deck, static tip only (no low port). Manual reset, wired in series with the start circuit R-G (remove the S1 jumper).
4. PR-274 stays inside the control center. Two 1/4 in FR poly tubes: LO to the A-306 on the roof (sloped, no traps), HI down beside the riser to the ceiling plenum. Both tubes and the 18/4 cables leave the unit through the base knockout into the curb.
5. Smoke detectors already installed and wired by the E.C. Remote display: mount in the utility room / closet at the shaft, using Greenheck's own 150 ft cable, if the engineer does not accept the web UI.
