

Area	Location	Bulletin 3 G (qty / CFM)	SD R2 LD (qty / CFM)	Main in cloud (SD R2)
29-1	North-east corner, W 42nd St / Broadway	4 / 1,200	4 / 1,200	31.3/12 approx. 16 LF; 26.1/10 with offset down approx. 6 LF; 14"Ø approx. 6 LF
29-2	Seventh Ave, north	2 / 800	3 / 800	29.3/10 approx. 13 LF
29-3	Seventh Ave, Open Office 29.42	4 / 1,200	6 / 1,600	26.1/10 approx. 20 LF (with tee)
29-4	Broadway, north	1 / 400	2 / 400	34.4/12 approx. 8 LF
29-5	Seventh Ave, south (north end of sheet B)	3 / 1,200	4 / 1,200	31.3/12 approx. 12 LF; 14"Ø approx. 8 LF
29-6	Seventh Ave, south	3 / 1,200	4 / 1,200	14"Ø approx. 13 LF; 29.3/10 approx. 7 LF
30-1	Seventh Ave, north	2 / 800	3 / 800	26.1/10 approx. 12 LF
30-2	Seventh Ave, Open Office 30.35	3 / 1,200	5 / 1,300	26.1/10 approx. 12 LF; 12"Ø approx. 9 LF
30-3	South wall (W 41st St side)	3 / 1,200	4 / 1,200	32.2/16 approx. 40 LF
31-1	Seventh Ave, north (Focus Rm 31.65 / Corridor 31.51)	2 / 800	2 / 400	26.1/10 approx. 4 LF (at elbow)
31-2	Seventh Ave, Huddle Rms 31.46 / 31.47	2 / 800	3 / 800	28.1/12 approx. 15 LF
31-3	Seventh Ave, at IDF 31.44 (match line)	1 / 400	1 / 300	34.4/12 (same run as 31-4)
31-4	Seventh Ave, 7P Meeting Rm 31.43	2 / 800	3 / 900	34.4/12 approx. 20 LF
31-5	Seventh Ave, south	2 / 800	3 / 800	28.1/12 approx. 15 LF
31-6	Broadway, south	2 / 600	2 / 600	29.3/10 approx. 13 LF
	Total	36 / 13,400	49 / 13,500	




G counts are the Bulletin 3 diffuser tags inside each cloud (mapped from the shop drawing); each tag is counted once. The perimeter G diffusers in Bulletin 3 sit in the ceiling set in from the window; the SD R2 LDs sit at the window wall in plenum boxes, so the G ceiling diffusers, their branch duct and flex would be deleted.

Please confirm per area: (1) delete the G diffusers and their branches, and whether any are already installed (removal) or only furnished (credit / restock); (2) whether the perimeter main shown in the cloud is existing to remain with new taps only.

29th Floor - Bulletin 3 (engineer) vs Shop Drawing SD R2 (1/2)

Left: Bulletin 3 M-529, cloud shown dashed | Right: SD R2 M-529A/B.SD | Q1 = G ceiling linear diffusers replaced | Q2 = perimeter main

Snowflake Fitout - 7 Times Square, Floors 29-31 | Perimeter Linear Diffusers

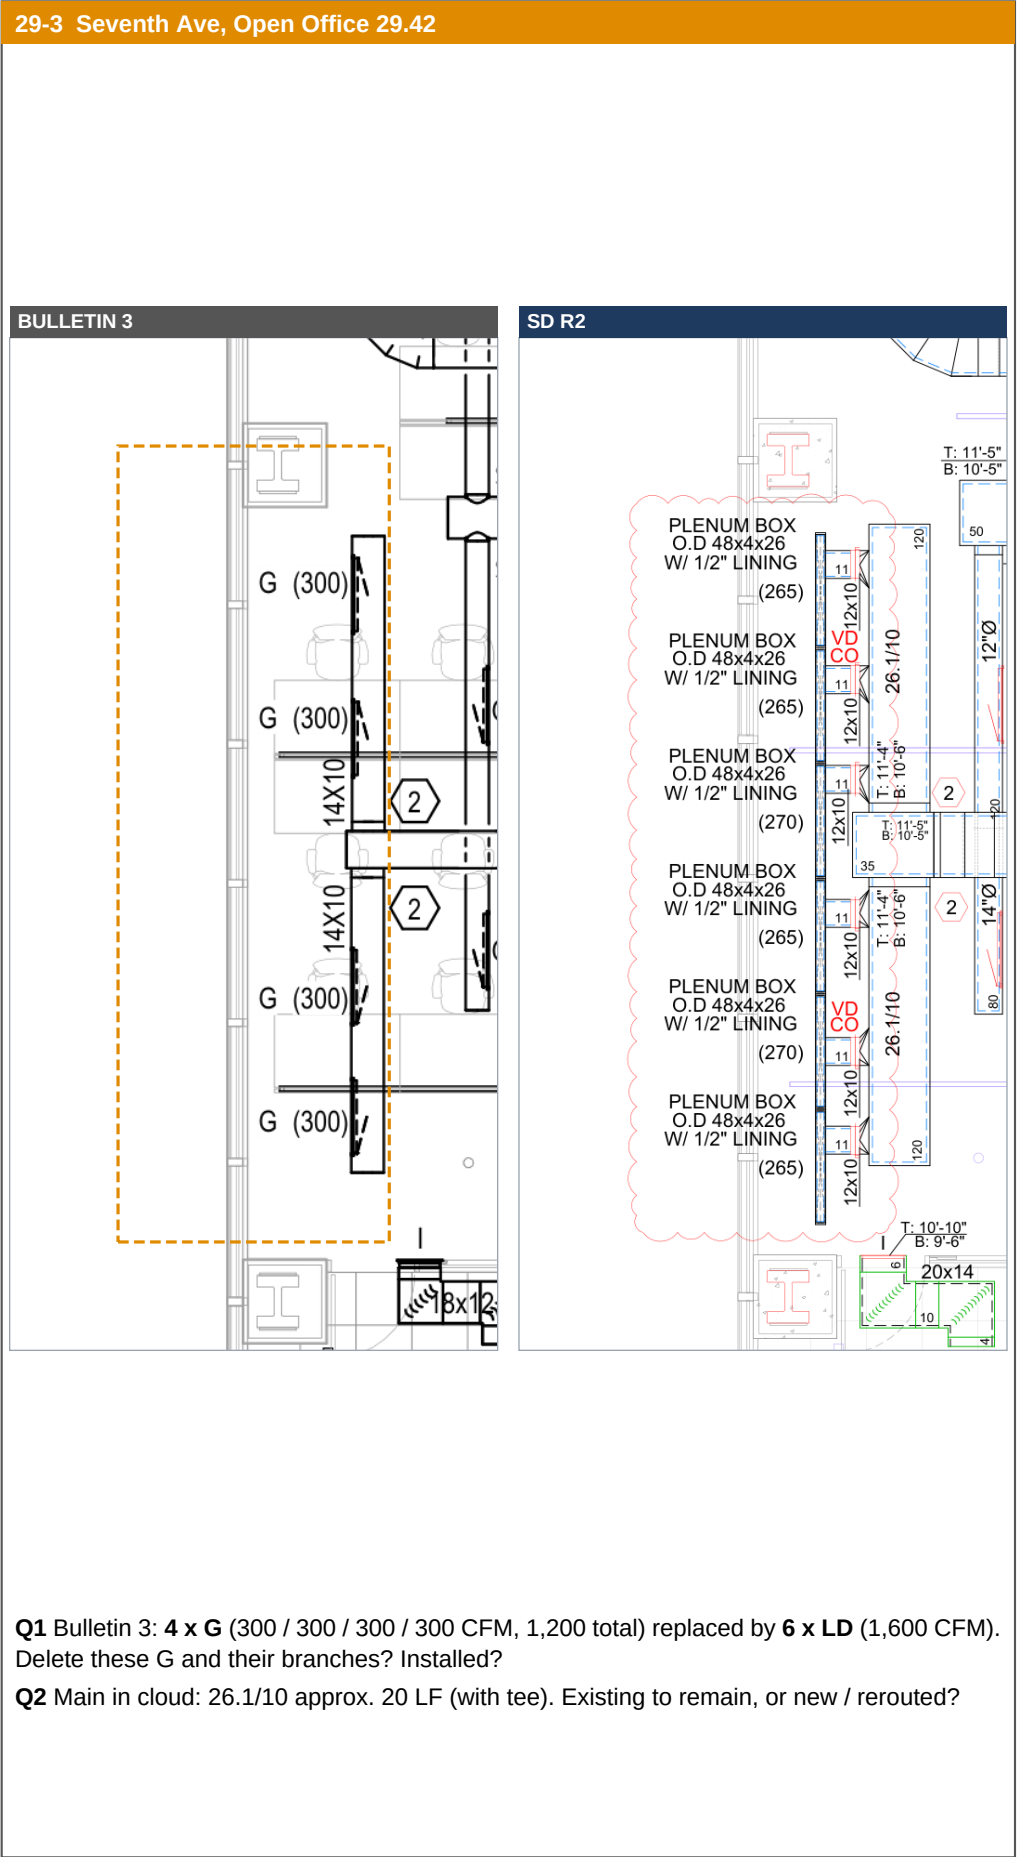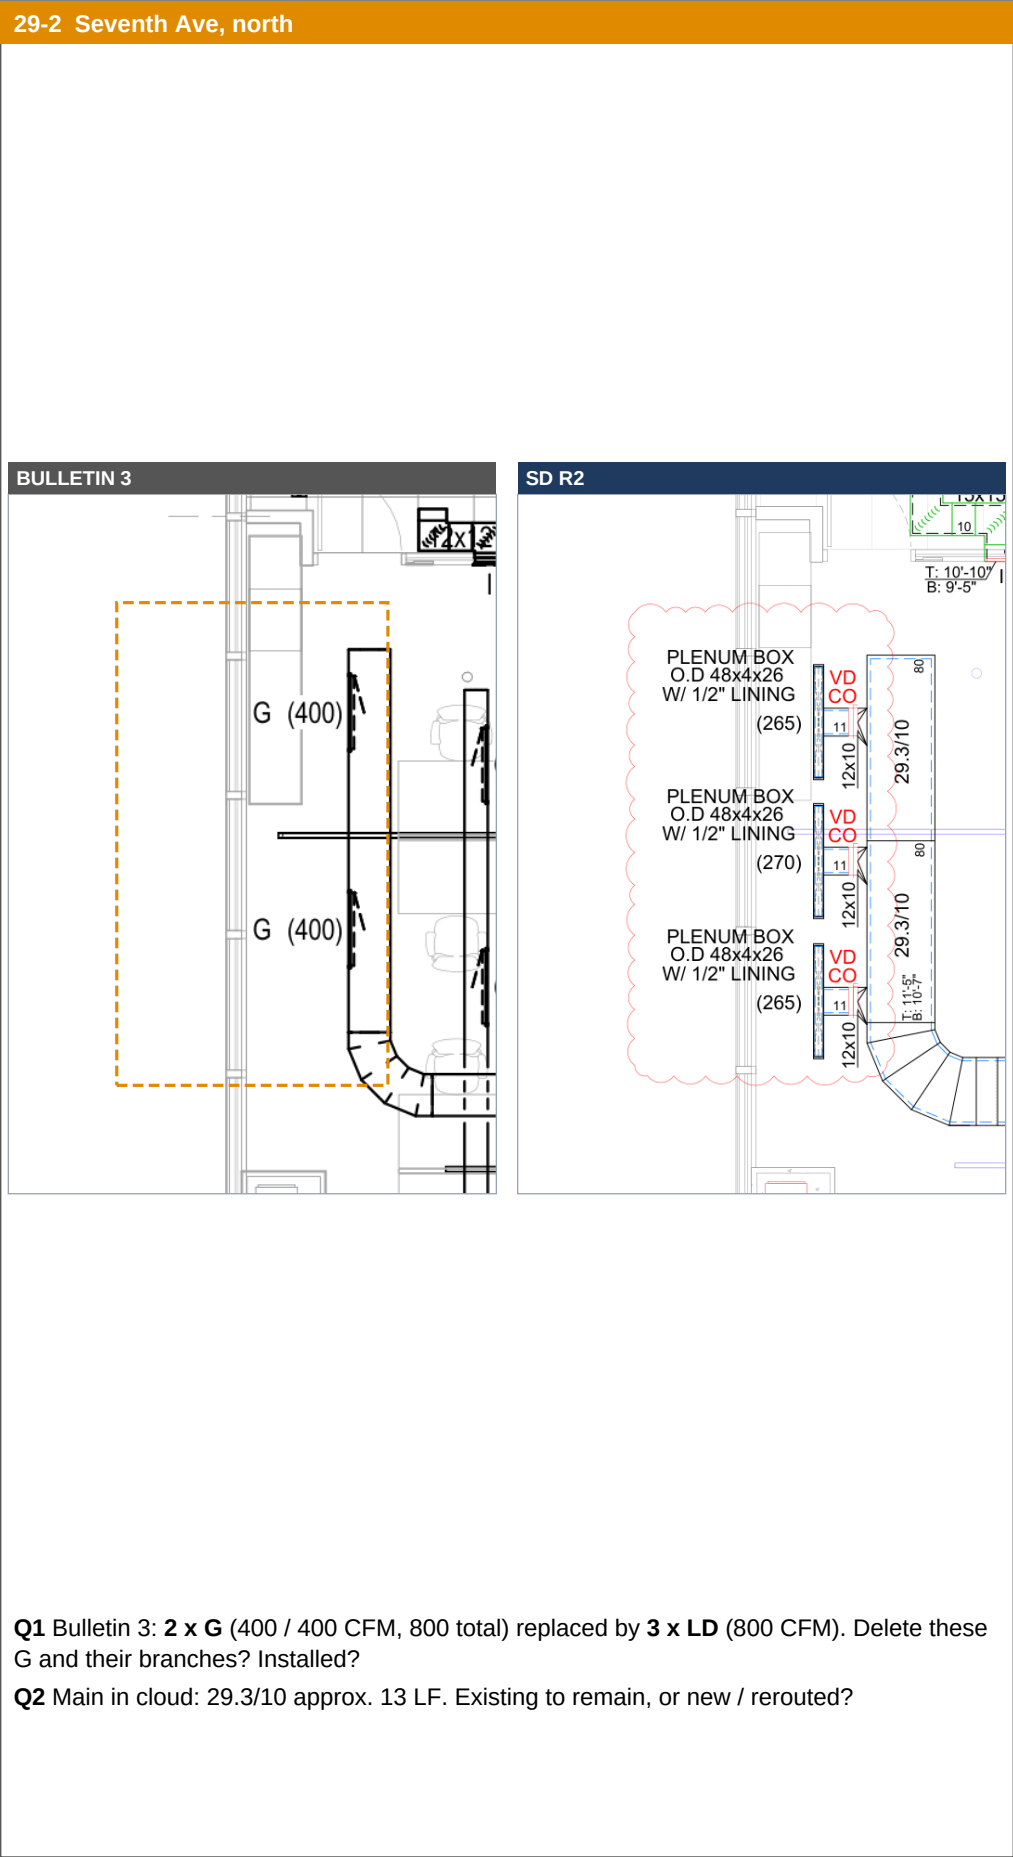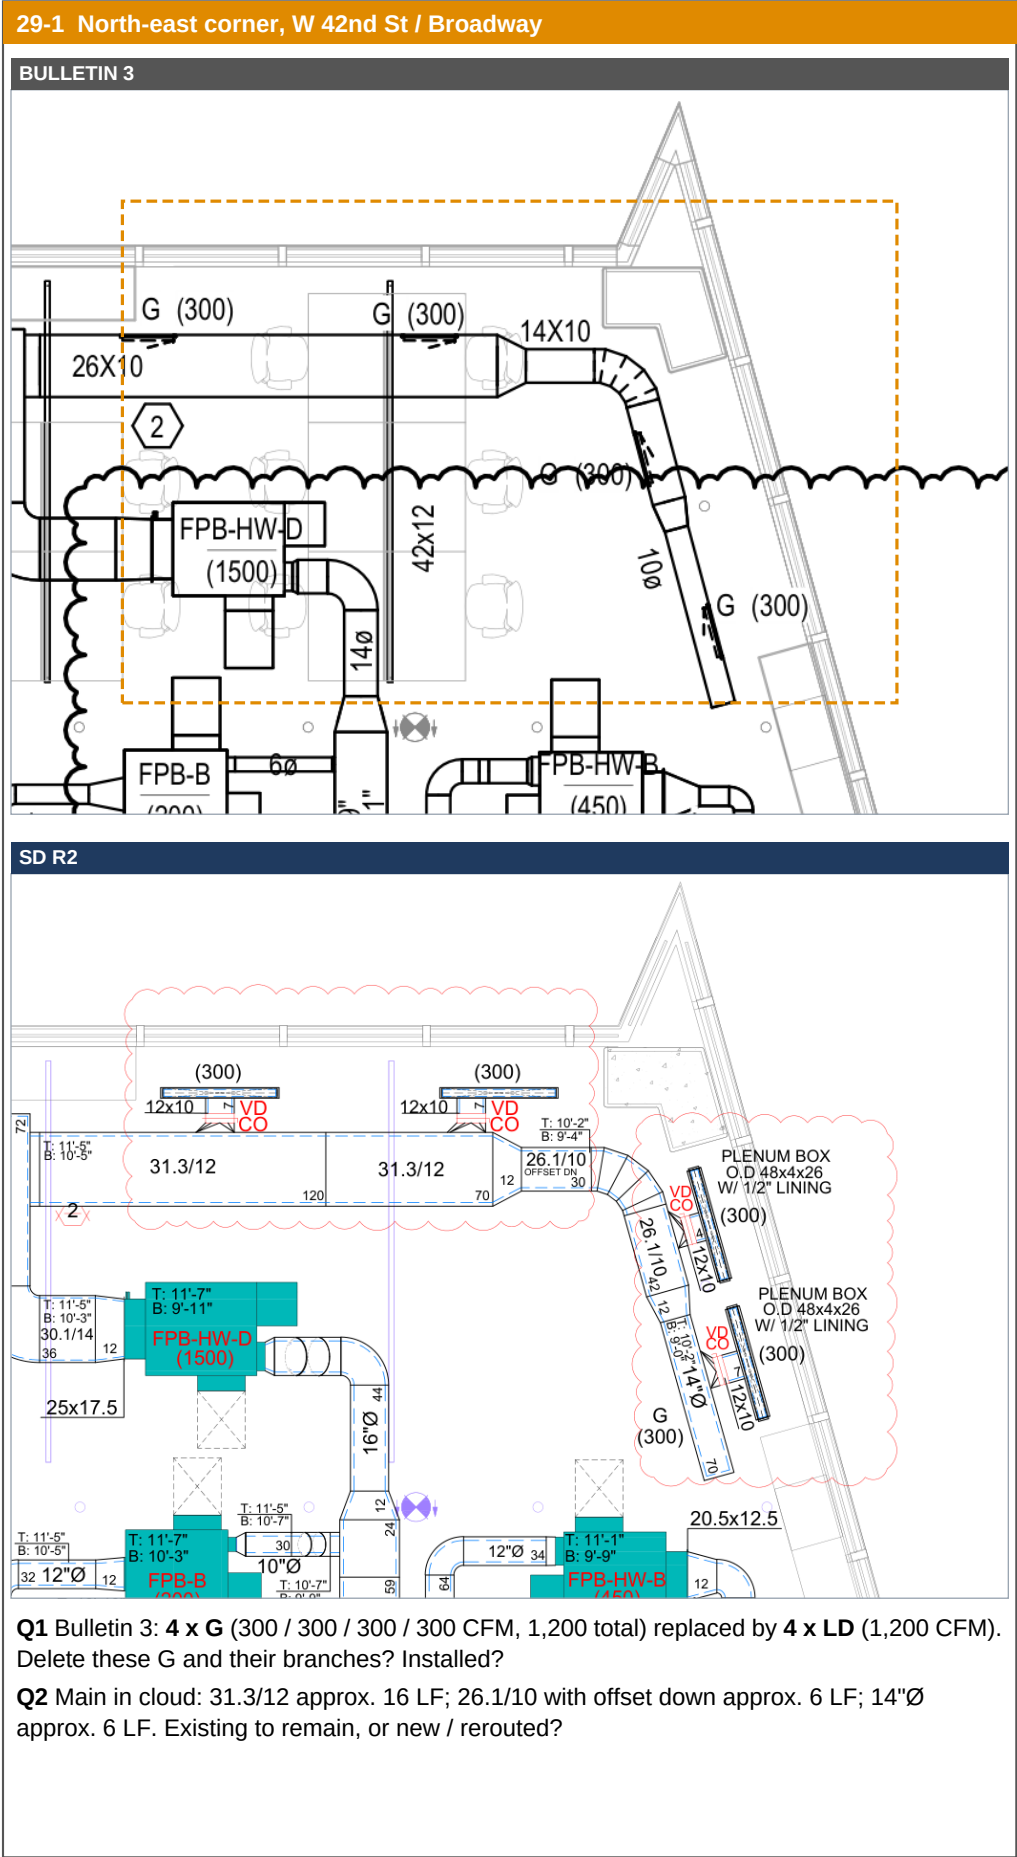

29-4 Broadway, north

BULLETIN 3

SD R2

Q1 Bulletin 3: **1 x G** (400 CFM, 400 total) replaced by **2 x LD** (400 CFM). Delete these G and their branches? Installed?

Q2 Main in cloud: 34.4/12 approx. 8 LF. Existing to remain, or new / rerouted?

29-5 Seventh Ave, south (north end of sheet B)

BULLETIN 3

SD R2

Q1 Bulletin 3: **3 x G** (400 / 400 / 400 CFM, 1,200 total) replaced by **4 x LD** (1,200 CFM). Delete these G and their branches? Installed?

Q2 Main in cloud: 31.3/12 approx. 12 LF; 14"Ø approx. 8 LF. Existing to remain, or new / rerouted?

29-6 Seventh Ave, south

BULLETIN 3

SD R2

Q1 Bulletin 3: **3 x G** (400 / 400 / 400 CFM, 1,200 total) replaced by **4 x LD** (1,200 CFM). Delete these G and their branches? Installed?

Q2 Main in cloud: 14"Ø approx. 13 LF; 29.3/10 approx. 7 LF. Existing to remain, or new / rerouted?

30-1 Seventh Ave, north

BULLETIN 3

SD R2

Q1 Bulletin 3: **2 x G** (400 / 400 CFM, 800 total) replaced by **3 x LD** (800 CFM). Delete these G and their branches? Installed?

Q2 Main in cloud: 26.1/10 approx. 12 LF. Existing to remain, or new / rerouted?

30-2 Seventh Ave, Open Office 30.35

BULLETIN 3

SD R2

Q1 Bulletin 3: **3 x G** (400 / 400 / 400 CFM, 1,200 total) replaced by **5 x LD** (1,300 CFM). Delete these G and their branches? Installed?

Q2 Main in cloud: 26.1/10 approx. 12 LF; 12"Ø approx. 9 LF. Existing to remain, or new / rerouted?







30-3 South wall (W 41st St side)

BULLETIN 3


SD R2

Q1 Bulletin 3: **3 x G** (400 / 400 / 400 CFM, 1,200 total) replaced by **4 x LD** (1,200 CFM). Delete these G and their branches? Installed?

Q2 Main in cloud: 32.2/16 approx. 40 LF. Existing to remain, or new / rerouted?

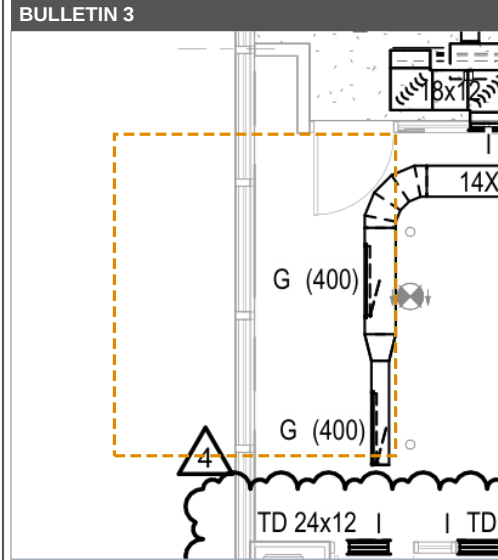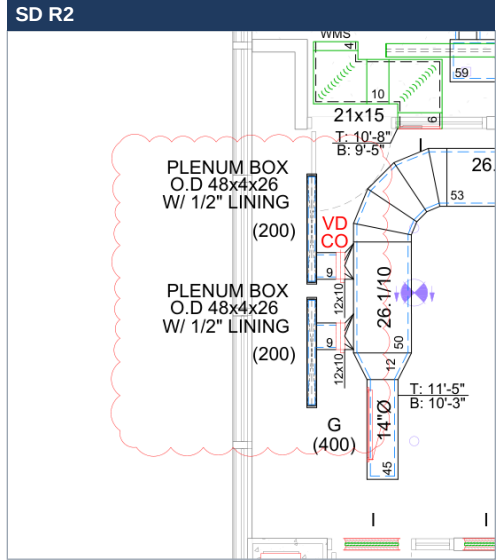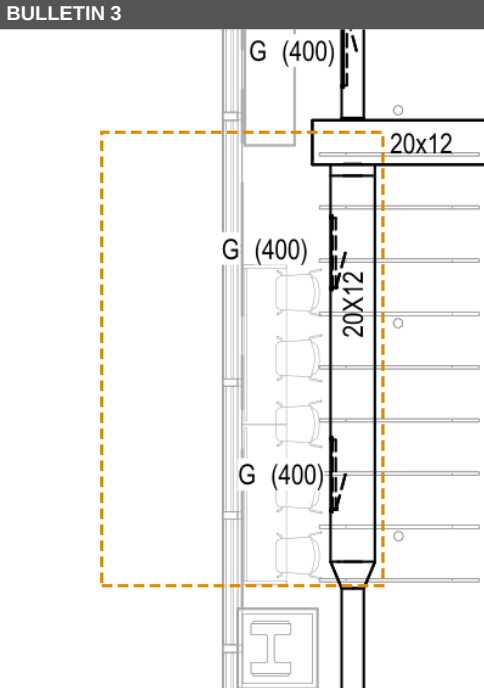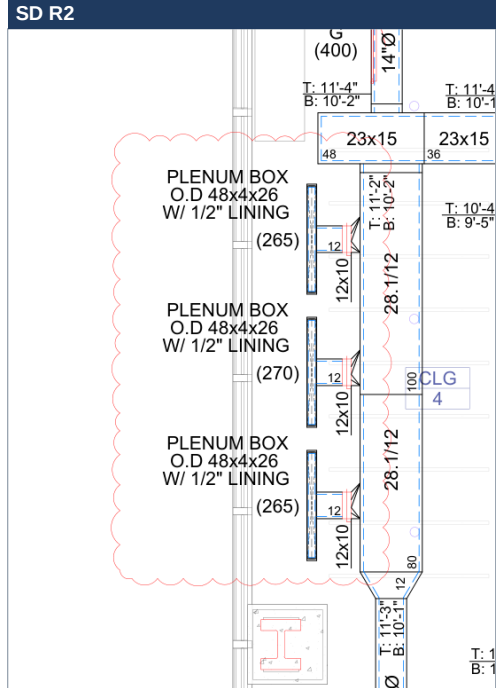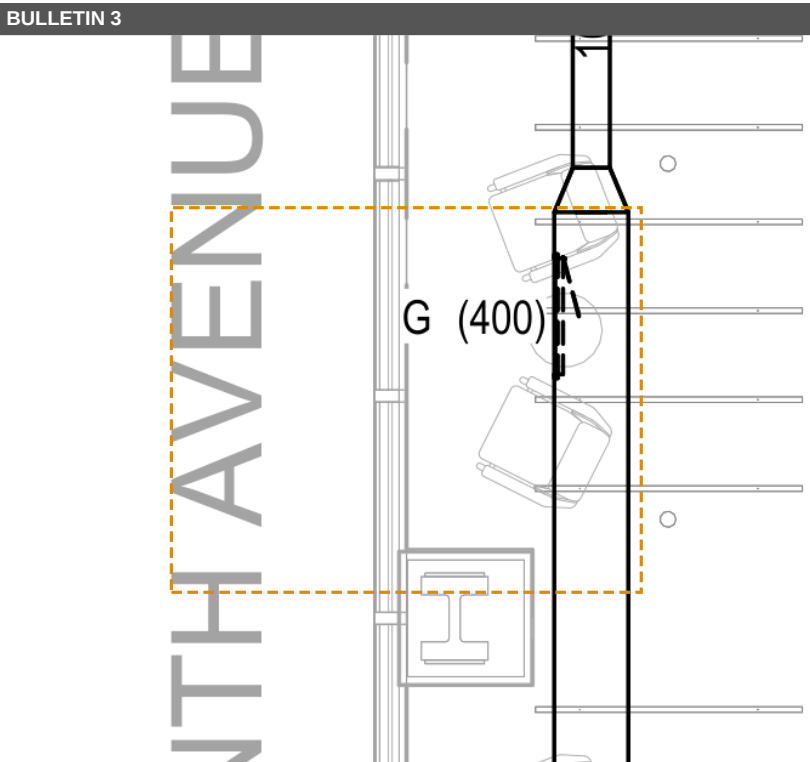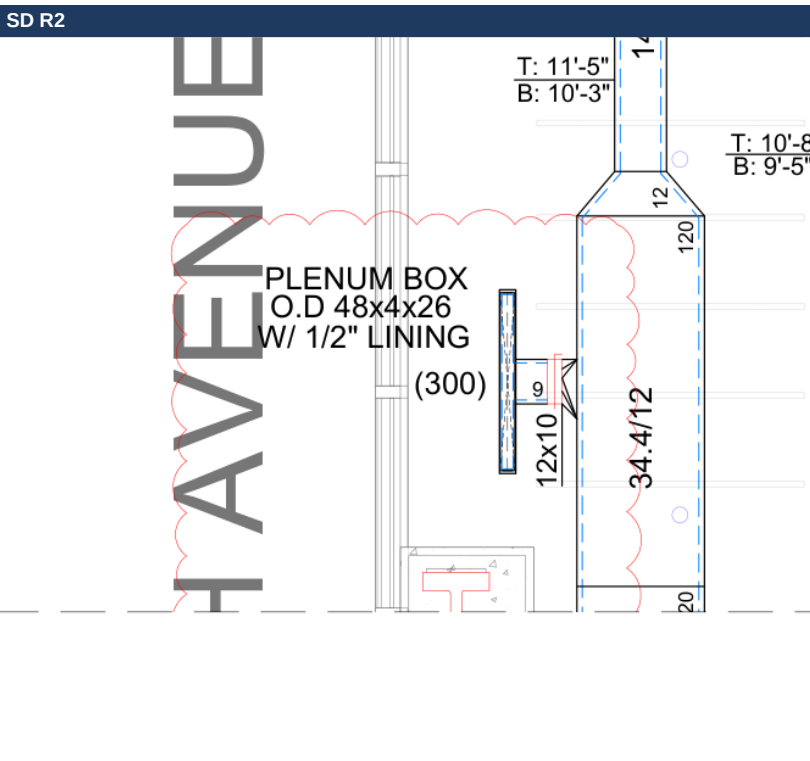31-1 Seventh Ave, north (Focus Rm 31.65 / Corridor 31.51)	31-2 Seventh Ave, Huddle Rms 31.46 / 31.47	31-3 Seventh Ave, at IDF 31.44 (match line)
BULLETIN 3  SD R2  Q1 Bulletin 3: 2 x G (400 / 400 CFM, 800 total) replaced by 2 x LD (400 CFM). Delete these G and their branches? Installed? Q2 Main in cloud: 26.1/10 approx. 4 LF (at elbow). Existing to remain, or new / rerouted?	BULLETIN 3  SD R2  Q1 Bulletin 3: 2 x G (400 / 400 CFM, 800 total) replaced by 3 x LD (800 CFM). Delete these G and their branches? Installed? Q2 Main in cloud: 28.1/12 approx. 15 LF. Existing to remain, or new / rerouted?	BULLETIN 3  SD R2  Q1 Bulletin 3: 1 x G (400 CFM, 400 total) replaced by 1 x LD (300 CFM). Delete these G and their branches? Installed? Q2 Main in cloud: 34.4/12 (same run as 31-4). Existing to remain, or new / rerouted?


31-4 Seventh Ave, 7P Meeting Rm 31.43

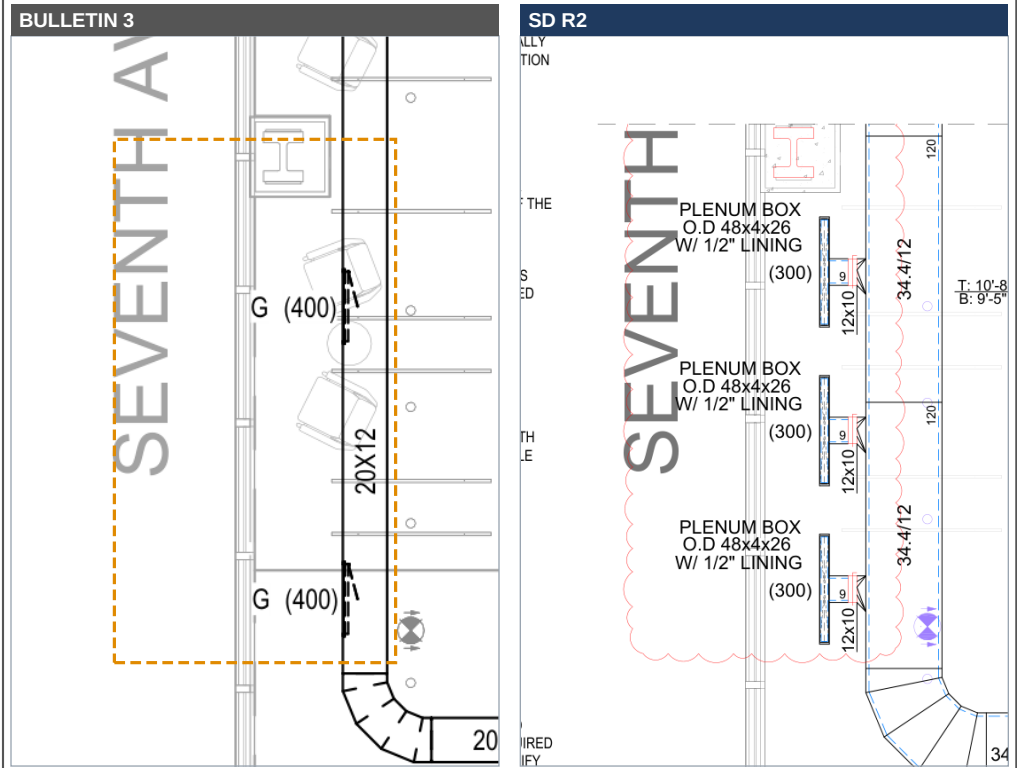

Q1 Bulletin 3: **2 x G** (400 / 400 CFM, 800 total) replaced by **3 x LD** (900 CFM). Delete these G and their branches? Installed?

Q2 Main in cloud: 34.4/12 approx. 20 LF. Existing to remain, or new / rerouted?


31-5 Seventh Ave, south

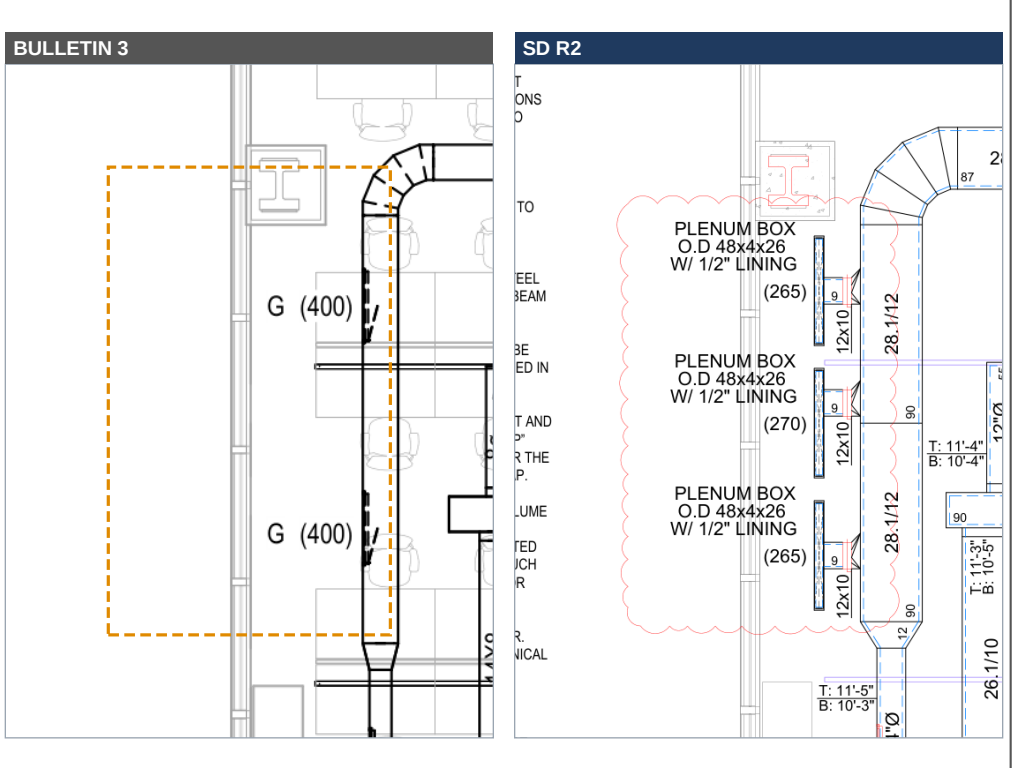

Q1 Bulletin 3: **2 x G** (400 / 400 CFM, 800 total) replaced by **3 x LD** (800 CFM). Delete these G and their branches? Installed?

Q2 Main in cloud: 28.1/12 approx. 15 LF. Existing to remain, or new / rerouted?

31-6 Broadway, south

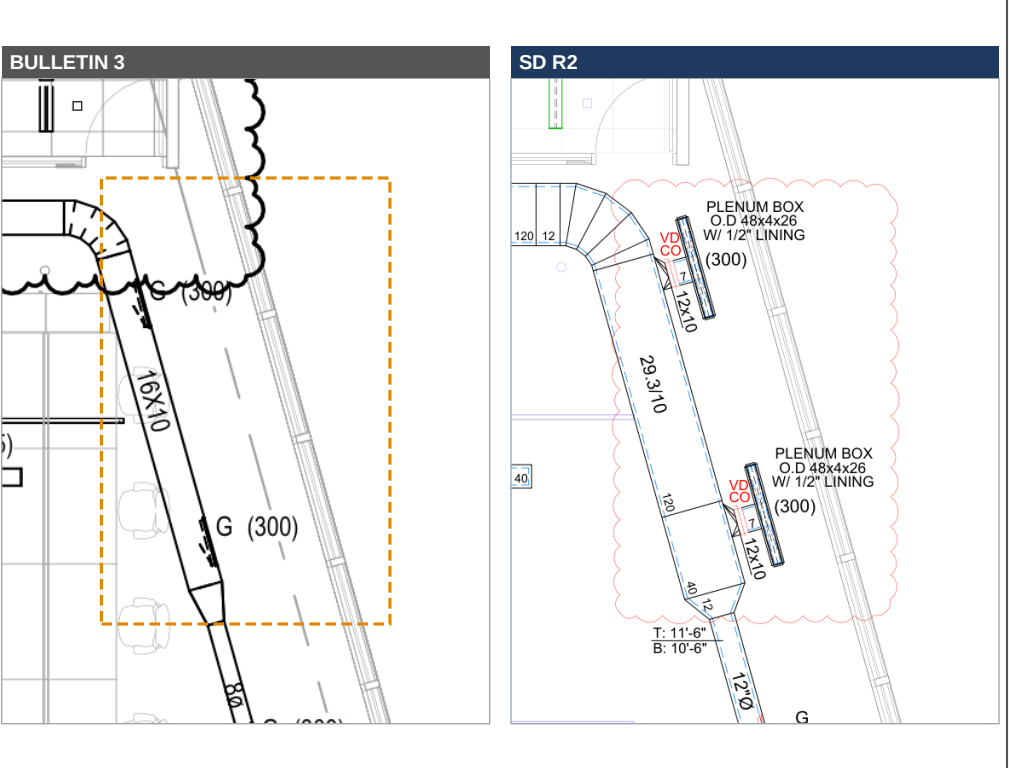

Q1 Bulletin 3: **2 x G** (300 / 300 CFM, 600 total) replaced by **2 x LD** (600 CFM). Delete these G and their branches? Installed?

Q2 Main in cloud: 29.3/10 approx. 13 LF. Existing to remain, or new / rerouted?
