

Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

ID	Task Mode	Task Name	Duration	Start	Finish
1		**Snowflake Floors 29-31 Project Schedule**	**173 days**	**Wed 5/20/26**	**Fri 1/15/27**
2		**Pre Construction**	**117 days**	**Wed 5/20/26**	**Thu 10/29/26**
3		GC Award	1 day	Wed 5/20/26	Wed 5/20/26
4		Award Trades, Insurance	3 wks	Thu 5/21/26	Wed 6/10/26
5		Review Food Service Bids	6 days	Thu 5/21/26	Thu 5/28/26
6		Award Food Service Vendor	2 wks	Fri 5/29/26	Thu 6/11/26
7		**Procurement (Inclusive of Submittals)**	**101 days**	**Thu 6/11/26**	**Thu 10/29/26**
24		**Construction Floors 29,30,31**	**168 days**	**Wed 5/27/26**	**Fri 1/15/27**
25		**GC Mobilization**	**3 days**	**Wed 5/27/26**	**Fri 5/29/26**
26		**Sprinkler Hydro Test**	**1 wk**	**Fri 9/18/26**	**Thu 9/24/26**
27		**Remove Temp Loop/Tie In Permanent Loop**	**2 days**	**Fri 9/25/26**	**Mon 9/28/26**
28		**IDF Room Ready**	**1 day**	**Fri 11/20/26**	**Fri 11/20/26**
29		**IDF Network Live**	**1 day**	**Fri 12/4/26**	**Fri 12/4/26**
30		**Air and Water Balancing**	**2 wks**	**Mon 11/9/26**	**Fri 11/20/26**
31		**Layout Furniture Onsite**	**1 wk**	**Tue 6/23/26**	**Mon 6/29/26**
32		**Deliver And Install Furniture**	**4 wks**	**Mon 12/21/26**	**Fri 1/15/27**
33		**Substantial Completion**	**1 day**	**Fri 12/18/26**	**Fri 12/18/26**
34		**Punch List/Project Completion**	**4 wks**	**Mon 12/21/26**	**Fri 1/15/27**
35		**DOB/TCO/PA- 1/22/27 Submission For DOB App**	**13 days**	**Mon 12/7/26**	**Wed 12/23/26**
36		Plumbing and Sprinkler Sign Offs	1 wk	Mon 12/7/26	Fri 12/11/26
37		Emergency Lighting Inspection	1 day	Mon 12/14/26	Mon 12/14/26
38		Fire Alarm Pre Test(Target)	**1 day**	**Mon 12/7/26**	**Mon 12/7/26**
39		FDNY (Target)	**1 day**	**Mon 12/14/26**	**Mon 12/14/26**
40		Fire Alarm Affadavit (If Required)	1 wk	Tue 12/15/26	Mon 12/21/26
41		TCO Pre Walk/Call for Inspection	3 days	Wed 12/16/26	Fri 12/18/26
42		DOB Walk	3 days	Mon 12/21/26	Wed 12/23/26
43		**Open Workstations and Seating**	**147 days**	**Thu 6/11/26**	**Fri 1/1/27**

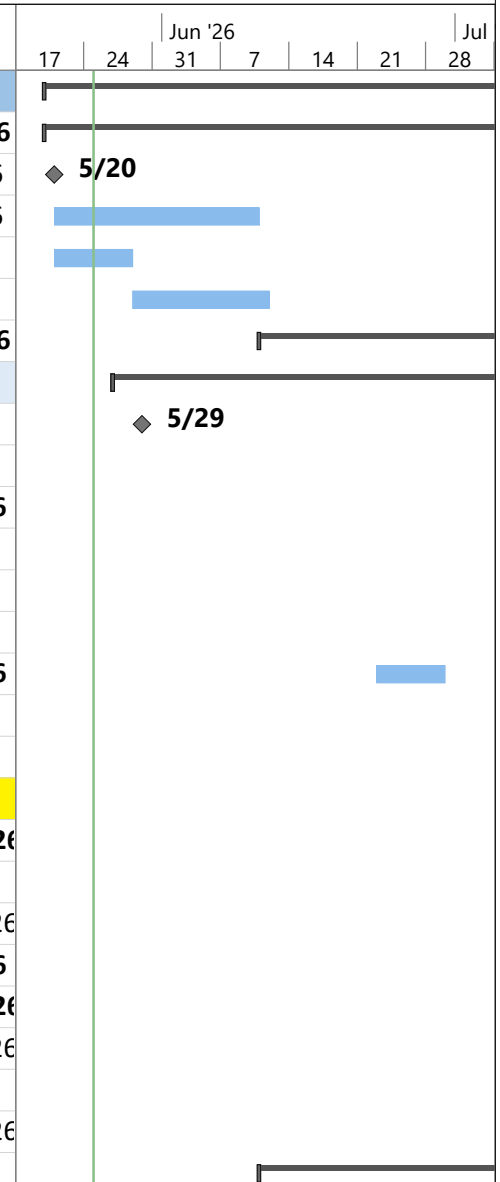


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

ID	Task Mode	Task Name	Duration	Start	Finish
44		**HVAC**	**85 days**	**Thu 6/11/26**	**Wed 10/7/26**
45		Tin Sketching	3 days	Thu 6/11/26	Mon 6/15/26
46		Shop Drawing Approval	2 wks	Tue 6/16/26	Mon 6/29/26
47		Duct Work	3 wks	Tue 6/30/26	Mon 7/20/26
48		Testing	3 days	Tue 7/21/26	Thu 7/23/26
49		Insulation	2 wks	Fri 7/24/26	Thu 8/6/26
50		Control Wiring Home Runs	2 wks	Tue 7/7/26	Mon 7/20/26
51		Diffusers	12 days	Tue 9/22/26	Wed 10/7/26
52		T-stats	1 wk	Thu 9/3/26	Thu 9/10/26
53		**Fire Protection**	**27 days**	**Tue 7/21/26**	**Wed 8/26/26**
54		Mains	2 wks	Tue 7/21/26	Mon 8/3/26
55		Branch Piping	2 wks	Tue 8/4/26	Mon 8/17/26
56		Upright Heads	7 days	Tue 8/18/26	Wed 8/26/26
57		**Electric & Fire Alarm**	**62 days**	**Tue 7/7/26**	**Wed 9/30/26**
58		Home Runs	2 wks	Tue 7/7/26	Mon 7/20/26
59		Wall Rough in	2 wks	Tue 7/7/26	Mon 7/20/26
60		Core Drills	2 wks	Tue 7/14/26	Mon 7/27/26
61		Terminate Wall Devices	2 wks	Thu 9/3/26	Thu 9/17/26
62		Open Ceiling Lighting	4 wks	Thu 9/3/26	Wed 9/30/26
63		**Data**	**47.5 days**	**Tue 7/14/26**	**Thu 9/17/26**
64		Pull Cabling	3 wks	Tue 7/14/26	Mon 8/3/26
65		Terminate Devices	2 wks	Thu 9/3/26	Thu 9/17/26
66		**Security**	**89 days**	**Tue 8/4/26**	**Fri 12/4/26**
67		Pull Cabling	5 days	Tue 8/4/26	Mon 8/10/26
68		Cameras	1 wk	Mon 11/23/26	Fri 11/27/26
69		Camera Aiming	1 wk	Mon 11/30/26	Fri 12/4/26
70		**Drywall and Ceilings**	**45.5 days**	**Thu 6/11/26**	**Thu 8/13/26**

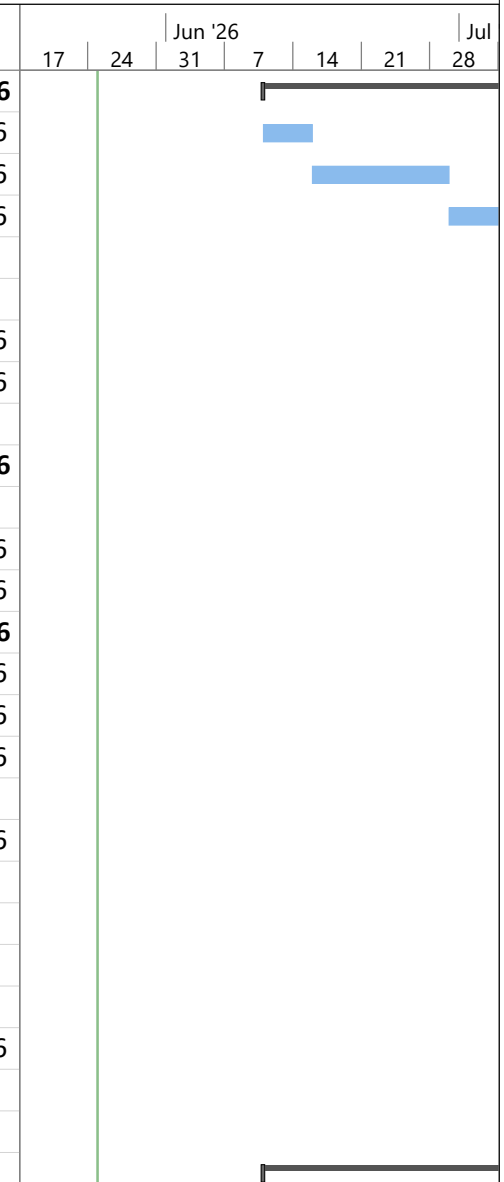


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

ID	Task Mode	Task Name	Duration	Start	Finish
71		Layout	6 days	Thu 6/11/26	Thu 6/18/26
72		Architect Approval	2 days	Fri 6/19/26	Mon 6/22/26
73		Top and Bottom Track	1 wk	Tue 6/23/26	Mon 6/29/26
74		Framing	1 wk	Tue 6/30/26	Mon 7/6/26
75		Insulation & Drywall	2 wks	Tue 7/14/26	Mon 7/27/26
76		Taping	2.5 wks	Tue 7/28/26	Thu 8/13/26
77		**K13**	**73 days**	**Tue 8/18/26**	**Thu 11/26/26**
78		Protecion after MEP	1 wk	Tue 8/18/26	Mon 8/24/26
79		Prep and Spray Ceilings	4 wks	Tue 8/25/26	Mon 9/21/26
80		Touch Ups Post Construction	1 wk	Fri 11/20/26	Thu 11/26/26
81		**Flooring**	**95 days**	**Thu 6/11/26**	**Wed 10/21/26**
82		Floor Grinding	4 wks	Thu 6/11/26	Wed 7/8/26
83		Protection	1 wk	Thu 7/9/26	Wed 7/15/26
84		Install Carpet Tile	3 wks	Thu 10/1/26	Wed 10/21/26
85		Install Base	1.5 wks	Thu 9/3/26	Mon 9/14/26
86		**Window Treatment**	**10 days**	**Thu 9/17/26**	**Wed 9/30/26**
87		Install Shades	2 wks	Thu 9/17/26	Wed 9/30/26
88		**Paint**	**101.5 days**	**Thu 8/13/26**	**Fri 1/1/27**
89		Prime Walls & Soffits	7 days	Thu 8/13/26	Mon 8/24/26
90		1st Coat	8 days	Mon 8/24/26	Thu 9/3/26
91		2nd Coat (During Punch List)	2 wks	Mon 12/21/26	Fri 1/1/27
92		**Core Bathrooms**	**80 days**	**Mon 9/14/26**	**Fri 1/1/27**
93		**HVAC**	**3 days**	**Mon 11/9/26**	**Wed 11/11/26**
94		Balancing	3 days	Mon 11/9/26	Wed 11/11/26
95		**Plumbing**	**15.5 days**	**Mon 9/14/26**	**Mon 10/5/26**
96		Remove Sinks and Disconnect Fixtures	1 wk	Mon 9/14/26	Fri 9/18/26
97		Install New Toilets and Urinals	1.5 wks	Mon 9/21/26	Wed 9/30/26

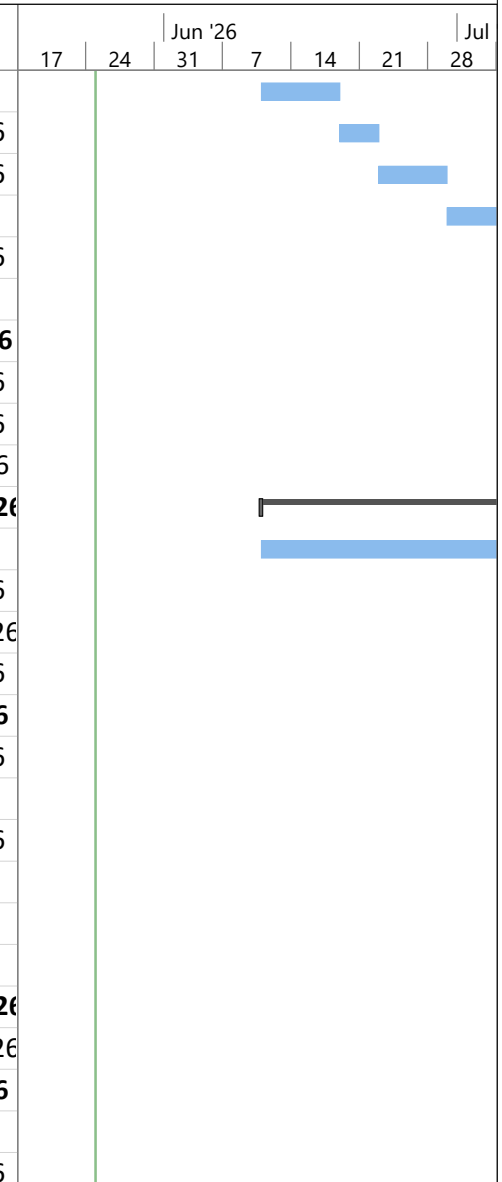


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

ID	Task Mode	Task Name	Duration	Start	Finish
98		Sinks & Faucets	3 days	Wed 9/30/26	Mon 10/5/26
99		**Carpentry**	**25 days**	**Mon 9/14/26**	**Fri 10/16/26**
100		New Ceiling Framing and Lighting	3 wks	Mon 9/14/26	Fri 10/2/26
101		Drywall and Taping	2 wks	Mon 10/5/26	Fri 10/16/26
102		Toilet Partitions	1 wk	Mon 9/14/26	Fri 9/18/26
103		Toilet Accessories	2 wks	Mon 9/21/26	Fri 10/2/26
104		**Stone**	**12.5 days**	**Mon 9/14/26**	**Wed 9/30/26**
105		Measure and Fabricate Counter Tops	1 wk	Mon 9/14/26	Fri 9/18/26
106		Install Counters & Backsplash	1.5 wks	Mon 9/21/26	Wed 9/30/26
107		**Paint**	**55 days**	**Mon 10/19/26**	**Fri 1/1/27**
108		Prime and Paint	1 wk	Mon 10/19/26	Fri 10/23/26
109		2nd Coat/Touch Ups	2 wks	Mon 12/21/26	Fri 1/1/27
110		**Elevator Lobby/Stair Case/Reception**	**147 days**	**Thu 6/11/26**	**Fri 1/1/27**
111		**HVAC**	**81.5 days**	**Thu 6/11/26**	**Fri 10/2/26**
112		Tin Sketching	3 days	Thu 6/11/26	Mon 6/15/26
113		Shop Drawing Approval	2 wks	Tue 6/16/26	Mon 6/29/26
114		Duct Work	3 wks	Tue 6/30/26	Mon 7/20/26
115		Medium Pressure Test (All Areas)	3 days	Tue 7/21/26	Thu 7/23/26
116		Insulation	1 wk	Fri 7/24/26	Thu 7/30/26
117		Control Wiring	3 wks	Fri 7/24/26	Thu 8/13/26
118		T-stats	2 wks	Fri 9/18/26	Fri 10/2/26
119		**Fire Protection**	**22.5 days**	**Tue 7/21/26**	**Thu 8/20/26**
120		Mains	2 wks	Tue 7/21/26	Mon 8/3/26
121		Branch Piping	1.5 wks	Tue 8/4/26	Thu 8/13/26
122		Upright Heads	1 wk	Thu 8/13/26	Thu 8/20/26
123		**Electric & Fire Alarm**	**58.5 days**	**Tue 7/7/26**	**Fri 9/25/26**
124		Home Runs	3 wks	Tue 7/7/26	Mon 7/27/26

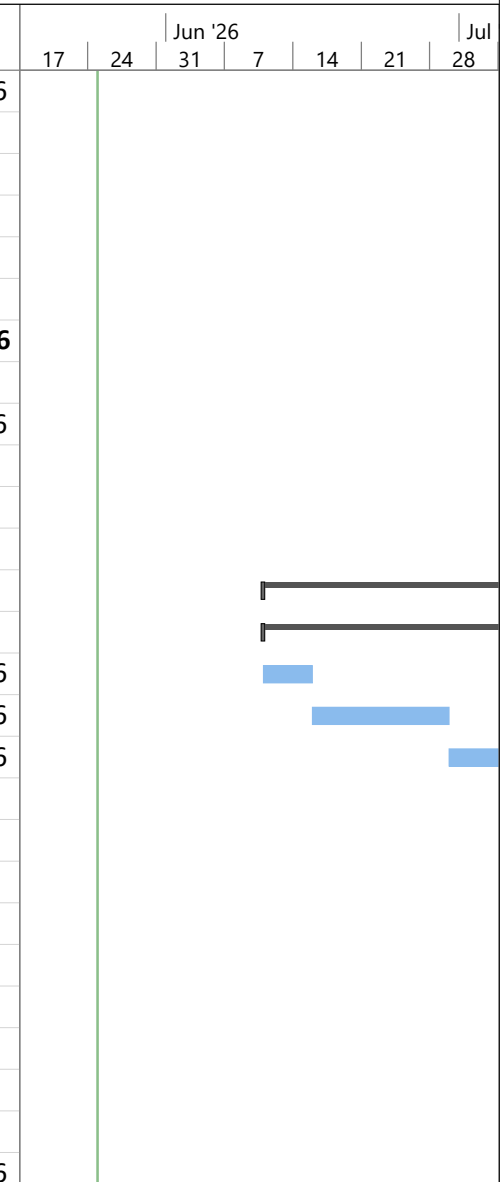


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

ID	Task Mode	Task Name	Duration	Start	Finish
125		Wall Rough in	2.5 wks	Wed 7/8/26	Fri 7/24/26
126		Install Light Fixtures(With Ceiling)	3 wks	Thu 8/20/26	Wed 9/9/26
127		Terminate Wall Devices	1 wk	Fri 9/18/26	Fri 9/25/26
128		**Data/Security**	**80 days**	**Fri 7/24/26**	**Fri 11/13/26**
129		Pull Cabling	3 wks	Fri 7/24/26	Fri 8/14/26
130		Wiring For Mag Locks	1 wk	Fri 10/16/26	Fri 10/23/26
131		Card Readers (Live for Pre Test)	2 wks	Fri 10/30/26	Fri 11/13/26
132		**Drywall and Ceilings**	**55.5 days**	**Thu 6/11/26**	**Thu 8/27/26**
133		Layout	6 days	Thu 6/11/26	Thu 6/18/26
134		Architect Approval	3 days	Fri 6/19/26	Tue 6/23/26
135		Top and Bottom Track	1.5 wks	Wed 6/24/26	Fri 7/3/26
136		Wall Framing	2.5 wks	Wed 7/1/26	Fri 7/17/26
137		Insulation & Drywall	2 wks	Wed 7/15/26	Tue 7/28/26
138		Taping	2 wks	Wed 7/29/26	Tue 8/11/26
139		Specialty Ceilings	2 wks	Thu 8/13/26	Thu 8/27/26
140		**K13**	**73 days**	**Tue 8/18/26**	**Thu 11/26/26**
141		Protecion after MEP	1 wk	Tue 8/18/26	Mon 8/24/26
142		Prep and Spray Ceilings	3 wks	Tue 8/25/26	Mon 9/14/26
143		Touch Ups Post Construction	1 wk	Fri 11/20/26	Thu 11/26/26
144		**Metal and Glass/ Tile**	**30 days**	**Fri 9/18/26**	**Fri 10/30/26**
145		Entry Way Tile	4 wks	Fri 9/18/26	Fri 10/16/26
146		Entry Doors	2 wks	Fri 10/16/26	Fri 10/30/26
147		**Flooring**	**131 days**	**Thu 6/11/26**	**Thu 12/10/26**
148		Floor Grinding and Mock up	4 wks	Thu 6/11/26	Wed 7/8/26
149		Protection	4 days	Thu 7/9/26	Tue 7/14/26
150		Final Sanding and Polishing	1 wk	Fri 12/4/26	Thu 12/10/26
151		**Stair Finishes**	**100 days**	**Wed 7/22/26**	**Tue 12/8/26**

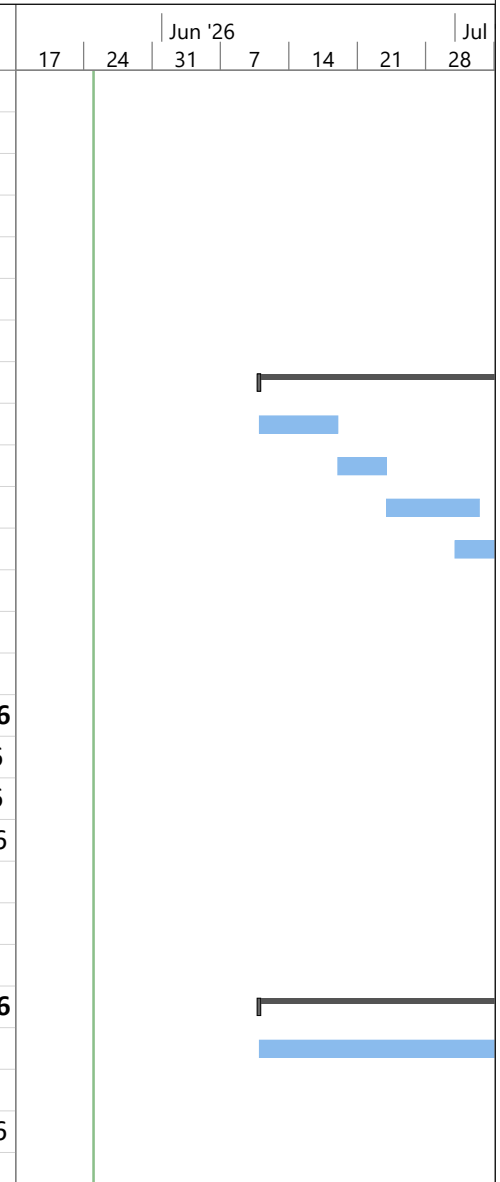


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

ID	Task Mode	Task Name	Duration	Start	Finish
152		Shop Drawings and Approvals	4 wks	Wed 7/22/26	Tue 8/18/26
153		Guard Rail Shoes	1 wk	Wed 10/28/26	Tue 11/3/26
154		EKG	2 wks	Wed 11/4/26	Tue 11/17/26
155		Stone Treads	2 wks	Wed 11/18/26	Tue 12/1/26
156		Glass and Handrails	1 wk	Wed 12/2/26	Tue 12/8/26
157		**Paint**	**103 days**	**Wed 8/12/26**	**Fri 1/1/27**
158		Prime Walls	1.5 wks	Wed 8/12/26	Fri 8/21/26
159		1st Coat	2 wks	Fri 9/4/26	Fri 9/18/26
160		2nd Coat (Punch List)	2 wks	Mon 12/21/26	Fri 1/1/27
161		**Conference Rooms/Phone Rooms**	**157 days**	**Thu 6/11/26**	**Fri 1/15/27**
162		**HVAC**	**97.5 days**	**Thu 6/11/26**	**Mon 10/26/26**
163		Tin Sketching	6 days	Thu 6/11/26	Thu 6/18/26
164		Shop Drawing Approval	2 wks	Fri 6/19/26	Thu 7/2/26
165		Duct Work	3 wks	Fri 7/3/26	Thu 7/23/26
166		Testing	3 days	Fri 7/24/26	Tue 7/28/26
167		Insulation	2 wks	Wed 7/29/26	Tue 8/11/26
168		Control Wiring	4 days	Fri 7/17/26	Wed 7/22/26
169		Diffusers	3 days	Tue 9/29/26	Fri 10/2/26
170		T-stats	3 days	Wed 10/21/26	Mon 10/26/26
171		**Fire Protection**	**35 days**	**Fri 7/31/26**	**Thu 9/17/26**
172		Mains	5 days	Fri 7/31/26	Thu 8/6/26
173		Branch Piping	5 days	Fri 8/7/26	Thu 8/13/26
174		Cut In Heads	2 days	Wed 9/16/26	Thu 9/17/26
175		**Electric & Fire Alarm**	**77 days**	**Thu 7/16/26**	**Mon 11/2/26**
176		Home Runs	2 wks	Fri 7/17/26	Thu 7/30/26
177		Wall Rough in	2 wks	Thu 7/16/26	Thu 7/30/26
178		Chief Boxes	1 wk	Thu 7/30/26	Thu 8/6/26

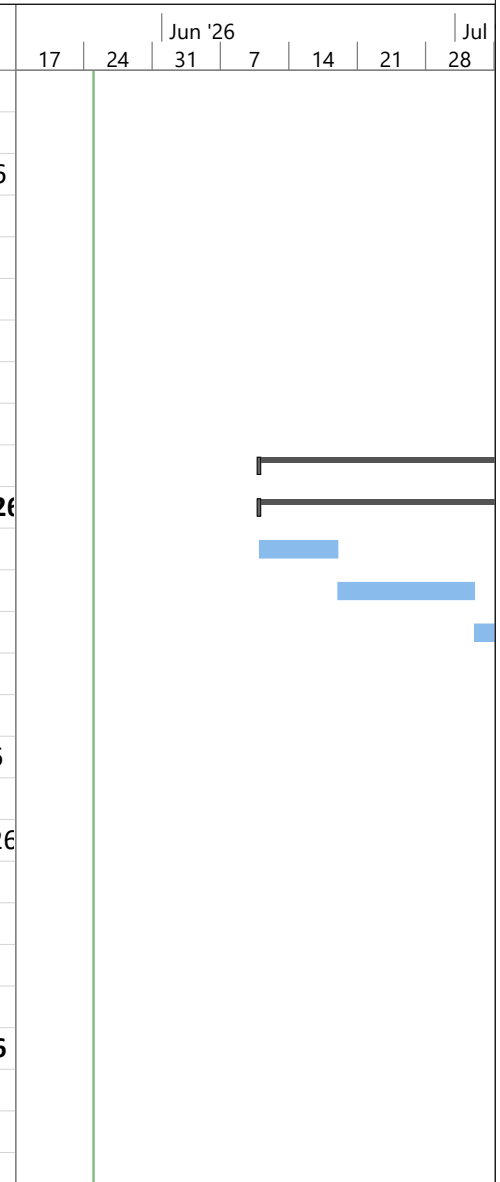


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

ID	Task Mode	Task Name	Duration	Start	Finish
179		Install Downlights	1 wk	Tue 9/8/26	Tue 9/15/26
180		Terminate Wall Devices	3 days	Wed 10/28/26	Mon 11/2/26
181		**Data**	**126.5 days**	**Thu 7/23/26**	**Fri 1/15/27**
182		Pull Cabling	3 wks	Thu 7/23/26	Thu 8/13/26
183		Wire Up Furniture	1 wk	Mon 1/11/27	Fri 1/15/27
184		**AV**	**126.5 days**	**Thu 7/23/26**	**Fri 1/15/27**
185		Pull Cabling	10 days	Thu 7/23/26	Thu 8/6/26
186		Box Walk Prior To Closing Walls	3 days	Thu 8/6/26	Tue 8/11/26
187		Mount Displays	1 wk	Mon 1/4/27	Fri 1/8/27
188		Table Devices	1 wk	Mon 1/4/27	Fri 1/8/27
189		Commissioning	1 wk	Mon 1/11/27	Fri 1/15/27
190		**Drywall and Ceilings**	**109.5 days**	**Thu 6/11/26**	**Wed 11/11/26**
191		Layout	5 days	Thu 6/11/26	Wed 6/17/26
192		Architect Approval	3 days	Thu 6/18/26	Mon 6/22/26
193		Top and Bottom Track	1.5 wks	Tue 6/23/26	Thu 7/2/26
194		Wall Framing	2 wks	Thu 7/2/26	Thu 7/16/26
195		Insulation & Drywall	3 wks	Fri 7/17/26	Fri 8/7/26
196		Taping	3 wks	Fri 8/7/26	Fri 8/28/26
197		Black Iron	1 wk	Fri 8/28/26	Fri 9/4/26
198		Ceiling Framing	1.5 wks	Fri 9/4/26	Tue 9/15/26
199		Drywall Ceilings	1.5 wks	Fri 9/18/26	Tue 9/29/26
200		Taping Ceilings	1 wk	Fri 10/2/26	Fri 10/9/26
201		Grid and Cut Tiles	1 wk	Fri 10/2/26	Fri 10/9/26
202		Specialty Ceilings	3 wks	Wed 10/21/26	Wed 11/11/26
203		**Flooring**	**3 days**	**Wed 10/14/26**	**Mon 10/19/26**
204		Install Carpet Tile	3 days	Wed 10/14/26	Mon 10/19/26
205		**Fabric Panels**	**15 days**	**Wed 10/21/26**	**Wed 11/11/26**

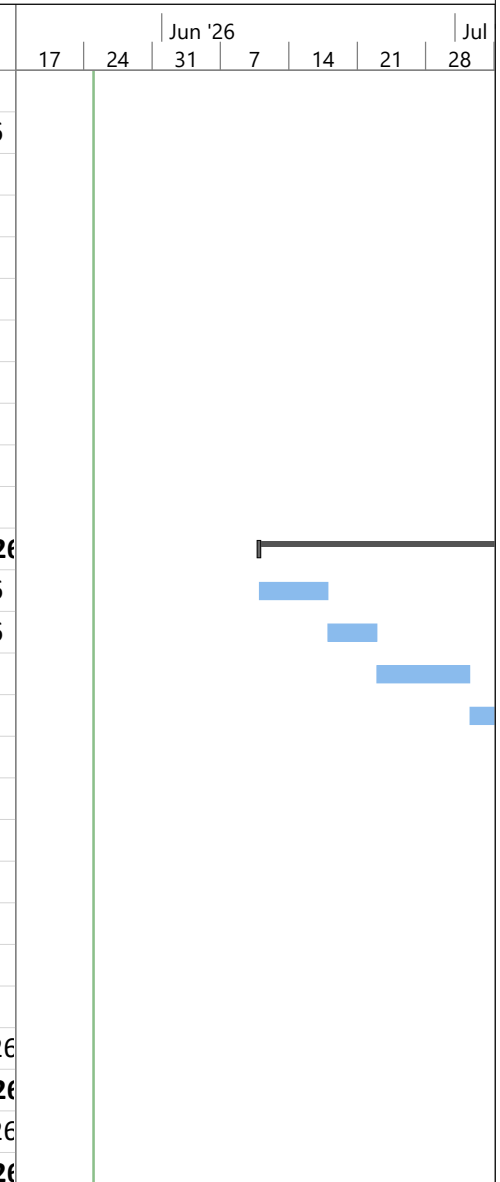


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

ID	Task Mode	Task Name	Duration	Start	Finish
206		Track and Insulation	1 wk	Wed 10/21/26	Wed 10/28/26
207		Fabric	2 wks	Wed 10/28/26	Wed 11/11/26
208		**Millwork**	**20 days**	**Mon 10/19/26**	**Mon 11/16/26**
209		Wellness/Mothers room cabinets	2 wks	Mon 10/19/26	Mon 11/2/26
210		Shelving and Closets	2 wks	Mon 11/2/26	Mon 11/16/26
211		**Office Fronts**	**110 days**	**Wed 7/29/26**	**Tue 12/29/26**
212		Field Dimensions	1 day	Wed 7/29/26	Wed 7/29/26
213		Deliver Fronts	1 wk	Wed 11/11/26	Tue 11/17/26
214		Installation	6 wks	Wed 11/18/26	Tue 12/29/26
215		**Millwork**	**2 days**	**Mon 10/19/26**	**Wed 10/21/26**
216		Wood Base	2 days	Mon 10/19/26	Wed 10/21/26
217		**Paint**	**55.5 days**	**Fri 10/9/26**	**Fri 12/25/26**
218		Prime Walls & Ceilings	3 days	Fri 10/9/26	Wed 10/14/26
219		1st Coat	1 wk	Wed 10/14/26	Wed 10/21/26
220		2nd Coat/Touch Ups	1 wk	Mon 12/21/26	Fri 12/25/26
221		**Café and Kitchen**	**157 days**	**Thu 6/11/26**	**Fri 1/15/27**
222		**HVAC**	**124 days**	**Thu 6/11/26**	**Tue 12/1/26**
223		Tin Sketching	4 days	Thu 6/11/26	Tue 6/16/26
224		Shop Drawing Approval	2 wks	Wed 6/17/26	Tue 6/30/26
225		Duct Work	3 wks	Wed 7/1/26	Tue 7/21/26
226		Testing	3 days	Wed 7/22/26	Fri 7/24/26
227		Insulation	3 days	Mon 7/27/26	Wed 7/29/26
228		Control Wiring	4 days	Wed 7/15/26	Mon 7/20/26
229		Diffusers	1 wk	Wed 11/25/26	Tue 12/1/26
230		T-stats	2 wks	Fri 9/18/26	Thu 10/1/26
231		**Fire Protection**	**89 days**	**Wed 7/29/26**	**Mon 11/30/26**
232		Mains	1 wk	Wed 7/29/26	Tue 8/4/26

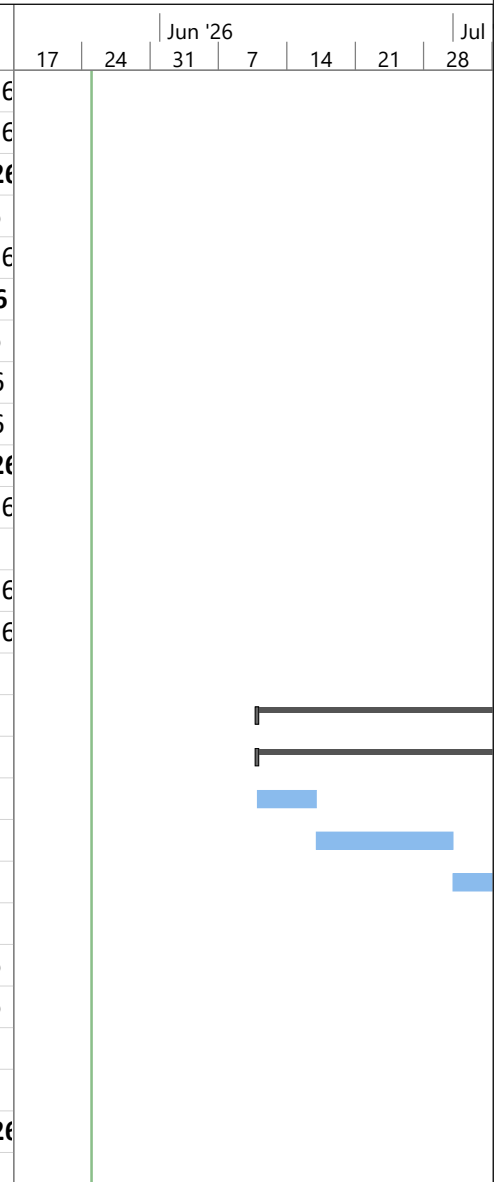


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

ID	Task Mode	Task Name	Duration	Start	Finish
233		Branch Piping	1.5 wks	Wed 8/5/26	Fri 8/14/26
234		Upright Heads	4 days	Fri 8/14/26	Thu 8/20/26
235		Cut In Heads	4 days	Wed 11/25/26	Mon 11/30/26
236		**Plumbing**	**111 days**	**Fri 7/10/26**	**Fri 12/11/26**
237		Rough in (with approved Food Service Shops	3 wks	Fri 7/10/26	Thu 7/30/26
238		Inspection	1 wk	Fri 7/31/26	Thu 8/6/26
239		Insulation	1 wk	Fri 8/7/26	Thu 8/13/26
240		Grease Trap and inspection	2 wks	Thu 10/1/26	Wed 10/14/26
241		Food Service Plumbing Hook ups	2 wks	Mon 11/30/26	Fri 12/11/26
242		**Electric & Fire Alarm**	**103 days**	**Fri 7/10/26**	**Tue 12/1/26**
243		Home Runs	2 wks	Wed 7/15/26	Tue 7/28/26
244		Wall Rough in	1.5 wks	Fri 7/10/26	Tue 7/21/26
245		Grid Lighting	1 wk	Wed 11/25/26	Tue 12/1/26
246		Open Area Lighting	3 wks	Thu 9/3/26	Wed 9/23/26
247		**Security**	**90 days**	**Wed 7/29/26**	**Tue 12/1/26**
248		Pull Cabling	2 wks	Wed 7/29/26	Tue 8/11/26
249		Cameras/Card Readers	1 wk	Wed 11/25/26	Tue 12/1/26
250		**AV**	**123 days**	**Wed 7/29/26**	**Fri 1/15/27**
251		Pull Cabling	2 wks	Wed 7/29/26	Tue 8/11/26
252		Displays	4 days	Mon 1/4/27	Thu 1/7/27
253		Commissioning	1 wk	Mon 1/11/27	Fri 1/15/27
254		**Drywall and Ceilings**	**119 days**	**Thu 6/11/26**	**Tue 11/24/26**
255		Layout	5 days	Thu 6/11/26	Wed 6/17/26
256		Architect Approval	2 days	Thu 6/18/26	Fri 6/19/26
257		Wall Framing	1.5 wks	Mon 6/22/26	Wed 7/1/26
258		Insulation & Drywall	2 wks	Fri 8/14/26	Thu 8/27/26
259		Taping	1 wk	Fri 8/28/26	Thu 9/3/26

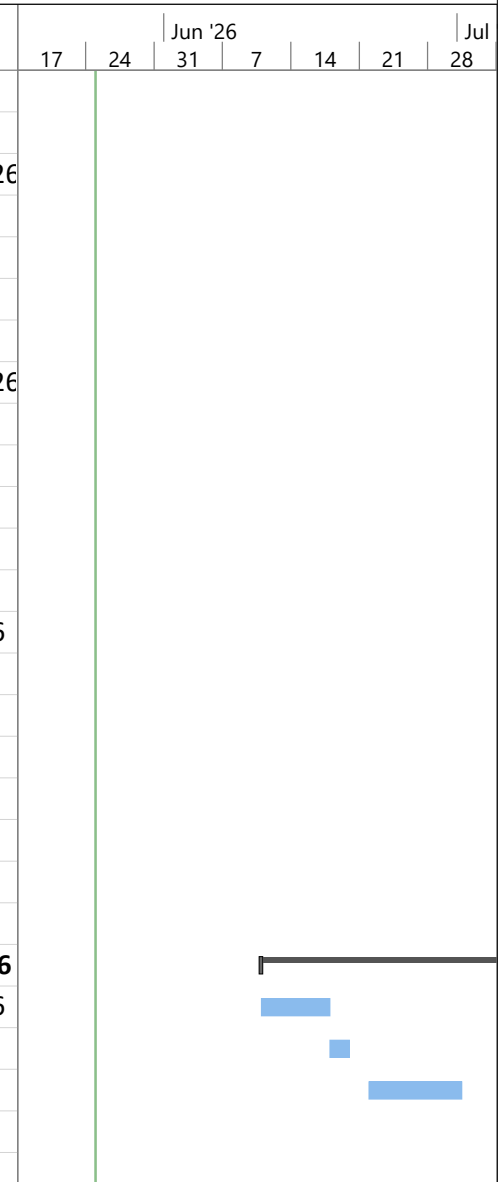


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

ID	Task Mode	Task Name	Duration	Start	Finish
260		Black Iron	1 wk	Fri 9/4/26	Thu 9/10/26
261		HM Doors and Jambs	4 days	Thu 10/1/26	Tue 10/6/26
262		Wall Paneling	1 wk	Wed 11/11/26	Tue 11/17/26
263		Grid and Tiles	1 wk	Wed 11/18/26	Tue 11/24/26
264		**Flooring**	**19 days**	**Thu 10/15/26**	**Tue 11/10/26**
265		Waterproofing	2 wks	Thu 10/15/26	Wed 10/28/26
266		Flood Tests	1 wk	Thu 10/29/26	Wed 11/4/26
267		Install SVT Flooring	4 days	Thu 11/5/26	Tue 11/10/26
268		**K13**	**74.5 days**	**Fri 8/14/26**	**Thu 11/26/26**
269		Protecion after MEP	1 wk	Fri 8/14/26	Fri 8/21/26
270		Prep and Spray Ceilings	4 wks	Fri 8/21/26	Fri 9/18/26
271		Touch Ups Post Construction	1 wk	Fri 11/20/26	Thu 11/26/26
272		**Steel**	**45 days**	**Wed 6/24/26**	**Tue 8/25/26**
273		Shops and Approval (Post Food Service Shop	3 wks	Wed 6/24/26	Tue 7/14/26
274		Fabrication	2 wks	Wed 7/15/26	Tue 7/28/26
275		Grease Trap Steel Ceiling of 29	1 wk	Wed 8/5/26	Tue 8/11/26
276		Inspection and Sign Offs	2 wks	Wed 8/12/26	Tue 8/25/26
277		**Food Service**	**130.5 days**	**Fri 6/12/26**	**Fri 12/11/26**
278		Shops, Approval, Layout in the Field	4 wks	Fri 6/12/26	Thu 7/9/26
279		Deliver and Install Equipment	2.5 wks	Wed 11/25/26	Fri 12/11/26
280		**Paint**	**81 days**	**Fri 9/4/26**	**Fri 12/25/26**
281		Prime Walls, Soffits, Ceiling Bands	1 wk	Fri 9/4/26	Thu 9/10/26
282		1st Coat	1 wk	Fri 9/11/26	Thu 9/17/26
283		2nd Coat/Touch Ups	1 wk	Mon 12/21/26	Fri 12/25/26
284		**IDF Rooms**	**143 days**	**Thu 6/11/26**	**Mon 12/28/26**
285		**IDF Rooms Ready**	**1 day**	**Fri 12/4/26**	**Fri 12/4/26**
286		**Network Live**	**1 day**	**Mon 12/28/26**	**Mon 12/28/26**

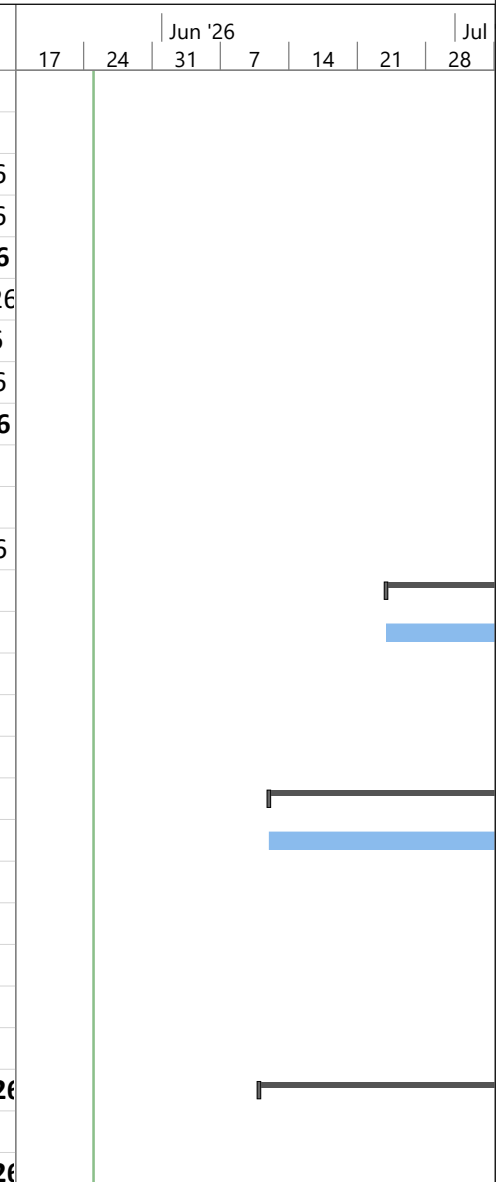


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

ID	Task Mode	Task Name	Duration	Start	Finish
287		**HVAC**	**112.5 days**	**Thu 6/11/26**	**Mon 11/16/26**
288		CRAC unit submittal, approval, lead time	14 wks	Thu 6/11/26	Wed 9/16/26
289		Condenser Water Piping	2 wks	Wed 7/22/26	Tue 8/4/26
290		Condenser Water Trim	2 wks	Thu 9/17/26	Wed 9/30/26
291		Hydro Test	1.5 wks	Thu 10/1/26	Mon 10/12/26
292		Chemical Cleaning	1 wk	Mon 10/12/26	Mon 10/19/26
293		Start ups	2 wks	Mon 10/19/26	Mon 11/2/26
294		Commissioning	2 wks	Mon 11/2/26	Mon 11/16/26
295		**Fire Protection**	**3 days**	**Wed 8/26/26**	**Fri 8/28/26**
296		Cut In Heads	3 days	Wed 8/26/26	Fri 8/28/26
297		**Electric & Fire Alarm**	**71 days**	**Fri 7/10/26**	**Fri 10/16/26**
298		In Wall Rough in	3 wks	Fri 7/10/26	Thu 7/30/26
299		Sleeves	1 wk	Fri 7/17/26	Thu 7/23/26
300		Ceiling Infrastructure	1 wk	Fri 8/14/26	Thu 8/20/26
301		Power to Security Panels	1 wk	Thu 9/24/26	Wed 9/30/26
302		Power to CRAC units	1 wk	Thu 10/1/26	Wed 10/7/26
303		Devices	3 days	Wed 10/14/26	Fri 10/16/26
304		Install Light Fixtures	1 wk	Thu 10/1/26	Wed 10/7/26
305		**Data**	**42.5 days**	**Fri 7/24/26**	**Tue 9/22/26**
306		Cabling Home Runs	3 wks	Fri 7/24/26	Fri 8/14/26
307		Install Ladder Racks	3 days	Thu 9/3/26	Mon 9/7/26
308		Dress Ladder Racks and Cabling	1 wk	Tue 9/8/26	Mon 9/14/26
309		Floor Racks	4 days	Thu 9/17/26	Tue 9/22/26
310		**Security**	**43.5 days**	**Fri 7/24/26**	**Wed 9/23/26**
311		Pull Cabling	5 days	Fri 7/24/26	Fri 7/31/26
312		Install Security Panels	2 wks	Thu 9/10/26	Wed 9/23/26
313		**AV**	**43.5 days**	**Fri 7/24/26**	**Wed 9/23/26**

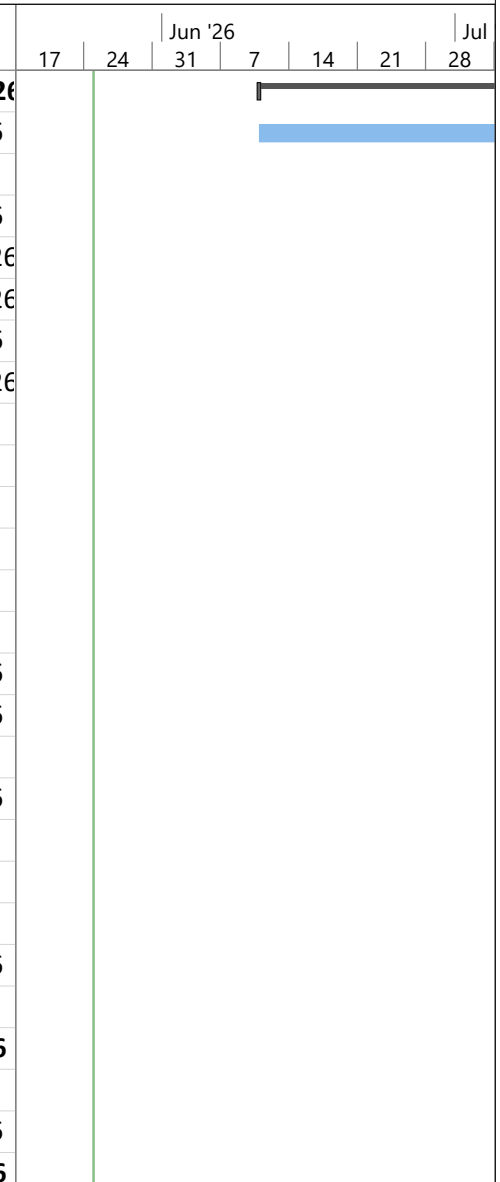


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26


ID	Task Mode	Task Name	Duration	Start	Finish
314		Pull Cabling	10 days	Fri 7/24/26	Fri 8/7/26
315		Deliver AV Racks	1 day	Wed 9/23/26	Wed 9/23/26
316		**Drywall and Ceilings**	**85 days**	**Thu 6/11/26**	**Wed 10/7/26**
317		Layout	2 wks	Thu 6/11/26	Wed 6/24/26
318		Architect Approval	2 days	Thu 6/25/26	Fri 6/26/26
319		Top and Bottom Track	4 days	Mon 6/29/26	Thu 7/2/26
320		Wall Framing	1 wk	Fri 7/3/26	Thu 7/9/26
321		Insulation & Drywall	2 wks	Fri 7/31/26	Thu 8/13/26
322		Taping	2 wks	Fri 8/14/26	Thu 8/27/26
323		Plywood	4 days	Fri 8/28/26	Wed 9/2/26
324		HM Door Jambs	5 days	Thu 9/17/26	Wed 9/23/26
325		Door and Hardware	5 days	Thu 10/1/26	Wed 10/7/26
326		**Concrete**	**3 days**	**Fri 8/21/26**	**Tue 8/25/26**
327		Fire Proofing Ceiling	3 days	Fri 8/21/26	Tue 8/25/26
328		**Flooring**	**26 days**	**Thu 9/10/26**	**Thu 10/15/26**
329		Install SDT Flooring	1 wk	Thu 9/10/26	Wed 9/16/26
330		Install Base and Transitions	2 days	Wed 10/14/26	Thu 10/15/26
331		**Paint**	**86 days**	**Wed 8/26/26**	**Wed 12/23/26**
332		Spray Ceilings	1 wk	Wed 8/26/26	Tue 9/1/26
333		Prime and Coat Walls/Plywood	1 wk	Thu 9/3/26	Wed 9/9/26
334		Paint Doors and Jambs	4 days	Thu 10/8/26	Tue 10/13/26
335		Final Touch ups	3 days	Mon 12/21/26	Wed 12/23/26

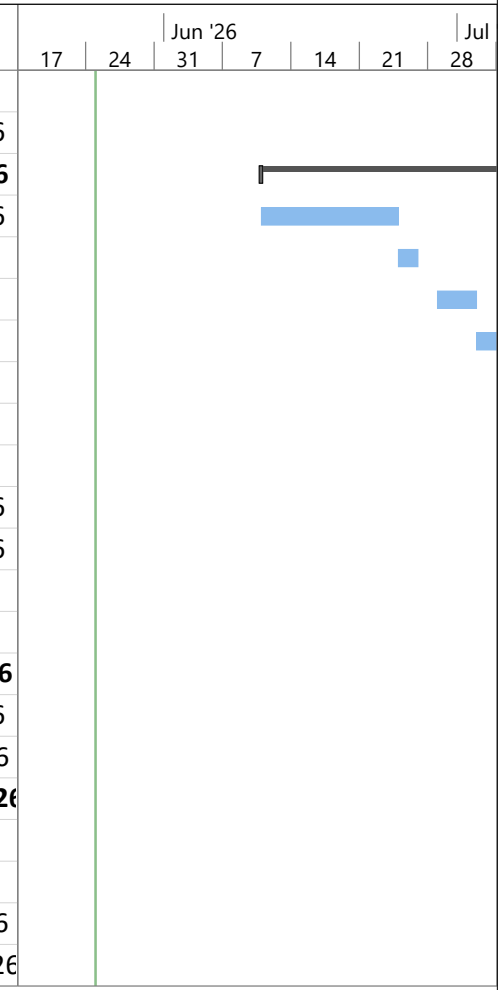


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

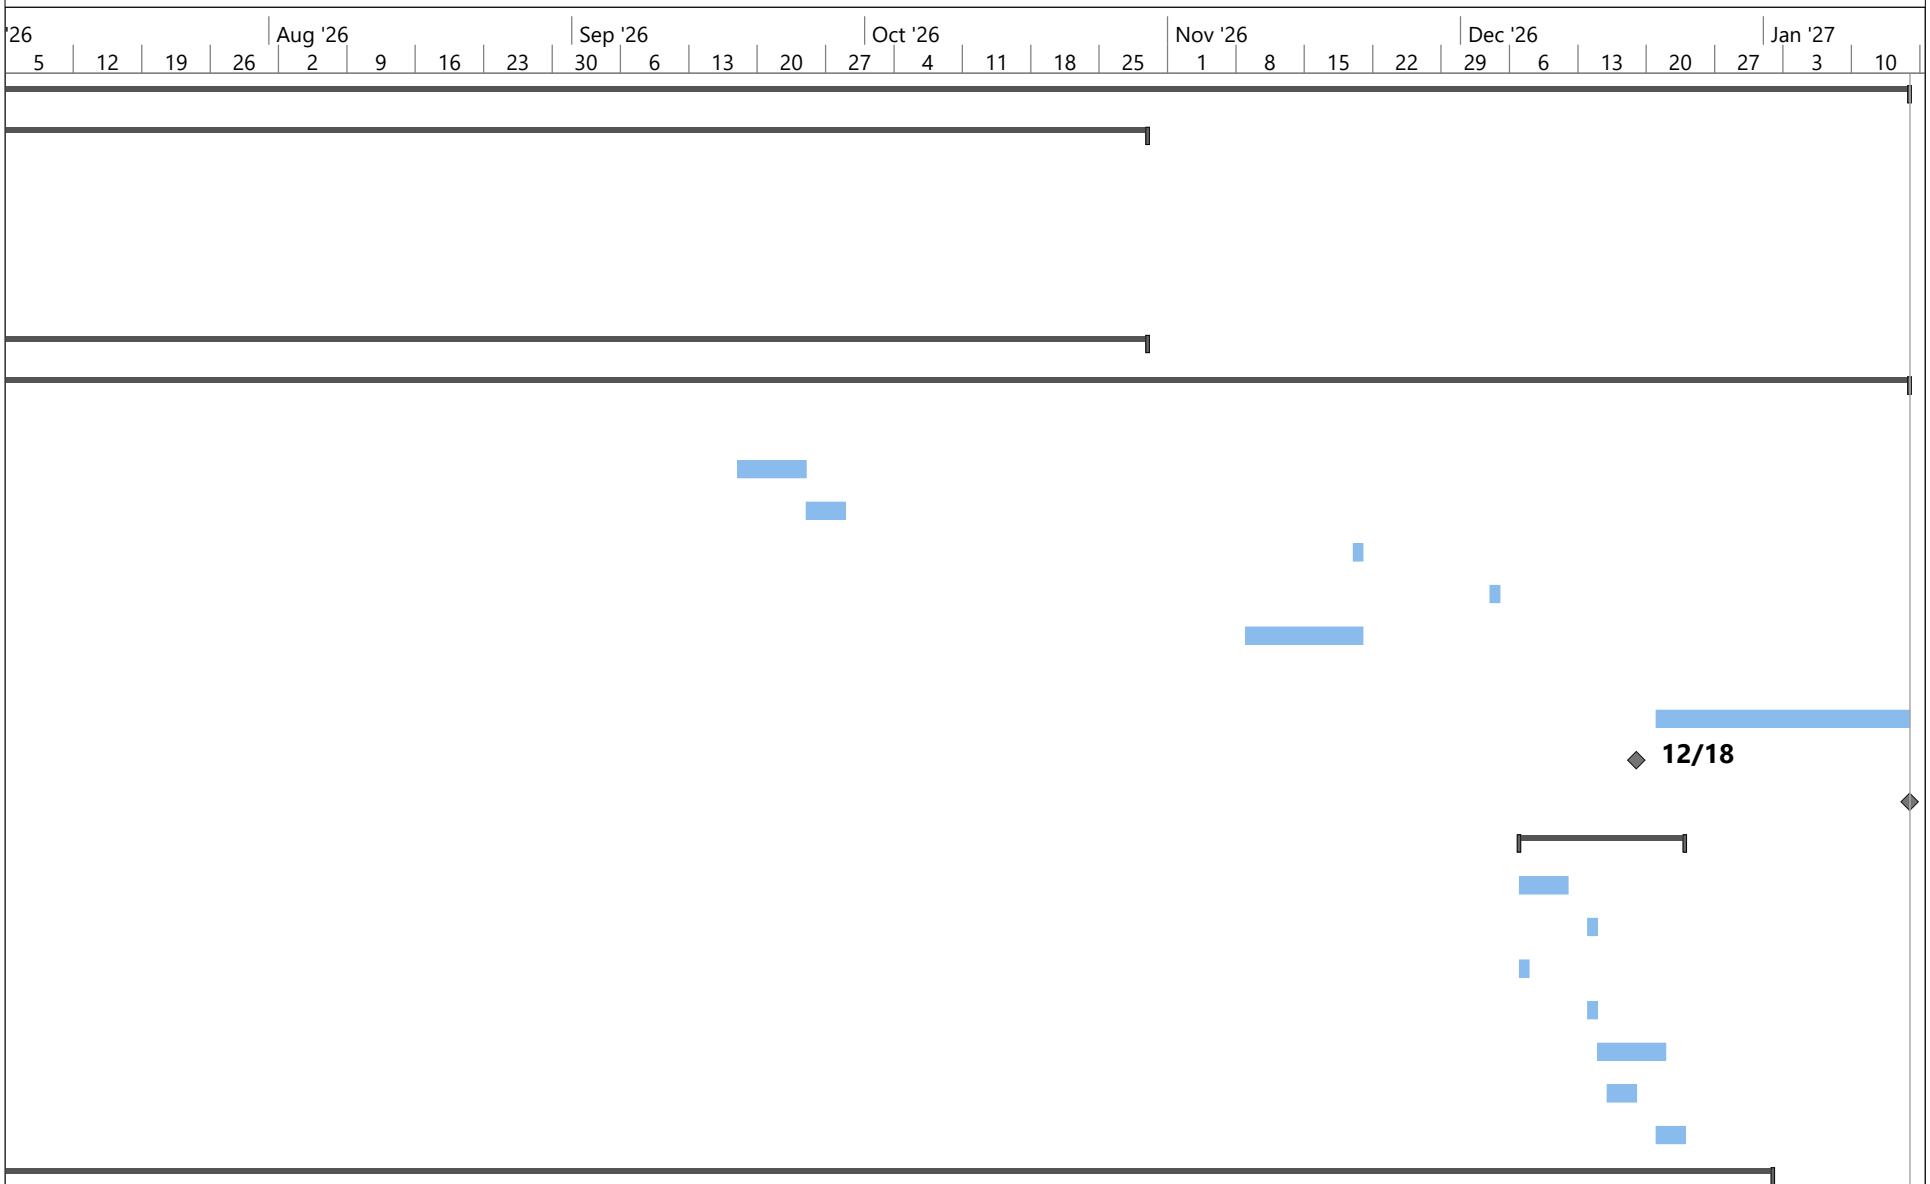


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

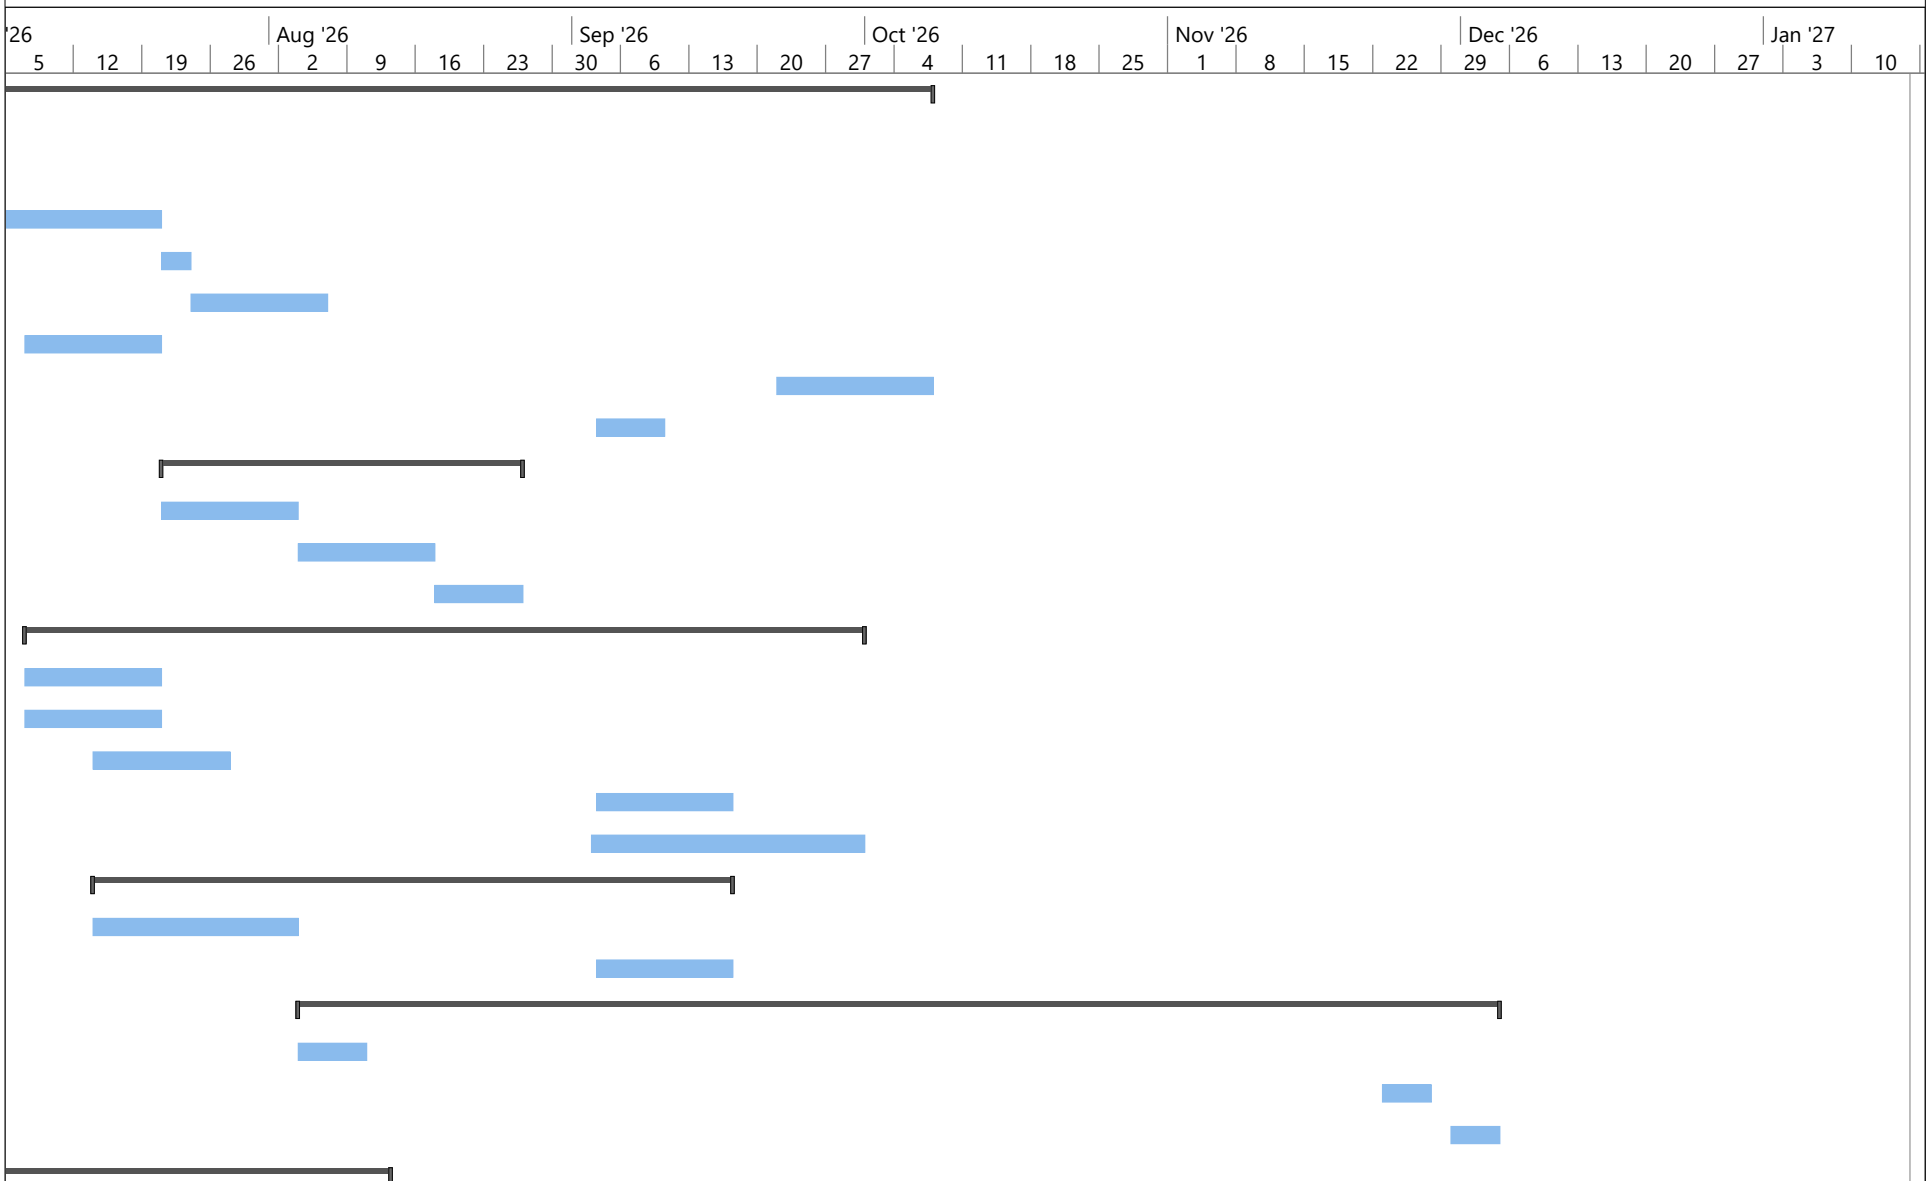


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

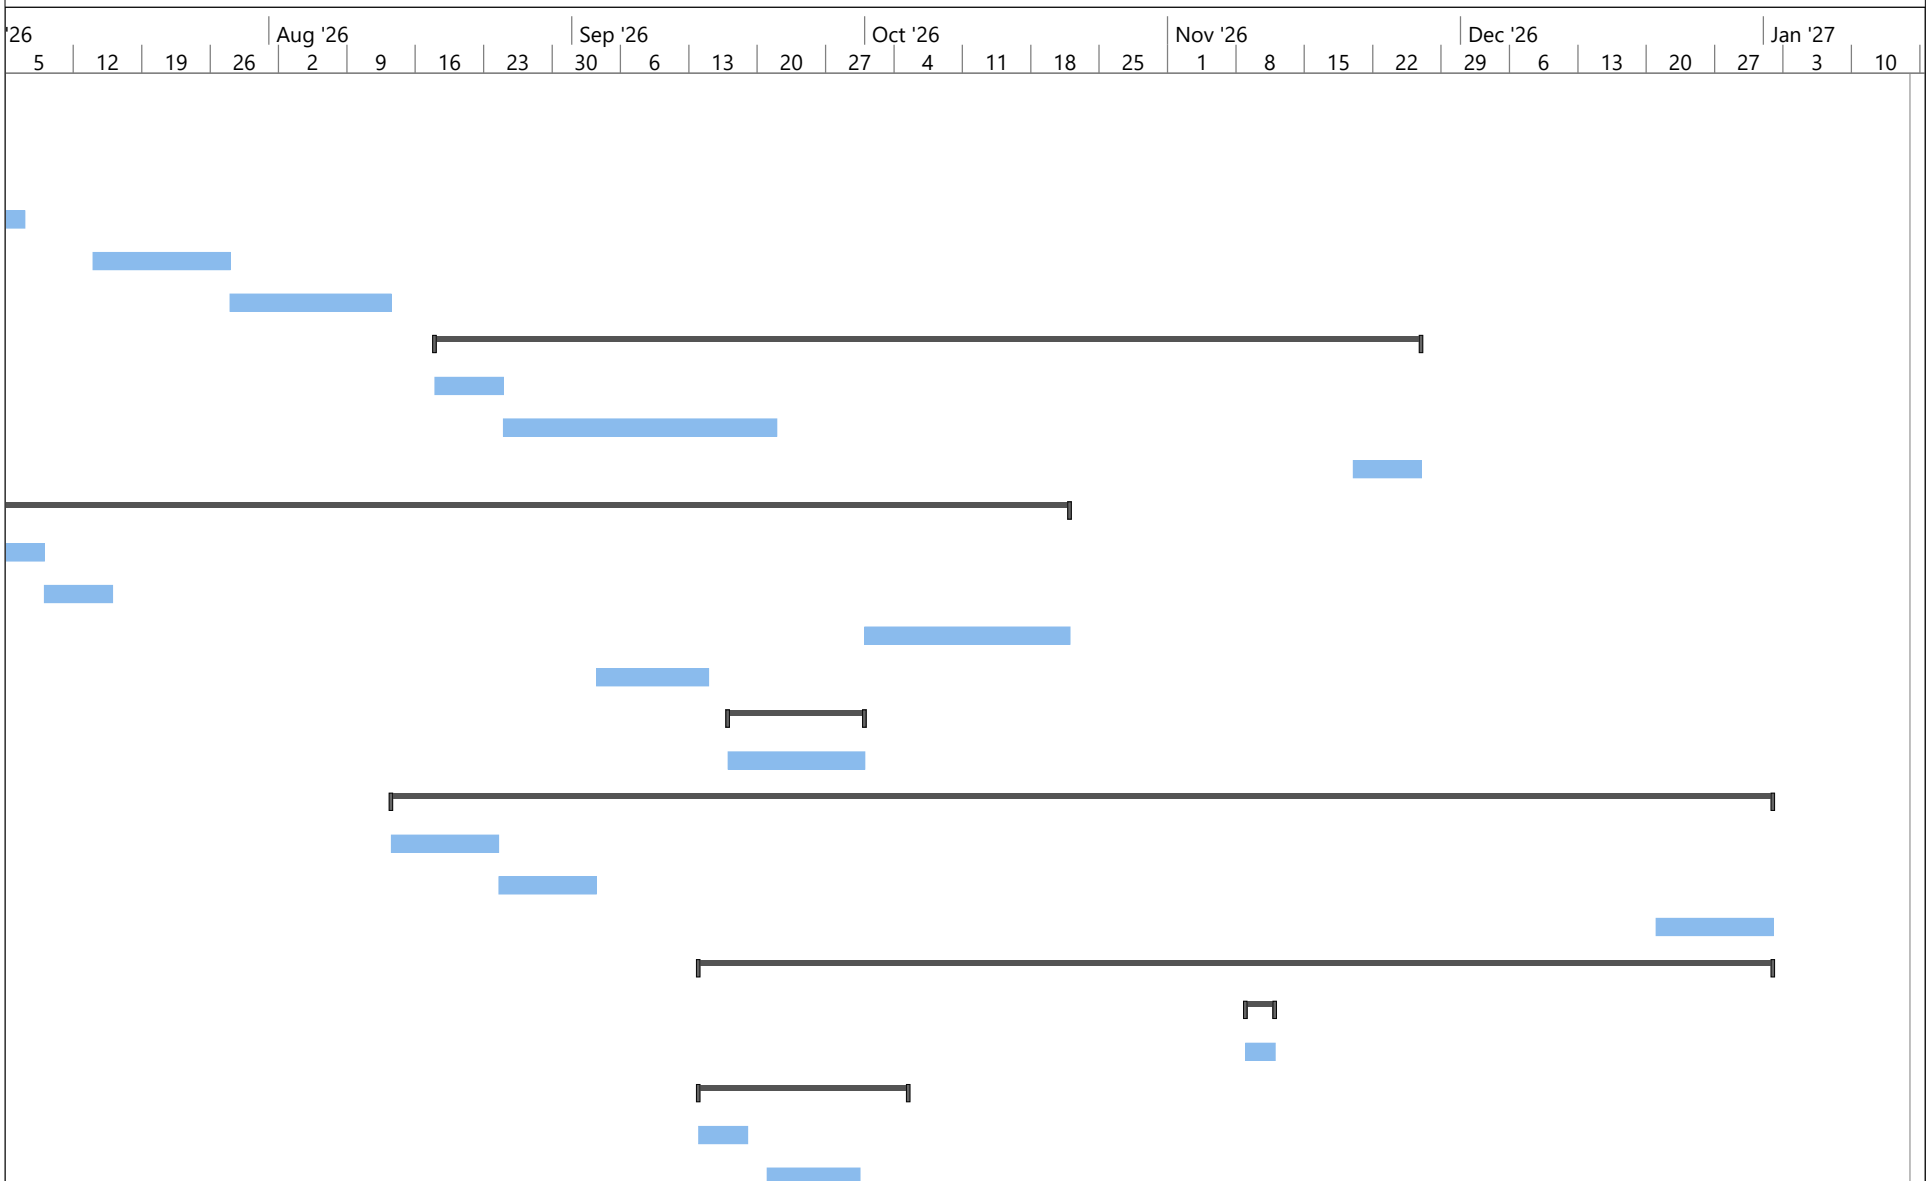


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

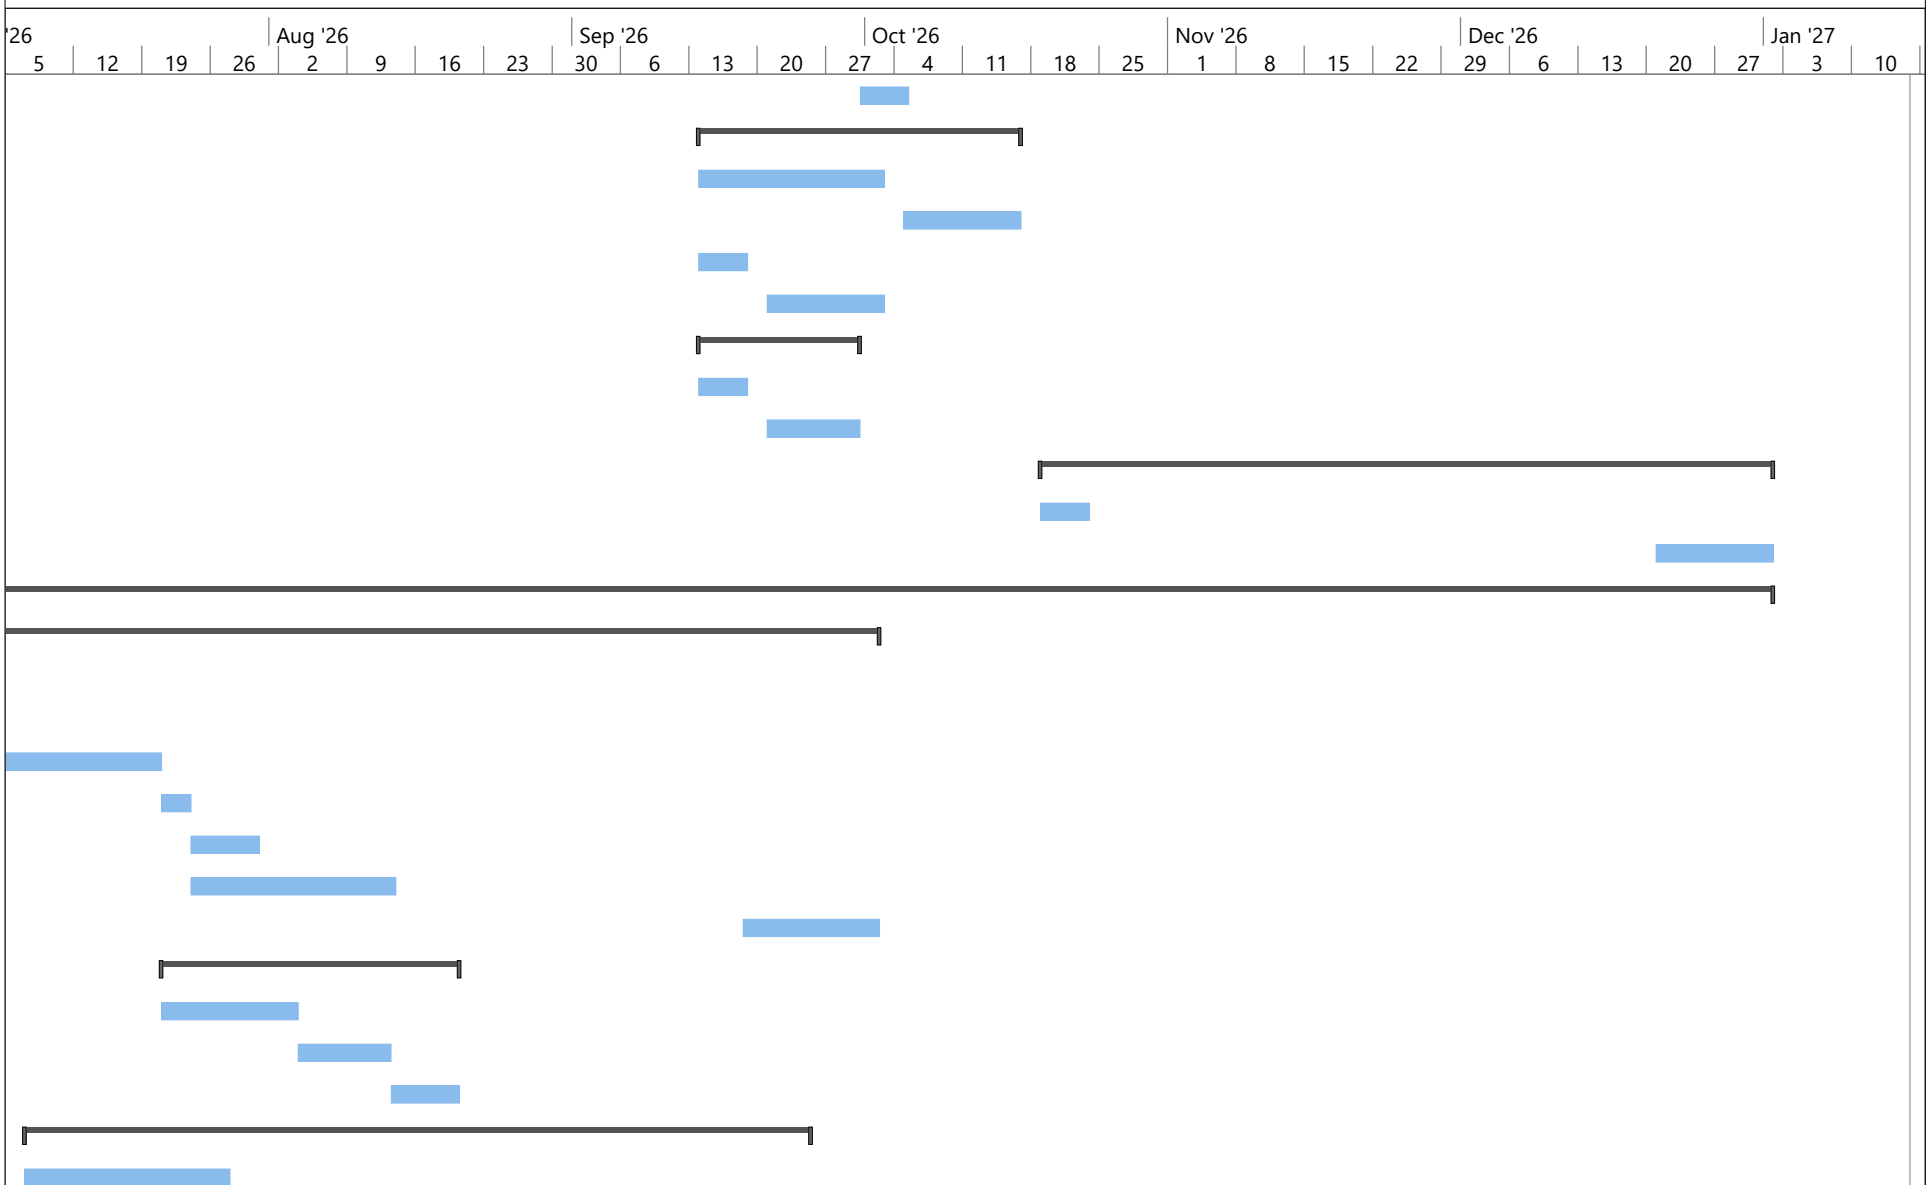


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

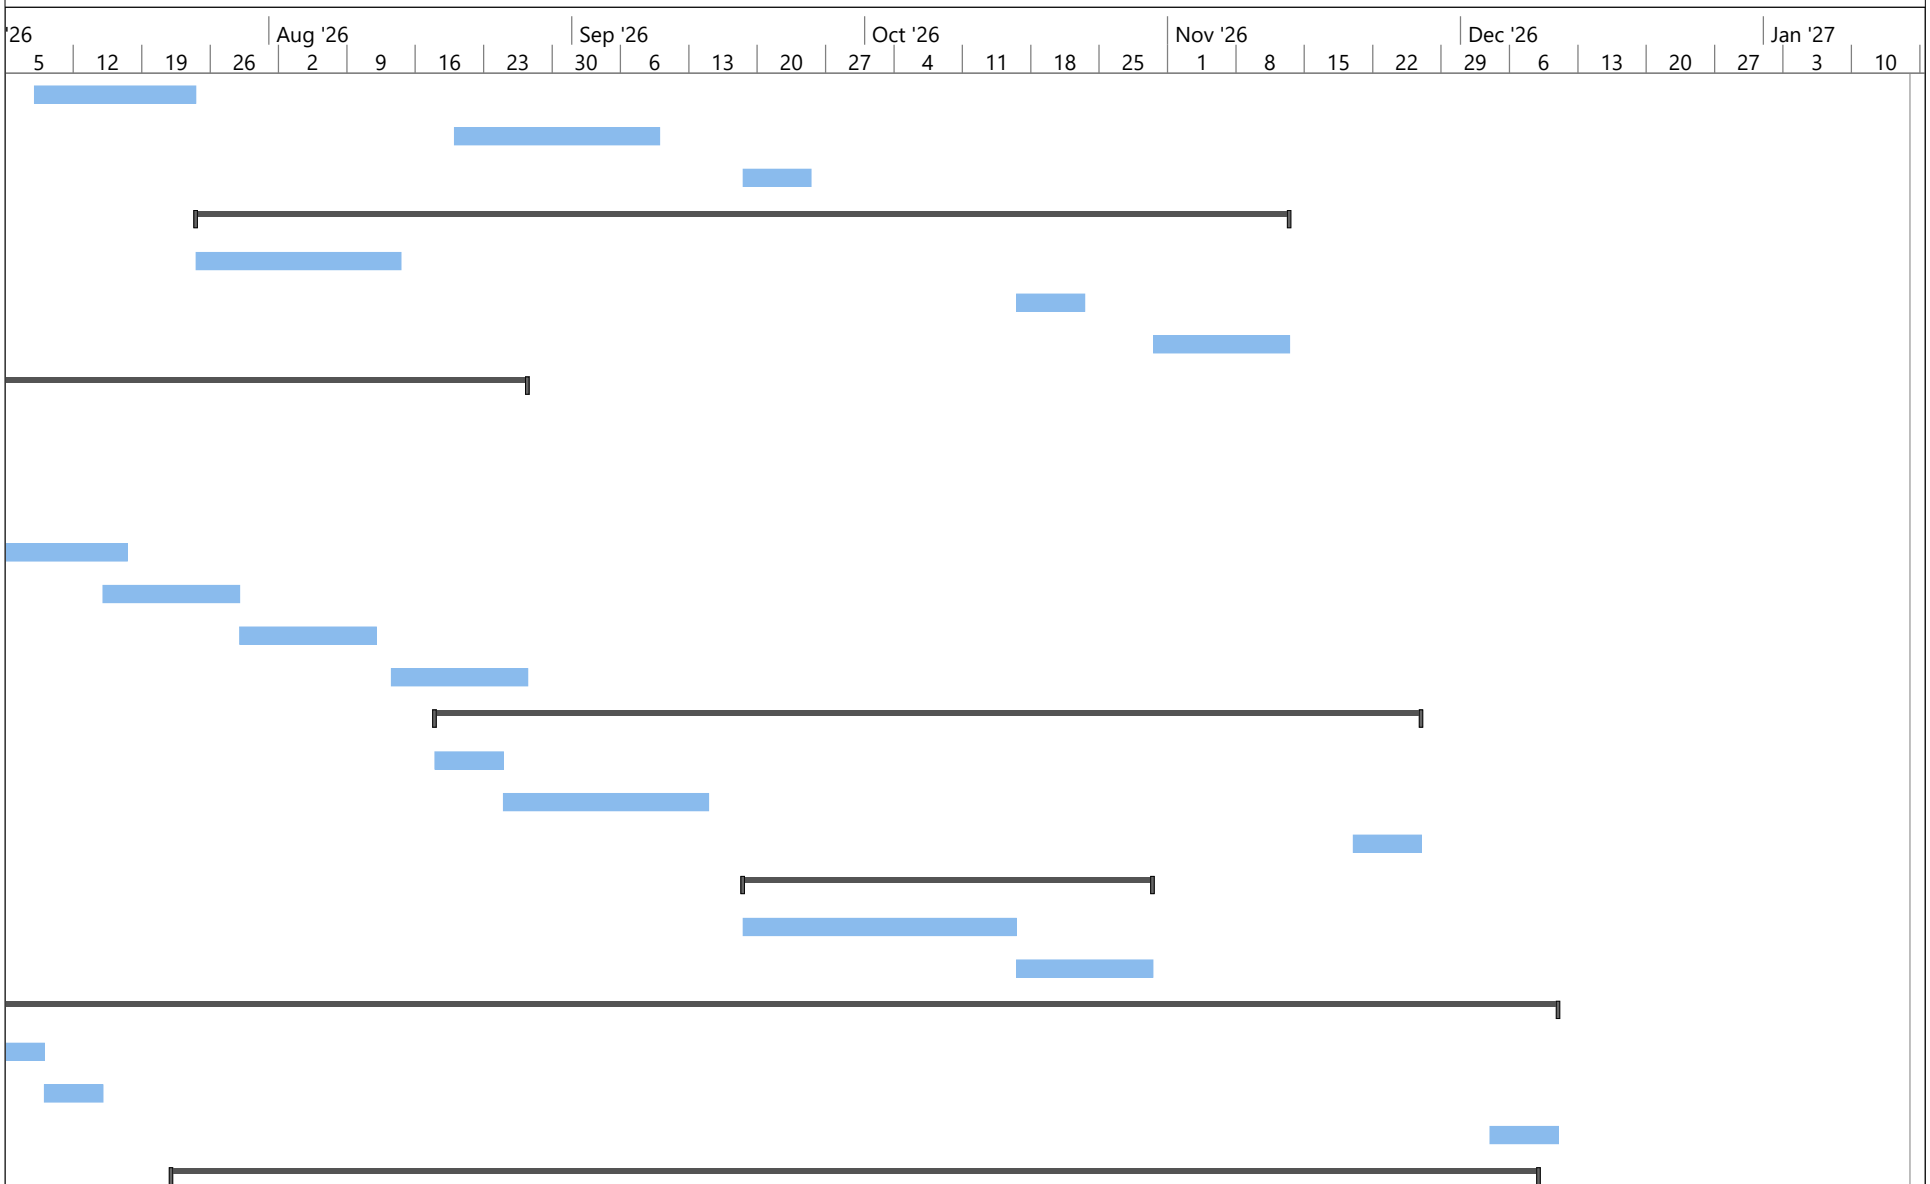


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

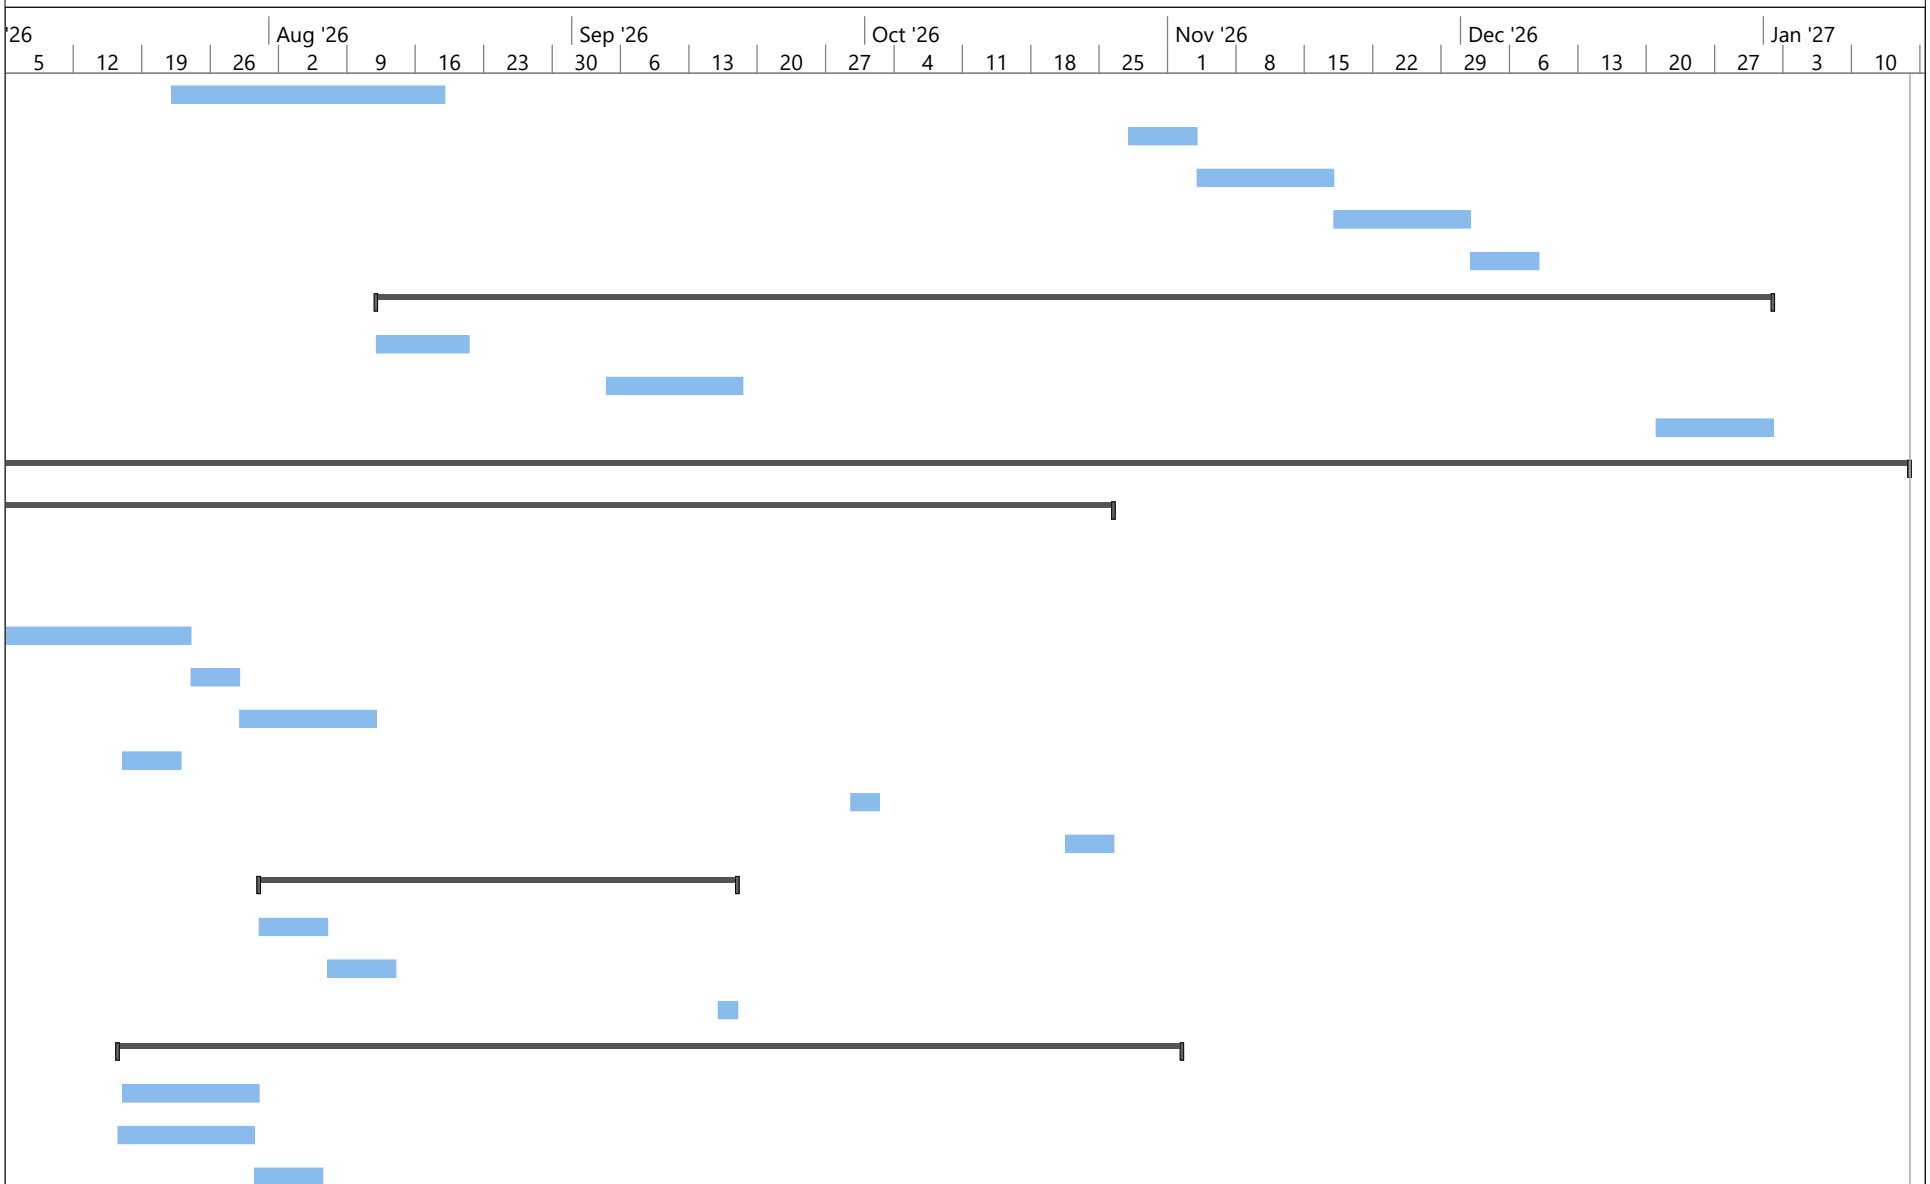


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

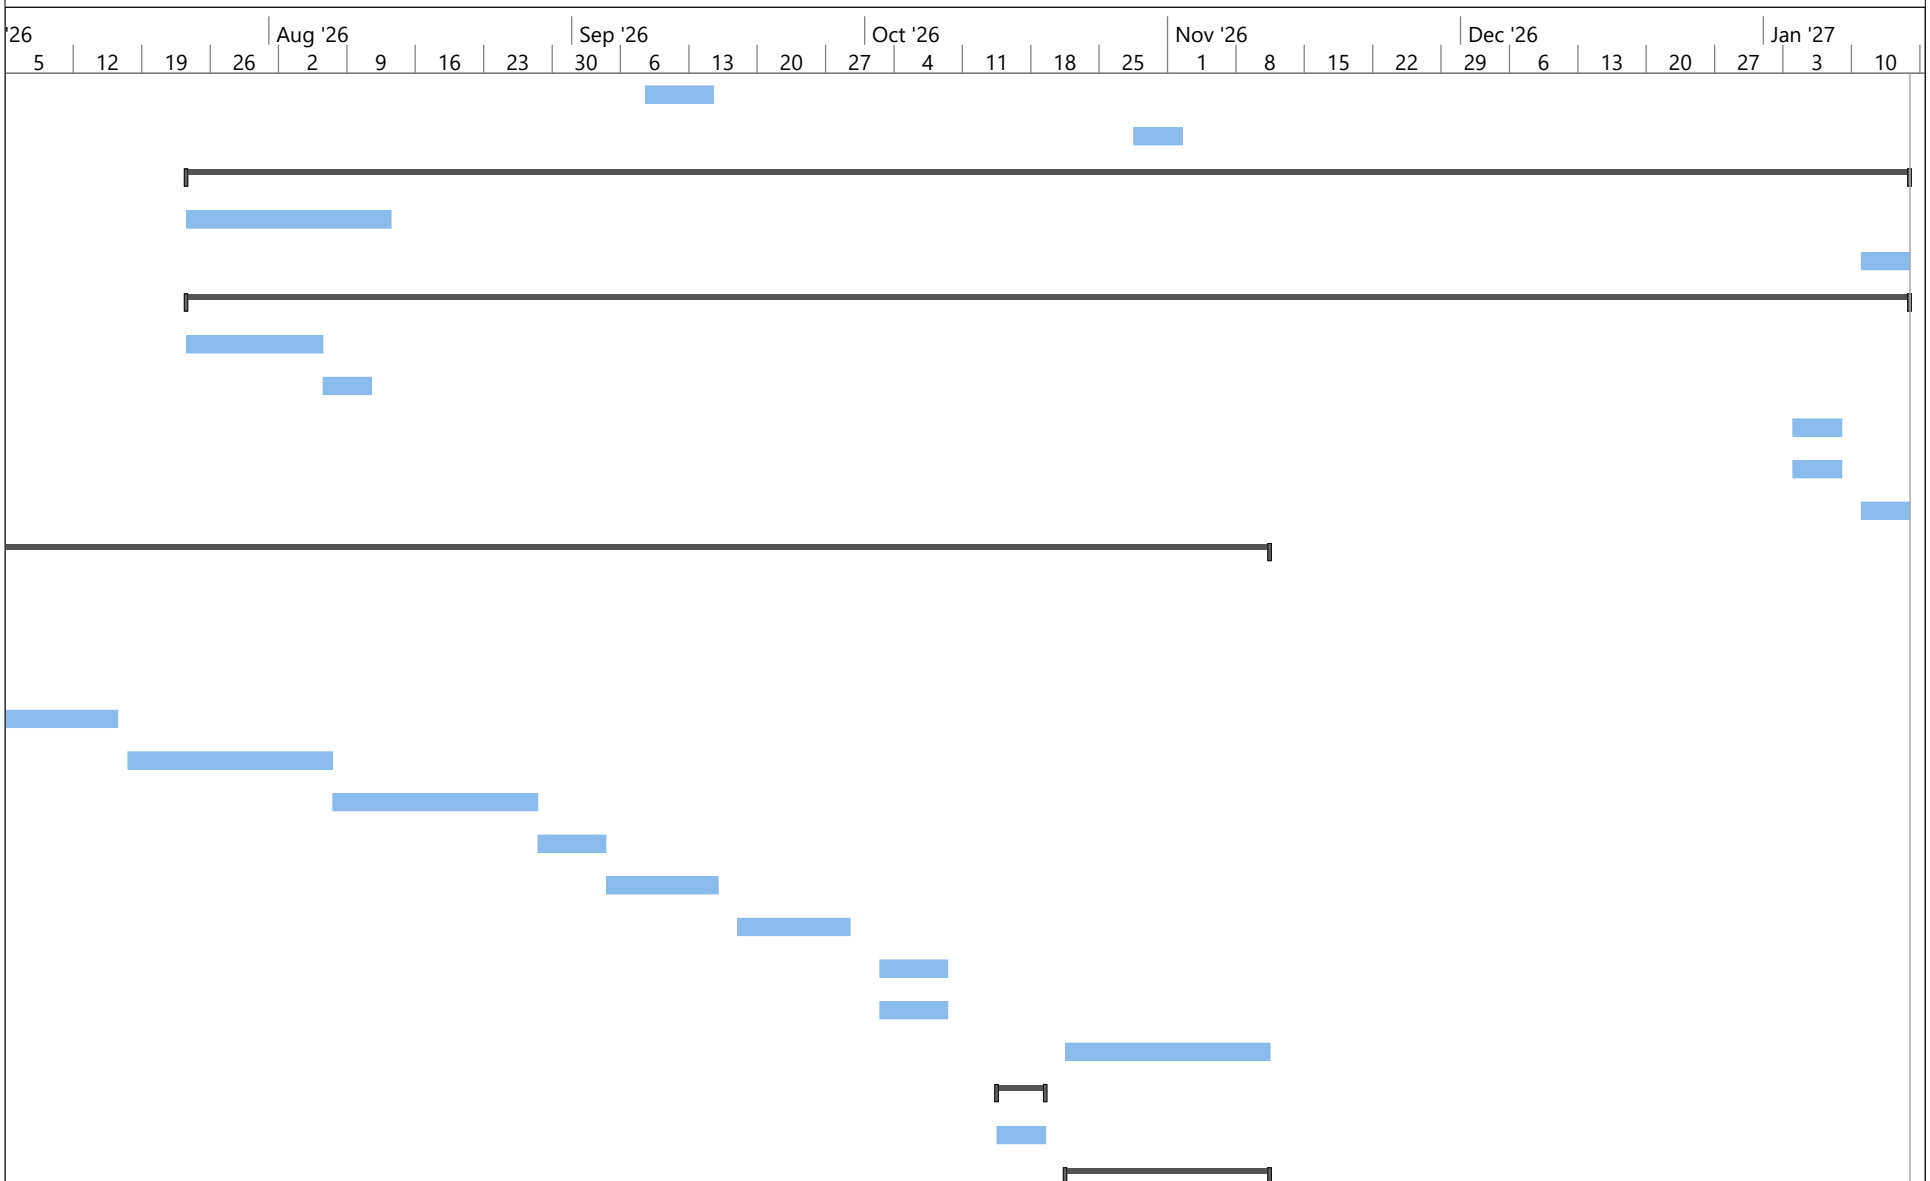


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

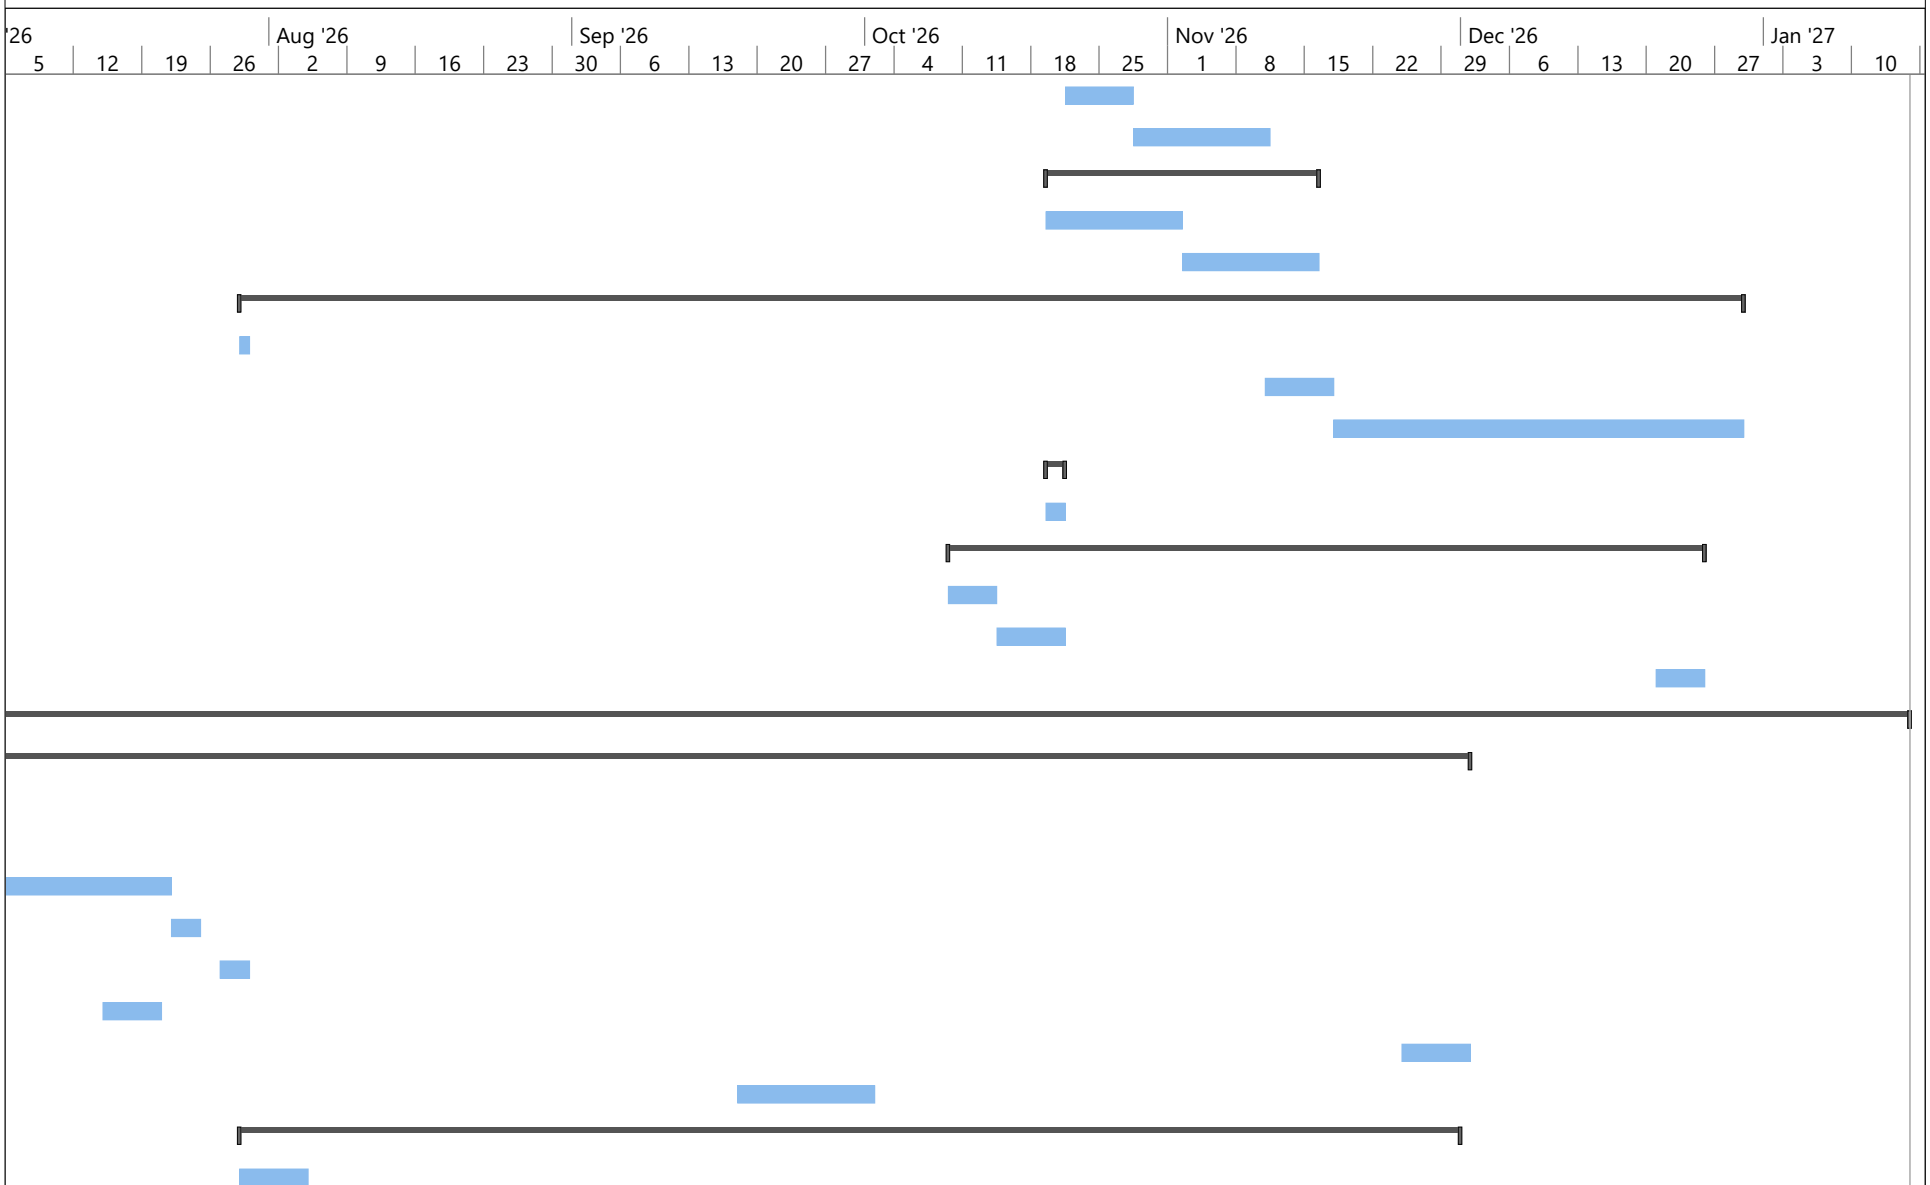


Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

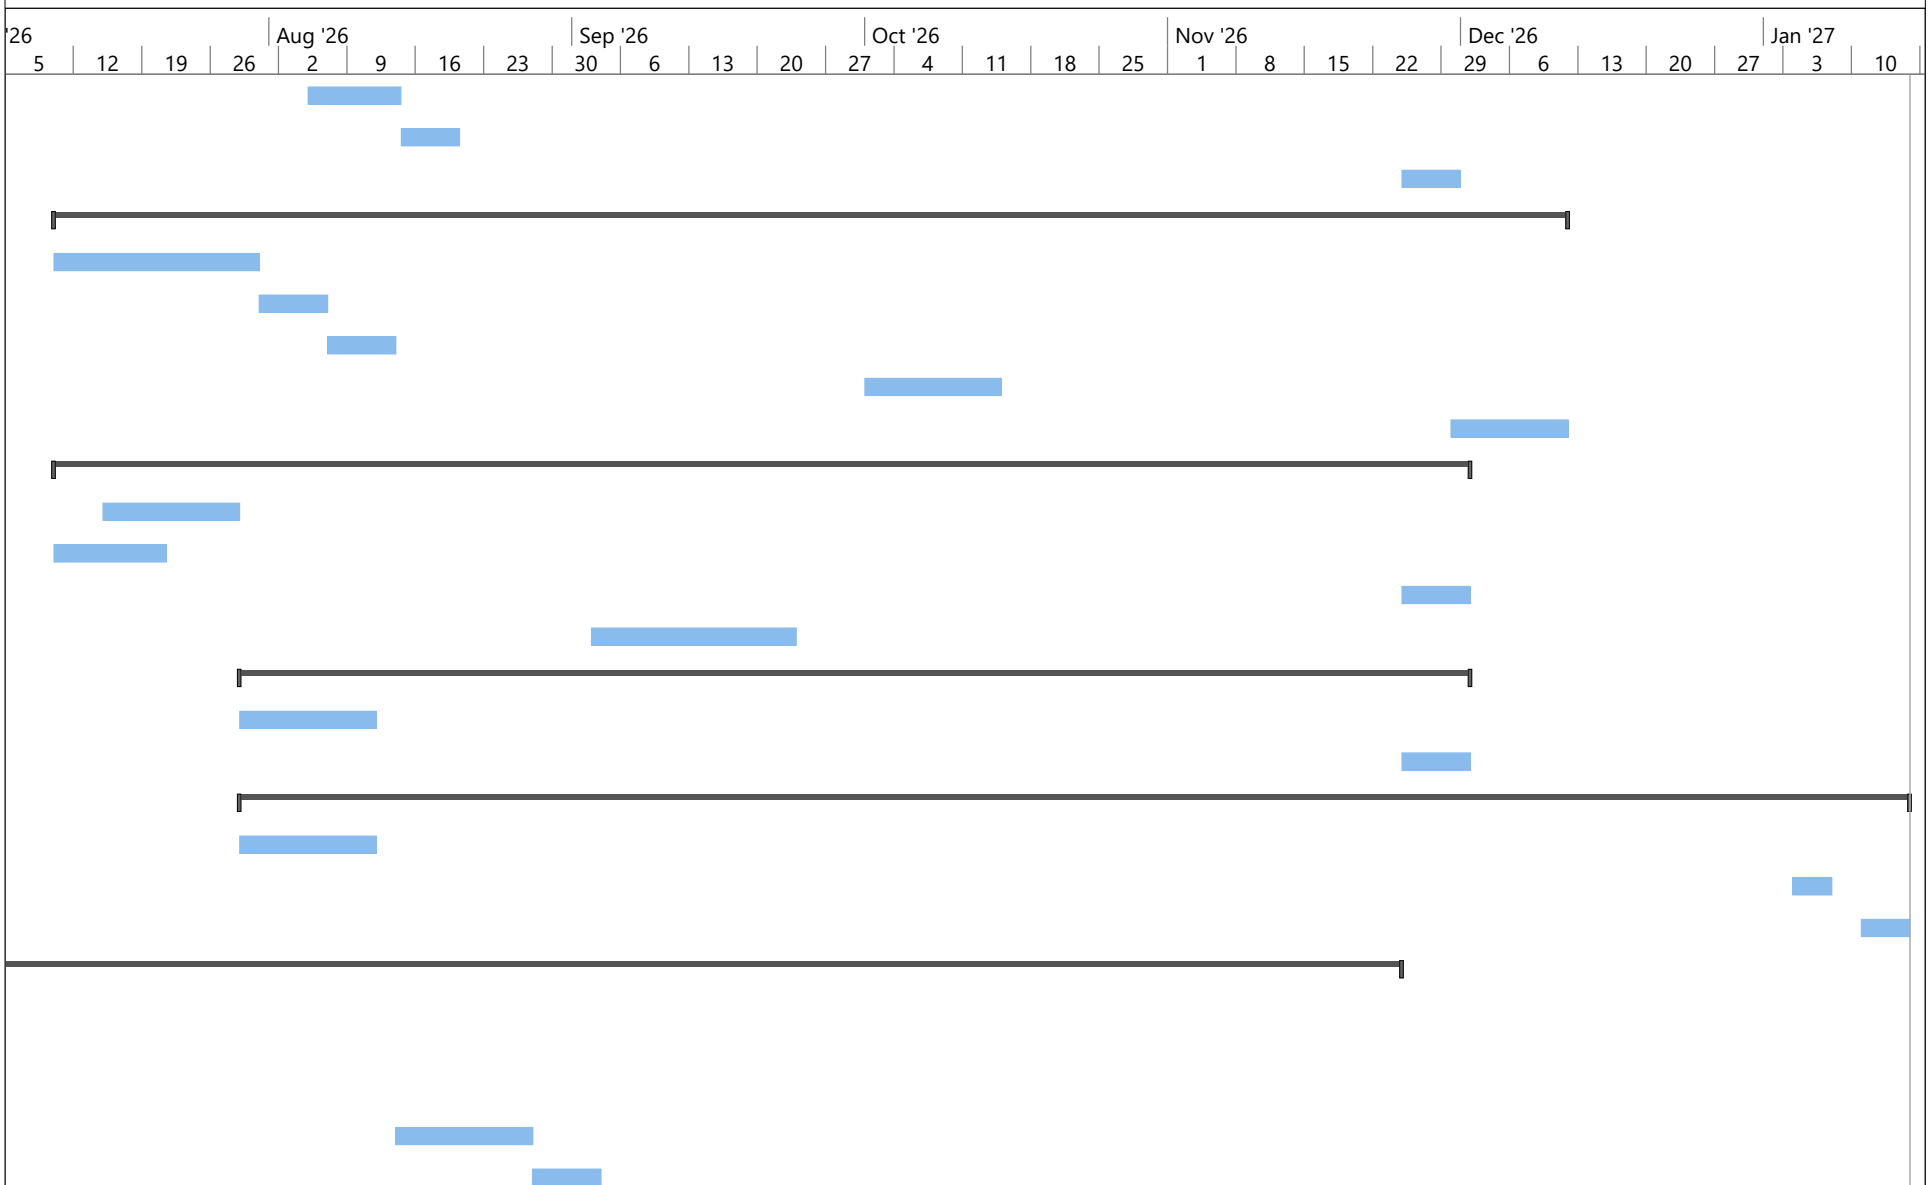

Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

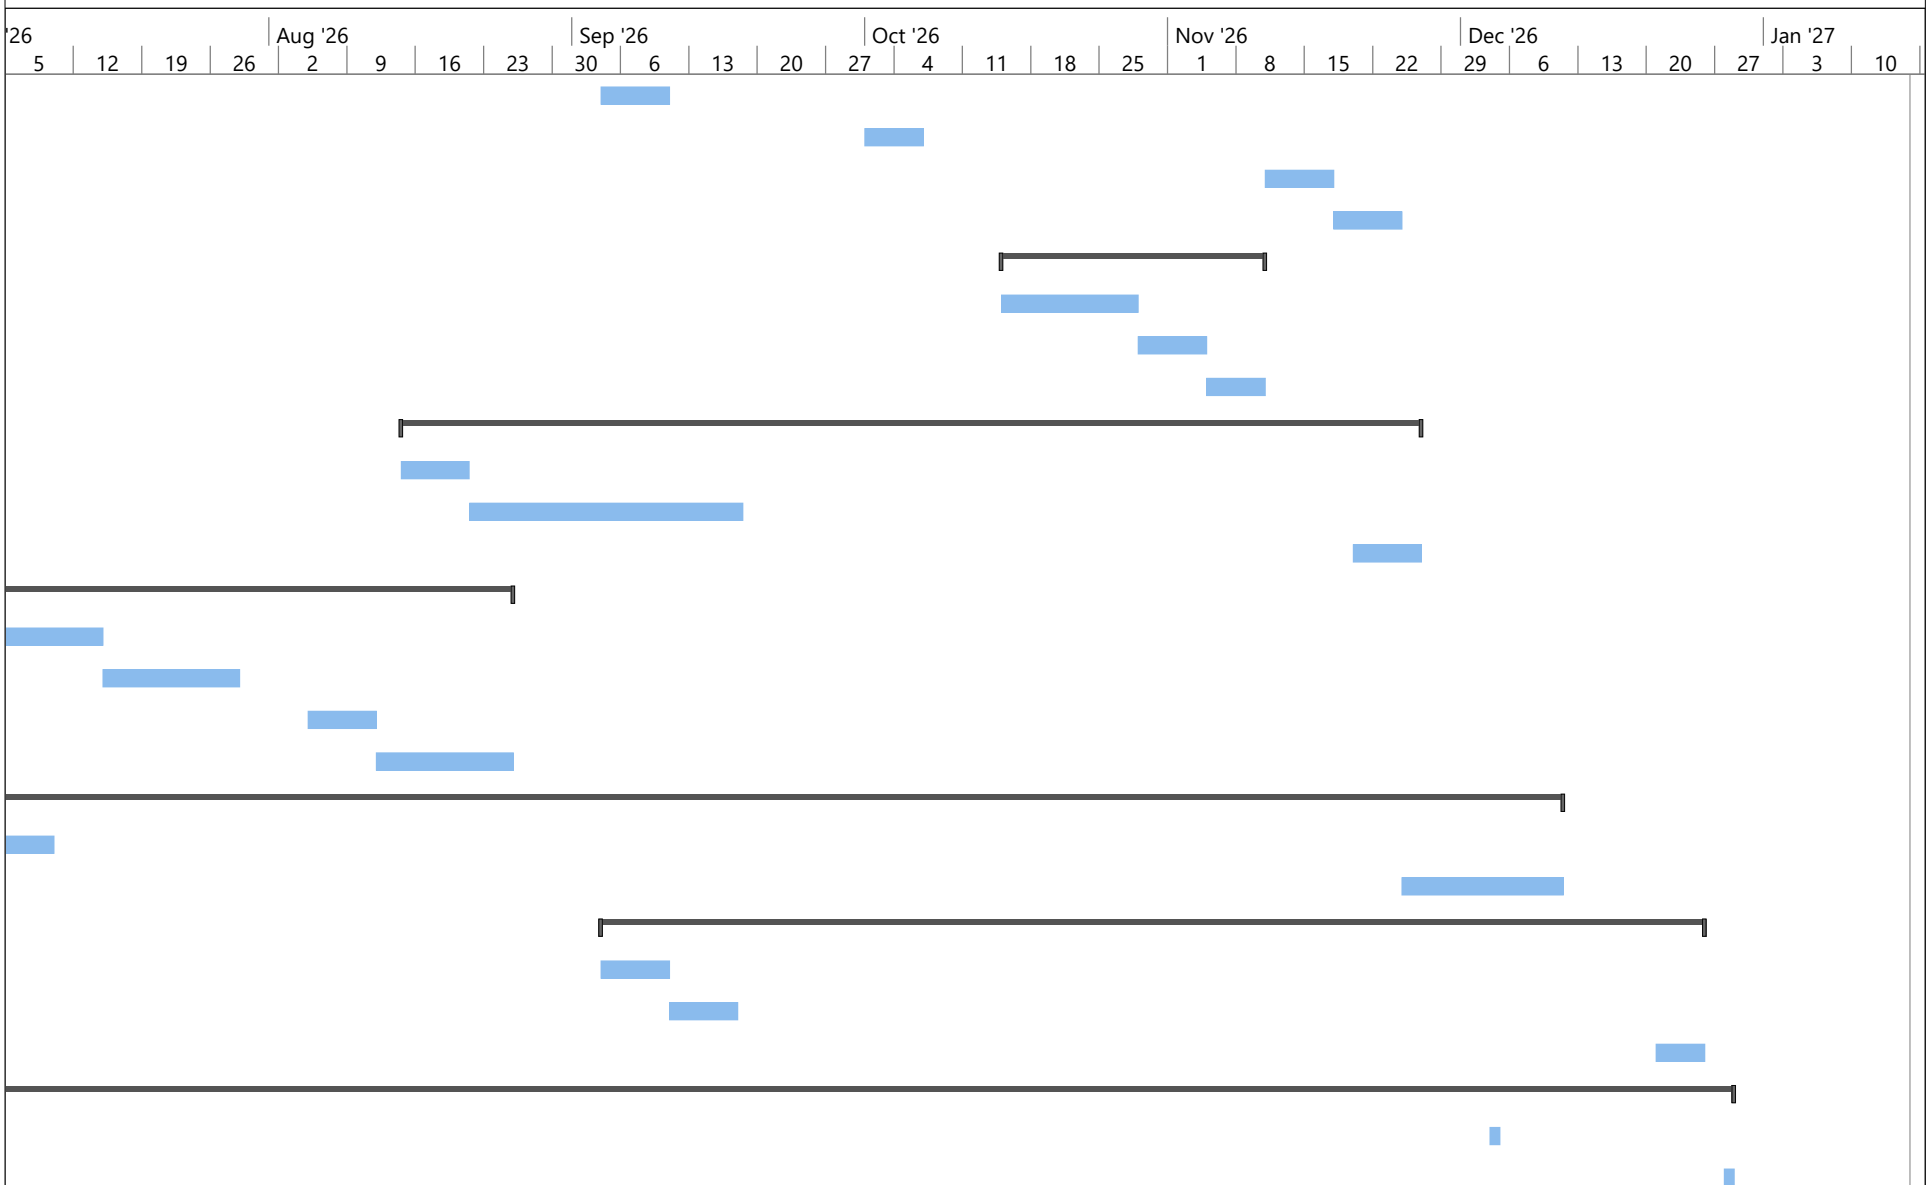

Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

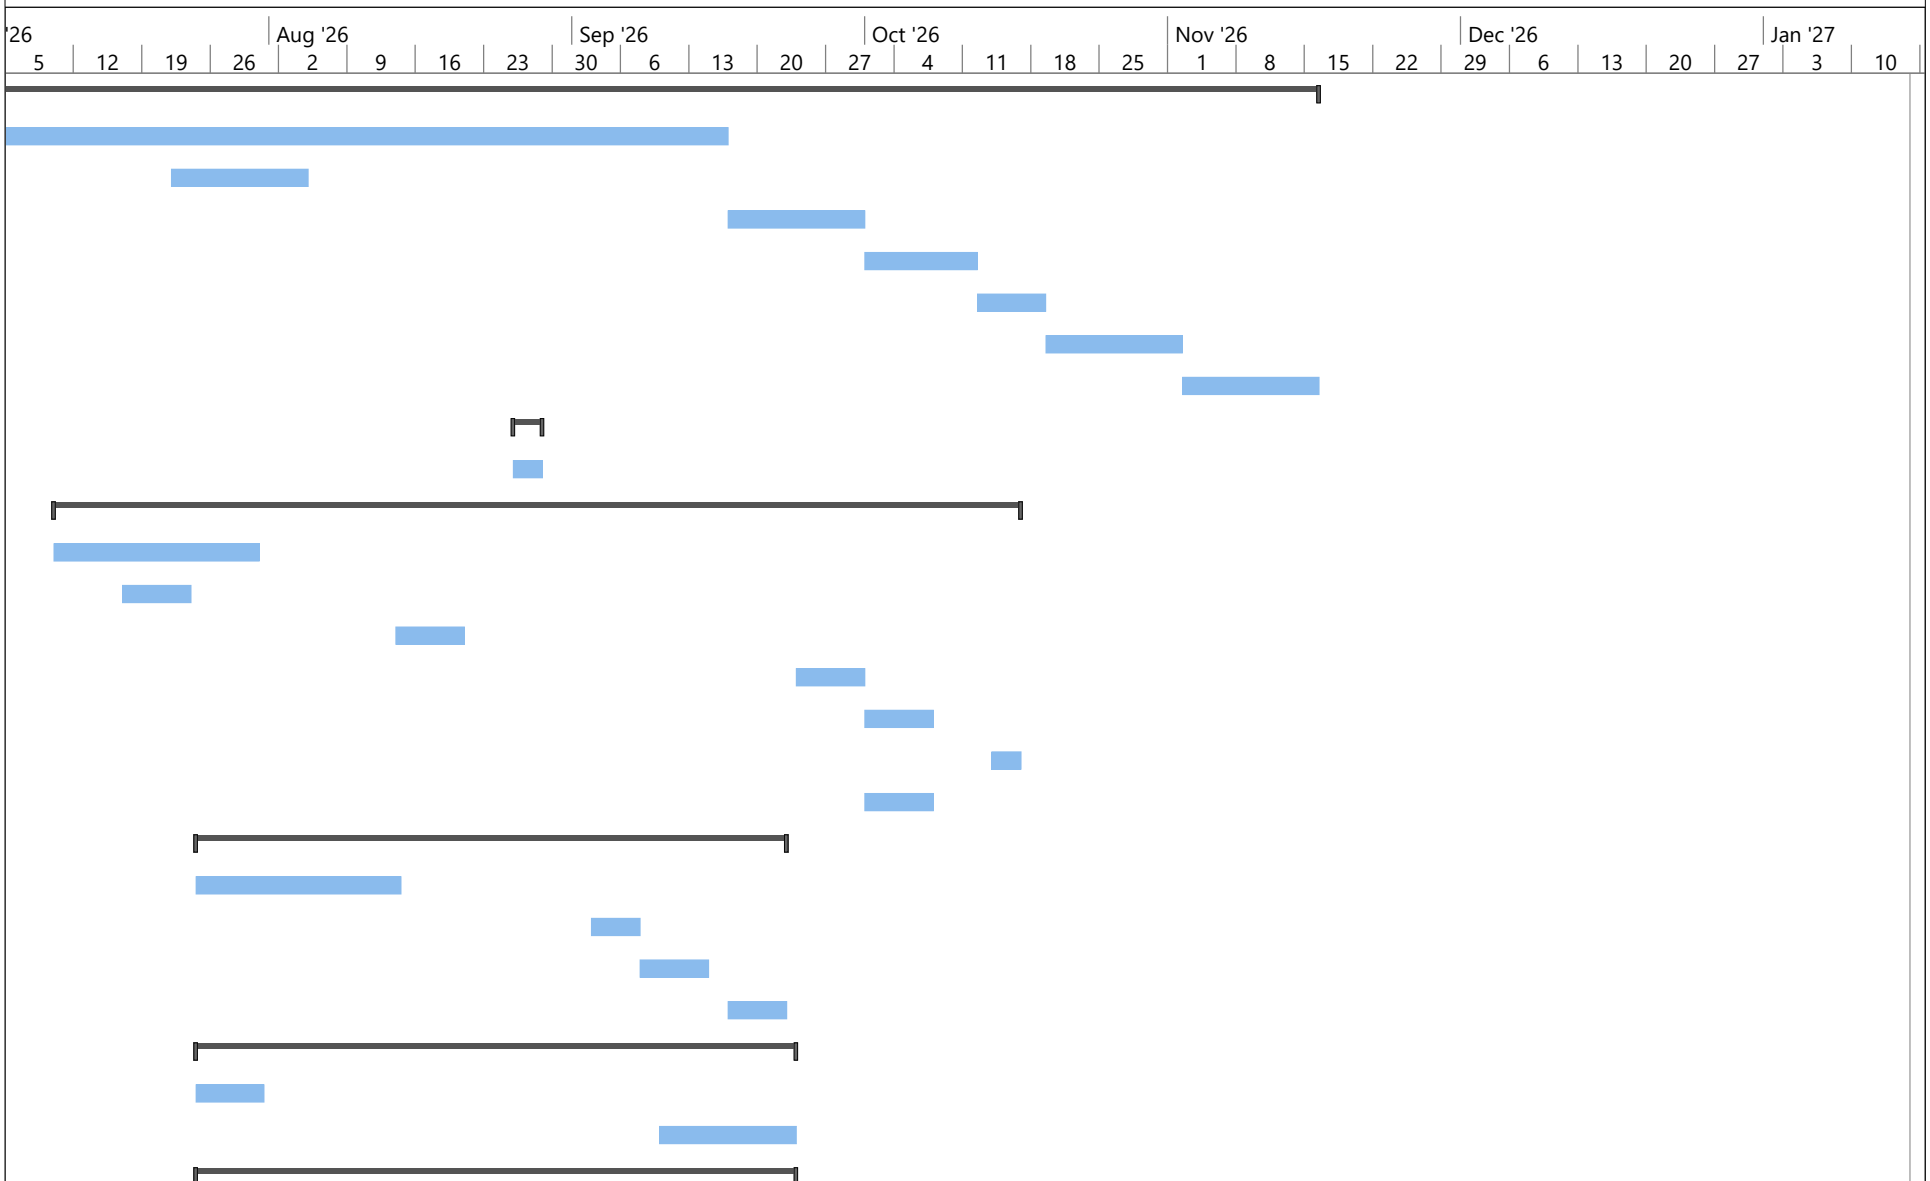

Snowflake
7 Times Square 29-31
STO Schedule
5/24/26

