NORTHERN WOLVES
AIR CONDITIONING

55 9th St, 55-A2, Brooklyn, NY 11215
(347) 463-9248


HYDRONIC PRESSURE TEST
TEST REPORT

Project: ACNE Studio
Address: 82-84 Gansevoort Street, New York, NY
System: Supply and return piping loop serving (2) water source heat pump (WSHP) units
Date of test: 07/15/2026
Report issued: 10/15/2026

Northern Wolves AC performed a pressure test on the hydronic supply and return piping loop serving the (2) water source heat pump units at the above project. The piping was pressurized to **175 psig** and held for **two (2) hours**. The test pressure held for the full test period and the piping was found tight. The system **passed** the test.

Test item	Result
Piping tested	Supply and return loop, (2) WSHP units
Test pressure	175 psig
Test duration	2 hours
Test gauge	Trerice pressure gauge, 0-300 psi
Pressure at end of test	175 psig, no pressure loss
Result	**PASSED**

Test gauge

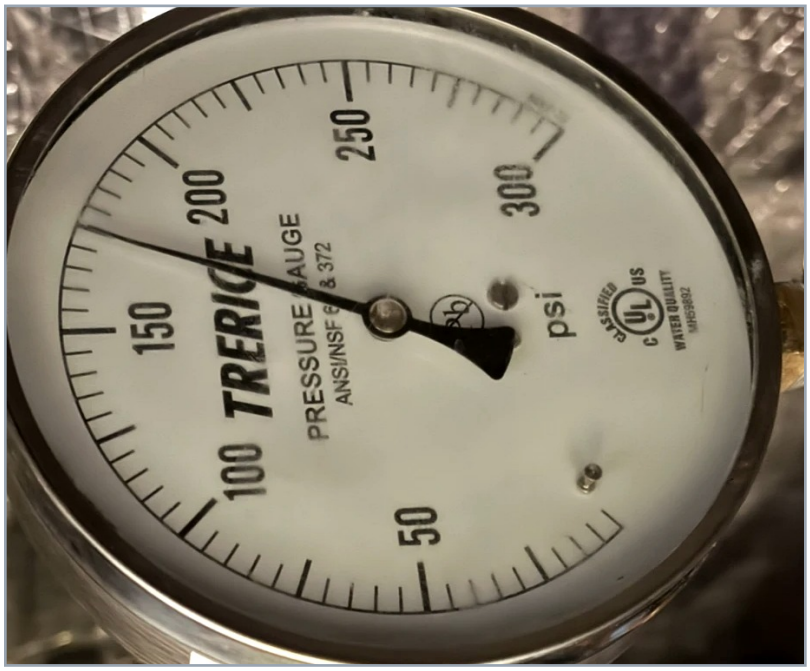

Test gauge reading 175 psig, 07/15/2026, 12:00 PM.

Test performed by:
Jean Ramirez
Technician, Northern Wolves AC
jean@northernwolvesac.com
(347) 463-9248

Technician signature / date

Witnessed by (name / company / date)
