NORTHERN WOLVES
AIR CONDITIONING

SADDLE RIVER DAY SCHOOL
147 Chestnut Ridge Rd, Saddle River, NJ 07458

RESPONSE TO MEP PUNCH LIST (JU# 24-050)
Mechanical items 1-17 - Backup Binder

Northern Wolves Inc. | November 9, 2026

DRAFT

EXHIBIT INDEX

A	Johnson & Urban MEP punch list, 7/15/2026 (JU# 24-050)
1-A	NWAC One-Year Labor Warranty, 6/18/2026
1-B	Contractor's Warranty (March form), 9/1/2026
1-C	O&M / IOM manuals and manufacturer warranties - transmittal 8/14/2026
1-D	HVAC as-built drawings, ductwork and piping
1-E	AME BMS as-builts / O&M, control submittal 25-05617
2-A	ADE VFD start-up report, lab hood exhaust fans LHEF-1/2/3, 6/3/2026
2-B	Boiler start-up and combustion test report (May 2026) (to be inserted)
2-C	RTU start-up reports (ADE / Greenheck) (to be inserted)
3	AME controls checkout, occupied / unoccupied schedules, thermostat limits (to be inserted)
5-A	Air balancing report, Rite Technical Services, 6/17/2026
5-B	Water balancing report, Rite Technical Services, 7/14/2026
8	HVAC owner training confirmation, training of 8/31/2026 (sent to March 10/6/2026)

EXHIBIT A

Johnson & Urban MEP punch list, 7/15/2026 (JU# 24-050)

Johnson & Urban, LLC
Consulting Engineers

July 15, 2026

Patryk Ciemierkiewicz,
Junior Architect III

DIG ARCHITECTURE
MBE | SBE Certified
pciemierkiewicz@digarch.com | digarch.com

RE: Saddle River Day School - MEP Punch List
JU#: 24-050

This letter is to provide you with our mechanical, electrical and plumbing punch list comments from our site visit and walk through of the referenced facility on July 8, 2026:

Mechanical

1. Provide As-Built drawings, O&M manuals, and Warranties.
2. Submit vendor equipment start-up reports.
3. Controls contractor to submit start-up checklist showing all control and monitor point as per this contract have been provided and tested.
4. Test unoccupied and occupied modes of operation for all equipment.
5. Provide air-side and water-side balancing reports.
6. Set thermostat limits per the owner's requirements.
7. Test heating/cooling mode of operation for RTU's.
8. Provide training for the new systems and controls for the owner.
9. The RTU condensate drains are PVC and the drawing spec on M-002 calls for copper type L piping with wrought copper fittings.
10. RTU-1 high stage compressor is extremely loud and was measured at 93db. This did not occur when first installed. This must be investigated and corrected. This sound radiates into the admin offices and is unacceptable.
11. The installation of the refrigerant lines through the roof curb boots is incorrect. The boot is cut out for the line set insulation but should have been cut only to accept the bare copper line set, with the insulation jacket butting up against the boot from both sides. Replace the boots and clamp boot directly to line set.
12. Provide 3 – L brackets, anchored into the slab, at the base of the hydronic expansion tanks.
13. The fin tube radiator enclosures are not securely mounted and are very wobbly. These will easily be damaged if pushed, stood on or otherwise impacted. Provide additional support to stiffen the enclosures.
14. Install rooftop fireplace exhaust fan control panel cover.

15. Visible bare control cable behind the fin tube radiators should be incased in flex metal conduit (not PVC clad), with connectors at both sides for a durable installation. The bare cable is subject to damage during cleaning behind the radiators.
16. Test all science lab hood exhaust fan systems.
17. Verify firestopping requirements for hydronic piping through block walls and rated walls. Provide sheet metal flashing to cover rough masonry openings or patch with cement. Especially where duct louvers are installed on block walls.

Electrical

1. Provide As-Built drawings, O&M manuals, and Warranties.
2. Provide typewritten panel schedules and identification tags for all panels and disconnects.
3. Label all disconnects, drives, enclosed circuit breakers, junction boxes pull points etc with panel and circuit information.
4. Test the Area of Refuge system, fire alarm and emergency radio systems. Provide start up checklists/start up reports to owner.
5. Provide lighting system training for the owner.
6. Verify that all lighting programming is completed and all lighting operates as per contract.
7. Flex conduit penetrates the roof curb boots and terminates at the condensers. Flex conduits should not be running through the boot. Provide metal conduit through boots and transition to flex within 3' of the equipment. As installed, the flex conduit has no support where it penetrates the boot and transitions to horizontal. This strain will result in breakage of the flex conduit.
8. Close up wireway under the pump drives in the boiler room.
9. Verify firestopping requirements for conduit penetrations through block walls and rated block walls.

Plumbing/FP

1. Provide As-Built drawings, O&M manuals, and Warranties for gas piping installation.
2. Provide HWH vendor start up report.
3. Set main tempering valve to 120 degrees maximum.
4. Set all flush valve to the manufacturers recommended pressures.
5. Clean all strainers.
6. Provide owner with the water sanitization report.
7. Provide 3 – L brackets, anchored into the slab, at the base of the HWH expansion tank.
8. Provide fire protection test report and town inspector approval to owner.
9. As installed, the under sink hot water tempering valves are hanging under the sinks with no support. The tempering valves should be fastened to the back wall with screws.
10. Verify that plastic traps are acceptable under the gang toilet sinks.

Thomas M Tiarks
Construction Management Engineer

EXHIBIT 1-A

NWAC One-Year Labor Warranty, 6/18/2026

NORTHERN WOLVES
AIR CONDITIONING

Northern Wolves Inc
(347) 463-9248
55 9th street, Unit 55A-2,
Brooklyn, NY 11215
United States

06/18/2026

MARCH ASSOCIATES CONSTRUCTION
601 Hamburg Turnpike,
Suite 300,
Wayne. NJ 07470.

Re: PROJECT SUBCONTRACTOR'S WARRANTY
Subject: **SADDLE RIVER DAY SCHOOL**
Project No: 482
147 Chestnut Ridge Rd.,
Saddle River, NJ 07458

Thank you for the opportunity to furnish and install the HVAC Systems at SADDLE RIVER DAY SCHOOL Project.

Our One-Years Labor warranty period began at the date of final system start-up and testing on 06/17/2026 and will expire one year from that date on 06/17/2027 at 12 AM EST).

General Warranty Terms:

1. Should any defect of workmanship develop during the warranty period, Northern Wolves, Inc will be responsible for repair or replacement (at our discretion) of any defective workmanship.
2. The Owner shall give prompt written notice of the defective work and Northern Wolves, Inc. shall have a reasonable period of time to address. During the warranty period, if Owner fails to notify Northern Wolves, Inc. and to give Northern Wolves, Inc. an opportunity to make the corrections, Owner waives the rights to require corrections by Northern Wolves, Inc. and to make a claim for breach of warranty.
3. It is our policy, when possible, to perform Warranty work during regular working hours. Unless the issue is an emergency, availability of personnel will be on a first call first response basis.
4. Northern Wolves, Inc is not responsible for warranty coverage on any equipment repaired by others, abused, altered, misused, damaged by fire, flood, or act of God, or which has not been reasonably and properly maintained, it is due to normal wear and tear.
5. Owner is responsible for preventive maintenance, inspections, calibration, and other general maintenance tasks.
6. Non-Warranty service calls are considered billable to the Owner. If the problem has been determined to be outside the scope of warranty coverage, our Service Technician will provide you with a written description of the problem encountered and with your approval, the corrective work will be performed. Other items not covered by Warranty include: any system upgrades, system parameter adjustments, problems with equipment other than that provided by Northern Wolves, Inc, etc.
7. This is non-revolving warranty, in that work repaired during the warranty period does not extend coverage beyond the original time period.
8. **All existing Landlord's equipment is NOT included in NWAC's warranty**.
9. DISCLAIMER.
   THIS IS THE SOLE WARRANTY GIVEN BY NORTHERN WOLVES, INC. IT IS IN LIEU OF ALL OTHER WARRANTIES, EXPRESSED OR IMPLIED, INCLUDING THE WARRANTIES OF MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE AND ALL WARRANTIES ARISING FROM COURSE OF DEALING OR USAGE OF TRADE.

Let us take this opportunity to thank you again for selecting a Northern Wolves, Inc for your project. Should you have any questions or concerns regarding your new system please do not hesitate to call us.

Sincerely,

Leonid Leonidov

Leonid Leonidov - General Manager
Northern Wolves, Inc.

EXHIBIT 1-B

Contractor's Warranty (March form), 9/1/2026

Contractor's Warranty – Saddle River Day School

Northern Wolves, Inc. (Hereinafter referred to as "Warrantor"), in connection with the Heating, Ventilation and Air Conditioning work performed by the Warrantor under agreement between **March Associates Construction, Inc.** and the Warrantor dated 05/06/2025 for Saddle River Day School located in 147 Chestnut Ridge Road, Saddle River NJ 07458, hereby warrants and guarantees, for a period commencing from the date of completion of the contract and extending for one year thereafter, that the project shall be free from defects and the Warrantor agrees to perform all work and repairs necessary, at its sole cost expense, to correct any faults and imperfections that may arise due to defects in material and/or workmanship, except that the period shall be extended for particular items of work where such longer periods are specified in the contract referred to herein. This Warranty shall extend to Saddle River Day School, and their successors and assigns. Saddle River Day School agrees to notify the Warrantor of the existence of any defects and Warrantor agrees to expeditiously make the necessary repairs. In the event the Warrantor fails to comply with its obligations hereunder, Saddle River Day School shall be entitled to contract with other companies for the repair, and Warrantor shall be liable for all damages, including legal fees and litigation costs, in connection with any such default.

Warrantor:
Northern Wolves, Inc.
Subcontractor

55 9th Street, Unit 55A-2,
Brooklyn, NY 11215
Address

Date of Commencement:
September 1, 2026

By: Leonid Leonidov
Name: Leonid Leonidov

Title: General Manager

EXHIBIT 1-C

O&M / IOM manuals and manufacturer warranties - transmittal 8/14/2026

O&M / IOM MANUALS AND MANUFACTURER WARRANTIES - TRANSMITTAL

Submitted by: Alikhan Ilyas, Northern Wolves Inc.
Date: August 14, 2026
To: Lorrany, March Associates (cc Gabriel Miani, P.E.)

Content: Installation, operation and maintenance manuals and manufacturer warranties for all HVAC equipment furnished under the Northern Wolves subcontract, delivered as a shared Dropbox folder.

Link:
https://www.dropbox.com/scl/fo/rykt36ff0fkd4uh5br5dd/APIWgmKFP-MdthlZG_hjGqA?rlkey=f9ftczvasc0vsttiv1njzbx1d&dl=0

A copy of the folder can be provided on a USB drive on request.

EXHIBIT 1-D

HVAC as-built drawings, ductwork and piping

HVAC AS-BUILT DRAWINGS, DUCTWORK AND PIPING

Provided electronically in the Saddle River Day School close-out folder (file size too large for this binder):

https://drive.google.com/drive/folders/1UIkEO-esOINCEb22ZkSWAfN4f3buonJ3

EXHIBIT 1-E

AME BMS as-builts / O&M, control submittal 25-05617

AME BMS AS-BUILTS / O&M, CONTROL SUBMITTAL 25-05617

Provided electronically in the Saddle River Day School close-out folder (file size too large for this binder):

https://drive.google.com/drive/folders/1UIkEO-esOINCEb22ZkSWAfN4f3buonJ3

EXHIBIT 2-A

ADE VFD start-up report, lab hood exhaust fans LHEF-1/2/3, 6/3/2026

ENGINEERED SERVICE, an ADE Company Date:6-3-26

150 ALBANY AVE., FREEPORT, N.Y. 11520 Day: 1 of 1 Page: 1 of : 1

EMAIL: SERVICE@ADEHVAC.COM

SERVICE REPORT

Bill to: Jobsite: SADDEL RIVER DAY SCHOOL Other info:

NORTHERN WOLVES 147 CHESTNUT RIDGE RD ,NJ. H.P.:

VOLTS:

Phone: Phone: 347-397-2551 AMPS:

Contact: Contact:ALBERTO

PO#:

Work Requested/Instructions:

SERIAL# J0235E135910055 MODEL#: CIMR-VU2A0006AA TAG # LHEF-1

SERIAL # J0235E135910129 MODEL # CIMR-VU2A0006AA TAG # LHEF-2

SERIAL # J062E2894728821 MODEL # CIMR-VU2A0010AA TAG # LHEF-3

Service Provided: START UP (3) V-1000 VFD"S. SET ROTATION, CHECKED AND SET AMPERAGE, SET ALL STANDARD PARAMETERS IN DRIVES TO START AND STOP SMOOTHLY AND QUIET PARAMETERS SET B1=COAST B3-01=1 B3-24=1 C1-01=30 SEC C1-02=30 SEC D2-02=25% E2-01=FLA L5-01=4 S1-01=1 RAN AUTO TUNE AND TURNED OFF PROGRAM WIZARD

TIES:ON -OFF 0-10 V SPEED REF AND STATUS

Follow-up REQ'D? Yes No X Explain:

Is Sticker on Drive? Yes X No

Labor			**Material**			
Hours	Rate	Total	Qty.	Part No./Description	Price	Total

Departed for Jobsite: 5.00 AM

Arrived @ Jobsite: 7.15.AM

Departed Jobsite: 12.20.PM

Arrived @ Office:

Other:

Total Miles Round Trip:_____ @ 50¢ per mile =

Tolls:_____ + Parking:_____ =

Misc.:_____ =

Service Fee:

Total Labor:

Total Material:

Total Other:

Sub Total:

Tax:

TOTAL:

Authorized Signature_____ Print Name/Date _____

EXHIBIT 2-B

Boiler start-up and combustion test report (May 2026)

TO BE INSERTED BEFORE ISSUE
Requested 11/9/2026 from Michael Liranzo (Ferguson) / Lochinvar.

EXHIBIT 2-C

RTU start-up reports (ADE / Greenheck)

TO BE INSERTED BEFORE ISSUE
Requested 11/9/2026 from Ryan Adams (ADE).

EXHIBIT 3

AME controls checkout, occupied / unoccupied schedules, thermostat limits

TO BE INSERTED BEFORE ISSUE
Requested from James Winship / Arth Patel (AME).

EXHIBIT 5-A

Air balancing report, Rite Technical Services, 6/17/2026

Rite Technical Services, Inc.
183 Broadway, Ste 216, Hicksville, NY 11801
Tel: (718) 576 1786

TESTING AND BALANCING REPORT

FOR

SADDLE RIVER DAY SCHOOL

147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

PREPARED FOR

NORTHERN WOLVES INC
55 9TH STREET, UNIT 55A-2
BROOKLYN, NY 11215

06/17/2026

CERTIFICATION

PROJECT NAME: SADDLE RIVER DAY SCHOOL

LOCATION: 147 CHESTNUT RIDGE ROAD, SADDLE RIVER, NJ 07458

The data presented in this report is a record of system measurements and final adjustments that have been obtained in accordance with the current edition of the NEBB procedural standards for testing, adjusting and balancing of environmental systems. Any variances from the design quantities, which exceed NEBB tolerances, are noted in the testing and balancing report.

STAMP



DATE:

06/17/2026

RITE TECHNICAL SERVICES, INC.
183 BROADWAY, STE 216
HICKSVILLE, NY 11801

AIR & HYDRONIC SYSTEMS
ROHIT ARORA
CERTIFICATON # 3540
EXPIRATION DATE: 12/31/2026

INSTRUMENTATION LIST

AND

CALIBRATION DATES

Instrument Ownership for Firm: Rite Technical Services, Inc.

Date: 05/02/2026

	FUNCTION	MINIMUM RANGE	MINIMUM ACCURACY	MINIMUM RESOLUTION	INSTRUMENT INFORMATION	CALIBRATION INTERVAL
A,H	**Rotation Measurement**	60 to 5000 rpm	± 2% of reading ± 2 rpm	± 1 rpm	Mfr. / Model Number: EXTECH/461920 Serial Number: 130723148	12 Months F Date: 05/02/2026
	Temperature Measurement					
A	Air	-0 to 200 deg. F (US) -20 to 100 deg. C (SI)	± 0.5% of reading ± 2 deg. F (US) ± 1 deg. C (SI)	0.1 deg. F (US) 0.1 deg. C (SI)	Mfr. / Model Number: SHORTRIDGE/ADM870C Serial Number: M13148	12 Months B Date: 05/02/2026
H	Immersion	-0 to 200 deg. F (US) -20 to 100 deg. C (SI)	± 0.5% of reading ± 2 deg. F (US) ± 1 deg. C (SI)	0.1 deg. F (US) 0.1 deg. C (SI)	Mfr. / Model Number: SHORTRIDGE/ADT442 Serial Number: M06306-2	12 Months D Date: 05/02/2026
H	Contact	-0 to 200 deg. F (US) -20 to 100 deg. C (SI)	± 0.5% of reading ± 2 deg. F (US) ± 1 deg. C (SI)	0.1 deg. F (US) 0.1 deg. C (SI)	Mfr. / Model Number: SHORTRIDGE/ADT444 Serial Number: 122611	12 Months E Date: 05/02/2026
	Electrical Measurement CAT III True RMS					
A,H	Volts	1 to 600 VAC	± 2% of reading	1.0 Volt	Mfr. / Model Number: FLUKE / 323	12 Months G
A,H	Amperes	0.1 to 100 Amps	± 2% of reading	0.1 Ampere	Serial Number: 51427508MV	Date: 05/02/2026
A	**Air Pressure Measurement**	0 to 10.00 in.w.g. (US) 0 to 2500 Pascals (SI)	± 2% of reading ± 0.001 in. w.g. (US) ± 0.25 Pa (SI)	0.001 in. w.g. ≤ 1 in. w.g. (US) 0.10 Pa ≤ 250 Pa (SI) 0.01 in. w.g. > 1 in. w.g. (US) 1.0 Pa > 250 Pa (SI)	Mfr. / Model Number: SHORTRIDGE/ADM870C Serial Number: M13148	12 Months B Date: 05/02/2026

Instrument Ownership for Firm: Rite Technical Services, Inc.

Date: 05/02/2026

	FUNCTION	MINIMUM RANGE	MINIMUM ACCURACY	MINIMUM RESOLUTION	INSTRUMENT INFORMATION	CALIBRATION INTERVAL
A	**Air Velocity Measurement Hot Wire Anemometer OR Airfoil with Digital Meter**	**100 to 3500 fpm**	**±5% of reading, ± 7 fpm**	**1.0 fpm**	Mfr. / Model Number: SHORTRIDGE/ADM870C Serial Number: M13148	12 Months B Date: 05/02/2026
A	**Air Velocity Measurement Rotating Vane**	**50 to 2500 fpm**	**± 2% of reading ± ± 4 fpm**	**1.0 fpm**	Mfr. / Model Number: TSI/8322 Serial Number: 55060516	12 Months A Date: 05/02/2026
A	**Humidity Measurement**	10 to 90% RH	3% of reading	1.0%	Mfr. / Model Number: EXTECH/RH300 Serial Number: 10386511	12 Months H Date: 05/02/2026
A	**Direct Reading Hood**	100 to 2000 cfm (US) 50 to 944 l/s (SI)	± 5% of reading ± 7 cfm (US) ± 4 l/s (SI)	Digital 1.0 cfm (US) Digital 1.0 l/s (SI) Analog - Not Applicable	Mfr. / Model Number: SHORTRIDGE/8400 Serial Number: M06306-1	12 Months C Date: 05/02/2026

Instrument Ownership for Firm: Rite Technical Services, Inc.

Date: 05/02/2026

	FUNCTION	MINIMUM RANGE	MINIMUM ACCURACY	MINIMUM RESOLUTION	INSTRUMENT INFORMATION	CALIBRATION INTERVAL
H						
	Hydronic Pressure Measurement	0.4 to 200 psi (US) 3 to 1400 kPa (SI)	± 2% of reading ± 1 psi (US) ± 7 kPa (SI)	0.1 psi (US) 1.0 kPa (SI)	Mfr. / Model Number: ALNOR/HM680 Serial Number: 70552168	12 Months I Date: 05/02/2026
H						
	Hydronic Differential Pressure Measurement	0.4 to 75 psi (US) 3 to 500 kPa (SI)	± 2% of reading ± 0.5 psi (US) ± 3.5 kPa (SI)	0.01 psi (US) 0.1 kPa (SI)	Mfr. / Model Number: ALNOR/HM680 Serial Number: 70552168	12 Months I Date: 05/02/2026

CONTENTS

PROJECT: SADDLE RIVER DAY SCHOOL

LOCATION: 147 CHESTNUT RIDGE ROAD, SADDLE RIVER, NJ 07458

S. NO.	DESCRIPTION	PAGE
1	SUMMARY	1.1
2	RTU-1 AND VAV'S TEST REPORT	2.1 – 2.13
3	RTU-2 AND VAV'S TEST REPORT	3.1 – 3.25
4	RTU-3 AND VAV'S TEST REPORT	4.1 – 4.19
5	RTU-4 TEST REPORT	5.1 – 5.4
6	RTU-5 TEST REPORT	6.1 – 6.4
7	RTU-6 TEST REPORT	7.1 – 7.4
8	RTU-7 TEST REPORT	8.1 – 8.4
9	LHEF-1, LHEF-2, LHEF-3 TEST REPORT	9.1 – 9.5
10	EF-1, EF-2, EF-3 TEST REPORT	10.1 – 10.4
11	NUMBERED LAYOUT	APPENDIX
12	ABBREVIATIONS & DEFINITIONS	APPENDIX

Rite Technical Services, Inc.
183 Broadway, Ste 216
Hicksville, NY 11801
T: (718) 576 1786

06/17/2026

SUMMARY

TESTING AND BALANCING

Northern Wolves Inc
55 9th Street, Unit 55A-2
Brooklyn, NY 11215

Ref: Saddle River Day School

Location: 147 Chestnut Ridge Road, Saddle River, NJ 07458

Attn: Ruslan Zhdamarov,

Our firm performed testing and balancing at the above referenced project. The measured results are listed in the attached detailed report.

Should you have any questions regarding the information in the report, please do not hesitate to call our office.

Yours truly,



Rohit Arora

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-1 (SUPPLY)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-1
MANUFACTURER	GREENHECK
MODEL NUMBER	RT-120-20L-M-G0
SERIAL NUMBER	28137399
LOCATION	ROOF

MOTOR DATA (2X)	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 184T
HP (KW)		5.0
RPM		1750
RATED VOLTS		460
RATED AMPS		6.6
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz AT VFD #1	60	62
OPERA. VOLTS L1/L2/L3 VFD #1	460	490/491/490
OPERA. AMPS L1/L2/L3 VFD #1	6.6	3.7/6.6/3.6

FAN DATA	DESIGN	ACTUAL
SUPPLY AIR CFM	5800	5669
OUTSIDE AIR CFM	1500	1630
EXTERNAL DISCHARGE S.P. in. w.g.	-	1.78
EXTERNAL SUCTION S.P. in. w.g.	-	-0.19
EXTERNAL S.P. in. w.g.	1.50	1.97
DIFF. S.P. in. w.g. @ DPR	-	0.16
DIFF. S.P. in. w.g. @ FF/CC	-	0.33
TOTAL S.P. in. w.g.	3.30	2.46
FAN RPM #1	1826	1836
FAN RPM #2	1826	1837

OTHER DATA	DESIGN	ACTUAL
OPERATING Hz AT VFD #2	60	62
OPERA. VOLTS L1/L2/L3 VFD #2	460	490/491/490
OPERA. AMPS L1/L2/L3 VFD #2	6.6	3.7/6.6/3.7

NOTE: S.P. SET PONIT AT BMS = 1.50" W.G.

NOTE: OAD: 20% OPEN, RAD: 80% OPEN AT BMS.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-1 (EXHAUST)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-1
MANUFACTURER	GREENHECK
MODEL NUMBER	AER-24-02-630--5HP
SERIAL NUMBER	205113682-0001 251
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 184T
HP (KW)		5
RPM		1750
RATED VOLTS		460
RATED AMPS		6.8
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	17.5
OPERA. VOLTS L1/L2/L3	460	490/489/490
OPERA. AMPS L1/L2/L3	6.8	2.1/2.2/2.2

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	1500	1530
DISCHARGE S.P. in. w.g.	-	0.01
SUCTION S.P. in. w.g.	-	-0.22
TOTAL S.P. in. w.g.	1.14	0.23
FAN RPM	1484	514

OTHER DATA	DESIGN	ACTUAL

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-1 (EXHAUST-ECONOMIZER MODE)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-1
MANUFACTURER	GREENHECK
MODEL NUMBER	AER-24-02-630--5HP
SERIAL NUMBER	205113682-0001 251
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 184T
HP (KW)		5
RPM		1750
RATED VOLTS		460
RATED AMPS		6.8
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	50
OPERA. VOLTS L1/L2/L3	460	490/489/490
OPERA. AMPS L1/L2/L3	6.8	5.2/5.3/5.2

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	5800	6120
DISCHARGE S.P. in. w.g.	-	0.01
SUCTION S.P. in. w.g.	-	-0.71
TOTAL S.P. in. w.g.	1.14	0.72
FAN RPM	1484	1473

OTHER DATA	DESIGN	ACTUAL

Rite T & B

ADDITIONAL INFORMATION

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

ADDITIONAL INFORMATION				
TERMINAL NUMBER	AIRFLOW SETPOINT	ACTUAL AIRFLOW	DAMPER POSITION	NOTES
VAV-1-1	2000 (MAX)	2020	100	
VAV-1-2	560 (MAX)	563	53	
VAV-1-3	780 (MAX)	786	74	
VAV-1-4	1290 (MAX)	1297	53	
VAV-1-5	200 (MAX)	205	45	
VAV-1-6	250 (MAX)	253	58	
VAV-1-7	80 (MAX)	83	38	
VAV-1-8	240 (MAX)	243	53	
VAV-1-9	215 (MIN)	219	19	

VAVS COMMANDED TO NOTED AIRFLOW SETPOINT TO SIMULATE RTU DESIGN AIRFLOW DUE TO DIVERSITY.

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-1-1	**PRIMARY MAXIMUM AIRFLOW CFM**	2000	1994	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	350	353	
SIZE	12Ø				
K STAND. / OFFSET	2062 / 477.29				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
LOBBY G-101	1	OED	28X8	-	-	750	-	746	
LOBBY G-101	2	OED	28X8	-	-	750	-	742	
LOBBY G-101	3	OED	28X8	-	-	500	-	506	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-1-2	**PRIMARY MAXIMUM AIRFLOW CFM**	560	572	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	210	212	
SIZE	7Ø				
K STAND. / OFFSET	702 / 20.47				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM G-102	1	SG	10X4	-	-	140	-	145	
ROOM G-102	2	SG	10X4	-	-	140	-	148	
ROOM G-102	3	SG	10X4	-	-	140	-	142	
ROOM G-102	4	SG	10X4	-	-	140	-	137	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-1-3	**PRIMARY MAXIMUM AIRFLOW CFM**	780	794	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	300	313	
SIZE	8Ø				
K STAND. / OFFSET	916 / 66.25				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM G-103B	1	SG	14X6	-	-	260	-	265	
ROOM G-103B	2	SG	14X6	-	-	260	-	259	
ROOM G-103B	3	SG	14X6	-	-	260	-	270	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-1-4	**PRIMARY MAXIMUM AIRFLOW CFM**	1290	1315	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	360	364	
SIZE	12Ø				
K STAND. / OFFSET	2062 / 168.07				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM G-103B	1	SG	16X8	-	-	430	-	440	
ROOM G-103B	2	SG	16X8	-	-	430	-	443	
ROOM G-103B	3	SG	16X8	-	-	430	-	432	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-1-5	**PRIMARY MAXIMUM AIRFLOW CFM**	200	202	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	40	42	
SIZE	4Ø				
K STAND. / OFFSET	229 / 125.72				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM G-101A	1	4WCD	24X24	-	-	200	-	202	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-1-6	**PRIMARY MAXIMUM AIRFLOW CFM**	250	253	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	60	62	
SIZE	5Ø				
K STAND. / OFFSET	358 / 67.69				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM G-101B	1	4WCD	24X24	-	-	250	-	253	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

MANUFACTURER	PRICE		**DESIGN**	**ACTUAL**	
NUMBER	VAV-1-7	**PRIMARY MAXIMUM AIRFLOW CFM**	80	82	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	40	41	
SIZE	4Ø				
K STAND. / OFFSET	229 / 136.04				

VAV OUTLET DATA

AREA SERVED	**OUTLET**				**DESIGN**		**FINAL**		
	NO	**TYPE**	**SIZE**	**AK***	**VEL**	**FLOW**	**VEL**	**FLOW**	
ROOM G-101C	1	4WCD	24X24	-	-	80	-	82	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-1-8	**PRIMARY MAXIMUM AIRFLOW CFM**	240	243	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	80	81	
SIZE	5Ø				
K STAND. / OFFSET	358 / 68.63				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM G-101	1	4WCD	24X24	-	-	240	-	243	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-1-9	**PRIMARY MAXIMUM AIRFLOW CFM**	1850	1814	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	215	217	
SIZE	12Ø				
K STAND. / OFFSET	2062 /-1.6				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
OPEN AREA	1	SG	14X6	-	-	280	-	283	
OPEN AREA	2	SG	14X6	-	-	280	-	273	
OPEN AREA	3	SG	14X6	-	-	270	-	269	
OPEN AREA	4	SG	14X6	-	-	270	-	279	
OPEN AREA	5	SG	14X6	-	-	270	-	264	
MENS RM.	6	4WCD	24X24	-	-	200	-	183	
WOMENS RM.	7	4WCD	24X24	-	-	200	-	181	
JANITOR CLOSET	8	SG	6X6	-	-	80	-	82	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-2 (SUPPLY)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-2
MANUFACTURER	GREENHECK
MODEL NUMBER	RVE-85-58D-301-N-G2
SERIAL NUMBER	28066155
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 215T
HP (KW)		10
RPM		1770
RATED VOLTS		460
RATED AMPS		12.5
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	66.2
OPERA. VOLTS L1/L2/L3	460	489/490/490
OPERA. AMPS L1/L2/L3	12.5	9.8/9.9/10.1

FAN DATA	DESIGN	ACTUAL
SUPPLY AIR CFM	7200	7084
OUTSIDE AIR CFM	4800	4962
EXTERNAL DISCHARGE S.P. in. w.g.	-	1.61
EXTERNAL SUCTION S.P. in. w.g.	-	-0.01
EXTERNAL S.P. in. w.g.	2.00	1.62
DIFF. S.P. in. w.g. @ PF	-	0.18
DIFF. S.P. in. w.g. @ FF	-	0.19
DIFF. S.P. in. w.g. @ EW	-	0.53
DIFF. S.P. in. w.g. @ DPR	-	0.30
DIFF. S.P. in. w.g. @ FF/CC	-	1.23
TOTAL S.P. in. w.g.	4.43	4.05
FAN RPM	1952	1973

OTHER DATA	DESIGN	ACTUAL

NOTE :- S.P. SET PONIT AT BMS 1.10 INCHES OF W.G.

NOTE :- OAD 68% OPEN AND RAD 32% OPEN AT BMS.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-2 (EXHAUST)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-2
MANUFACTURER	GREENHECK
MODEL NUMBER	RVE-85-58D-301-N-G2
SERIAL NUMBER	28066155
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 215T
HP (KW)		10
RPM		1770
RATED VOLTS		460
RATED AMPS		12.5
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	42
OPERA. VOLTS L1/L2/L3	460	490/489/490
OPERA. AMPS L1/L2/L3	12.5	6.2/6.3/6.2

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	4800	4920
EXTERNAL DISCHARGE S.P. in. w.g.	-	0.44
EXTERNAL SUCTION S.P. in. w.g.	-	0.44
EXTERNAL S.P. in. w.g.	0.50	0.88
DIFF. S.P. in. w.g. @ DPR	-	0.31
DIFF. S.P. in. w.g. @ FF	-	0.05
DIFF. S.P. in. w.g. @ EW	-	0.58
TOTAL S.P. in. w.g.	1.83	1.82
FAN RPM	1324	1243

OTHER DATA	DESIGN	ACTUAL

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-2 (EXHAUST-ECONOMIZER MODE)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-2
MANUFACTURER	GREENHECK
MODEL NUMBER	RVE-85-58D-301-N-G2
SERIAL NUMBER	28066155
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 215T
HP (KW)		10
RPM		1770
RATED VOLTS		460
RATED AMPS		12.5
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	60
OPERA. VOLTS L1/L2/L3	460	490/489/489
OPERA. AMPS L1/L2/L3	12.5	8.4/8.5/8.4

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	7200	6920
EXTERNAL DISCHARGE S.P. in. w.g.	-	0.68
EXTERNAL SUCTION S.P. in. w.g.	-	-0.97
EXTERNAL S.P. in. w.g.	0.50	1.65
DIFF. S.P. in. w.g. @ DPR	-	0.29
DIFF. S.P. in. w.g. @ FF	-	0.19
DIFF. S.P. in. w.g. @ EW	-	0.84
TOTAL S.P. in. w.g.	2.43	2.97
FAN RPM	1759	1775

OTHER DATA	DESIGN	ACTUAL

Rite T & B

ADDITIONAL INFORMATION

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

ADDITIONAL INFORMATION				
TERMINAL NUMBER	AIRFLOW SETPOINT	ACTUAL AIRFLOW	DAMPER POSITION	NOTES
VAV-2-1	520 (MAX)	522	71	
VAV-2-2	550 (MAX)	545	70	
VAV-2-3	540 (MAX)	530	97	
VAV-2-4	590 (MAX)	593	82	
VAV-2-5	590 (MAX)	582	86	
VAV-2-6	100 (MAX)	100	100	
VAV-2-7	180 (MAX)	175	100	
VAV-2-8	100 (MAX)	100	80	
VAV-2-10	400 (MAX)	400	82	
VAV-2-12	680 (MAX)	676	79	
VAV-2-13	750 (MAX)	683	100	
VAV-2-14	600 (MAX)	581	100	
VAV-2-15	700 (MAX)	690	100	
VAV-2-18	365 (MAX)	366	68	
VAV-2-19	300 (MAX)	301	91	
VAV-2-21	250 (MAX)	240	100	

VAVS COMMANDED TO NOTED AIRFLOW SETPOINT TO SIMULATE RTU DESIGN AIRFLOW DUE TO DIVERSITY.

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-1	**PRIMARY MAXIMUM AIRFLOW CFM**	520	510	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	310	312	
SIZE	7Ø				
K STAND. / OFFSET	702 / -14.02				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM # 101	1	OED	6ϕ	-	-	175	-	170	
ROOM # 101	2	OED	6ϕ	-	-	175	-	172	
ROOM # 101	3	OED	6ϕ	-	-	170	-	168	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

MANUFACTURER	PRICE		**DESIGN**	**ACTUAL**	
NUMBER	VAV-2-2	**PRIMARY MAXIMUM AIRFLOW CFM**	550	541	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	265	267	
SIZE	8Ø				
K STAND. / OFFSET	916 / -1.5				

VAV OUTLET DATA

AREA SERVED	**OUTLET**				**DESIGN**		**FINAL**		
	NO	**TYPE**	**SIZE**	**AK***	**VEL**	**FLOW**	**VEL**	**FLOW**	
ROOM # 102	1	4WCD	24X24	-	-	185	-	175	
ROOM # 102	2	4WCD	24X24	-	-	185	-	182	
ROOM # 102	3	4WCD	24X24	-	-	180	-	184	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-3	**PRIMARY MAXIMUM AIRFLOW CFM**	540	551	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	265	267	
SIZE	7Ø				
K STAND. / OFFSET	702 / 6.16				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM # 104	1	4WCD	24X24	-	-	180	-	188	
ROOM # 104	2	4WCD	24X24	-	-	180	-	193	
ROOM # 104	3	4WCD	24X24	-	-	180	-	170	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-4	**PRIMARY MAXIMUM AIRFLOW CFM**	590	595	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	310	312	
SIZE	7Ø				
K STAND. / OFFSET	702 / 4.22				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM # 106	1	4WCD	24X24	-	-	200	-	194	
ROOM # 106	2	4WCD	24X24	-	-	200	-	200	
ROOM # 106	3	4WCD	24X24	-	-	190	-	201	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

MANUFACTURER	PRICE		**DESIGN**	**ACTUAL**	
NUMBER	VAV-2-5	**PRIMARY MAXIMUM AIRFLOW CFM**	590	596	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	310	311	
SIZE	7Ø				
K STAND. / OFFSET	702 / 6.88				

VAV OUTLET DATA

AREA SERVED	**OUTLET**				**DESIGN**		**FINAL**		
	NO	**TYPE**	**SIZE**	**AK***	**VEL**	**FLOW**	**VEL**	**FLOW**	
ROOM # 108	1	4WCD	24X24	-	-	200	-	195	
ROOM # 108	2	4WCD	24X24	-	-	200	-	206	
ROOM # 108	3	4WCD	24X24	-	-	190	-	195	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-6	**PRIMARY MAXIMUM AIRFLOW CFM**	100	102	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	100	102	
SIZE	4Ø				
K STAND. / OFFSET	229 / 96.67				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM # 110	1	4WCD	24X24	-	-	100	-	102	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-7	**PRIMARY MAXIMUM AIRFLOW CFM**	180	183	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	65	67	
SIZE	4Ø				
K STAND. / OFFSET	229 / 131.4				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM # 110A	1	4WCD	24X24	-	-	180	-	183	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-8	**PRIMARY MAXIMUM AIRFLOW CFM**	100	106	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	100	106	
SIZE	4Ø				
K STAND. / OFFSET	229 / 141.59				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
TOILET 100A	1	4WCD	24X24	-	-	50	-	54	
TOILET 100D	2	4WCD	24X24	-	-	50	-	52	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-9	**PRIMARY MAXIMUM AIRFLOW CFM**	400	412	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	280	282	
SIZE	6Ø				
K STAND. / OFFSET	515 / 4.33				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 109	1	4WCD	24X24	-	-	200	-	208	
ROOM 109	2	4WCD	24X24	-	-	200	-	204	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

MANUFACTURER	PRICE		**DESIGN**	**ACTUAL**	
NUMBER	VAV-2-10	**PRIMARY MAXIMUM AIRFLOW CFM**	400	399	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	280	281	
SIZE	6Ø				
K STAND. / OFFSET	515 / 11.52				

VAV OUTLET DATA

AREA SERVED	**OUTLET**				**DESIGN**		**FINAL**		
	NO	**TYPE**	**SIZE**	**AK***	**VEL**	**FLOW**	**VEL**	**FLOW**	
ROOM 109	1	4WCD	24X24	-	-	200	-	203	
ROOM 109	2	4WCD	24X24	-	-	200	-	196	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-11	**PRIMARY MAXIMUM AIRFLOW CFM**	650	647	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	350	352	
SIZE	7Ø				
K STAND. / OFFSET	702 / 3.72				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 107	1	4WCD	24X24	-	-	220	-	201	
ROOM 107	2	4WCD	24X24	-	-	220	-	225	
ROOM 107	3	4WCD	24X24	-	-	210	-	221	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-12	**PRIMARY MAXIMUM AIRFLOW CFM**	680	676	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	290	292	
SIZE	8Ø				
K STAND. / OFFSET	916 / 18.83				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 105	1	4WCD	24X24	-	-	230	-	220	
ROOM 105	2	4WCD	24X24	-	-	230	-	235	
ROOM 105	3	4WCD	24X24	-	-	220	-	221	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-13	**PRIMARY MAXIMUM AIRFLOW CFM**	750	738	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	430	430	
SIZE	8Ø				
K STAND. / OFFSET	916 / 18.25				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 200	1	4WCD	24X24	-	-	250	-	261	
ROOM 200	2	4WCD	24X24	-	-	250	-	245	
ROOM 200	3	4WCD	24X24	-	-	250	-	232	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

MANUFACTURER	PRICE		**DESIGN**	**ACTUAL**	
NUMBER	VAV-2-14	**PRIMARY MAXIMUM AIRFLOW CFM**	660	666	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	390	392	
SIZE	7Ø				
K STAND. / OFFSET	702 / 4.33				

VAV OUTLET DATA

AREA SERVED	**OUTLET**				**DESIGN**		**FINAL**		
	NO	**TYPE**	**SIZE**	**AK***	**VEL**	**FLOW**	**VEL**	**FLOW**	
ROOM 202	1	4WCD	24X24	-	-	220	-	228	
ROOM 202	2	4WCD	24X24	-	-	220	-	234	
ROOM 202	3	4WCD	24X24	-	-	220	-	204	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

MANUFACTURER	PRICE		**DESIGN**	**ACTUAL**	
NUMBER	VAV-2-15	**PRIMARY MAXIMUM AIRFLOW CFM**	700	694	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	350	352	
SIZE	7Ø				
K STAND. / OFFSET	702 / 3.57				

VAV OUTLET DATA

AREA SERVED	**OUTLET**				**DESIGN**		**FINAL**		
	NO	**TYPE**	**SIZE**	**AK***	**VEL**	**FLOW**	**VEL**	**FLOW**	
ROOM 204	1	4WCD	24X24	-	-	235	-	221	
ROOM 204	2	4WCD	24X24	-	-	235	-	225	
ROOM 204	3	4WCD	24X24	-	-	230	-	248	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-16	**PRIMARY MAXIMUM AIRFLOW CFM**	770	768	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	365	367	
SIZE	8Ø				
K STAND. / OFFSET	916 / -18.57				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 206	1	4WCD	24X24	-	-	260	-	245	
ROOM 206	2	4WCD	24X24	-	-	260	-	255	
ROOM 206	3	4WCD	24X24	-	-	250	-	268	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

MANUFACTURER	PRICE		**DESIGN**	**ACTUAL**	
NUMBER	VAV-2-17	**PRIMARY MAXIMUM AIRFLOW CFM**	700	709	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	270	273	
SIZE	7Ø				
K STAND. / OFFSET	702 / 9.60				

VAV OUTLET DATA

AREA SERVED	**OUTLET**				**DESIGN**		**FINAL**		
	NO	**TYPE**	**SIZE**	**AK***	**VEL**	**FLOW**	**VEL**	**FLOW**	
ROOM 208	1	4WCD	24X24	-	-	235	-	225	
ROOM 208	2	4WCD	24X24	-	-	235	-	243	
ROOM 208	3	4WCD	24X24	-	-	230	-	241	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-18	**PRIMARY MAXIMUM AIRFLOW CFM**	365	362	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	90	92	
SIZE	6Ø				
K STAND. / OFFSET	515 / -57.66				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 210	1	4WCD	24X24	-	-	120	-	110	
ROOM 210	2	4WCD	24X24	-	-	120	-	128	
ROOM 210	3	4WCD	24X24	-	-	125	-	124	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-19	**PRIMARY MAXIMUM AIRFLOW CFM**	300	301	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	90	91	
SIZE	4Ø				
K STAND. / OFFSET	229 / 177.02				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
CORRIDOR	1	4WCD	24X24	-	-	250	-	248	
STORAGE 203	2	OED	6ϕ	-	-	50	-	53	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-20	**PRIMARY MAXIMUM AIRFLOW CFM**	100	106	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	100	106	
SIZE	4Ø				
K STAND. / OFFSET	229 / 107.87				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
BATHROOM 200A	1	4WCD	24X24	-	-	50	-	52	
BATHROOM 200B	2	4WCD	24X24	-	-	50	-	54	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-2-21	**PRIMARY MAXIMUM AIRFLOW CFM**	250	252	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	90	91	
SIZE	5Ø				
K STAND. / OFFSET	358 / -34.65				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
CORRIDOR	1	4WCD	24X24	-	-	200	-	198	
STORAGE 105	2	OED	6ϕ	-	-	50	-	54	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

MANUFACTURER	PRICE		**DESIGN**	**ACTUAL**	
NUMBER	VAV-2-22	**PRIMARY MAXIMUM AIRFLOW CFM**	1000	999	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	1000	999	
SIZE	9Ø				
K STAND. / OFFSET	1120 / 763.50				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
CORRIDOR	1	SG	14X8	-	-	350	-	354	
WATER SERV. RM.	2	SG	12X4	-	-	150	-	153	
BOILER RM.	3	SG	12X8	-	-	250	-	242	
FIRE ALARM RM.	4	SG	10X4	-	-	100	-	102	
ELECTRICAL RM.	5	SG	10X6	-	-	150	-	148	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-3 (SUPPLY)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-3
MANUFACTURER	GREENHECK
MODEL NUMBER	RVE-85-58D-301-O-G2
SERIAL NUMBER	28066156
LOCATION	ROOF

MOTOR DATA (2X)	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 213T
HP (KW)		7.5
RPM		1770
RATED VOLTS		460
RATED AMPS		9.8
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz AT VFD #1	60	82.6
OPERA. VOLTS L1/L2/L3 VFD #1	460	490/489/489
OPERA. AMPS L1/L2/L3 VFD #1	9.8	6.4/6.5/6.5

FAN DATA	DESIGN	ACTUAL
SUPPLY AIR CFM	8600	8332
OUTSIDE AIR CFM	3300	3460
EXTERNAL DISCHARGE S.P. in. w.g.	-	1.47
EXTERNAL SUCTION S.P. in. w.g.	-	-0.01
EXTERNAL S.P. in. w.g.	2.00	1.48
DIFF. S.P. in. w.g. @ PF	-	0.08
DIFF. S.P. in. w.g. @ FF	-	0.07
DIFF. S.P. in. w.g. @ EW	-	0.53
DIFF. S.P. in. w.g. @ DPR	-	0.72
DIFF. S.P. in. w.g. @ FF/CC	-	1.35
TOTAL S.P. in. w.g.	4.63	4.23
FAN RPM #1	2436	2463
FAN RPM #2	2436	2462

OTHER DATA	DESIGN	ACTUAL
OPERATING Hz AT VFD #2	60	82.6
OPERA. VOLTS L1/L2/L3 VFD #2	460	490/489/*489
OPERA. AMPS L1/L2/L3 VFD #2	9.8	6.6/6.7/6.6

NOTE :- S.P. SET PONIT AT BMS 1.35 INCHES OF W.G.

NOTE :- OAD 30% OPEN AND RAD 70% OPEN AT BMS.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-3 (EXHAUST)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-3
MANUFACTURER	GREENHECK
MODEL NUMBER	RVE-85-58D-301-O-G2
SERIAL NUMBER	28066156
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 215T
HP (KW)		10
RPM		1770
RATED VOLTS		460
RATED AMPS		12.5
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz AT VFD	60	36
OPERA. VOLTS L1/L2/L3 VFD	460	489/489/490
OPERA. AMPS L1/L2/L3	12.5	6.1/6.2/6.2

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	3300	3260
EXTERNAL DISCHARGE S.P. in. w.g.	-	0.19
EXTERNAL SUCTION S.P. in. w.g.	-	-0.67
EXTERNAL S.P. in. w.g.	0.50	0.86
DIFF. S.P. in. w.g. @ DPR	-	0.46
DIFF. S.P. in. w.g. @ FF	-	0.18
DIFF. S.P. in. w.g. @ EW	-	0.58
TOTAL S.P. in. w.g.	1.56	2.08
FAN RPM	1091	1219

OTHER DATA	DESIGN	ACTUAL

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-3 (EXHAUST-ECONOMIZER MODE)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-3
MANUFACTURER	GREENHECK
MODEL NUMBER	RVE-85-58D-301-O-G2
SERIAL NUMBER	28066156
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 215T
HP (KW)		10
RPM		1770
RATED VOLTS		460
RATED AMPS		12.5
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz AT VFD	60	68.8
OPERA. VOLTS L1/L2/L3 VFD	460	489/490/490
OPERA. AMPS L1/L2/L3	12.5	10.8/10.9/10.8

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	8600	8056
EXTERNAL DISCHARGE S.P. in. w.g.	-	0.48
EXTERNAL SUCTION S.P. in. w.g.	-	-1.26
EXTERNAL S.P. in. w.g.	0.50	1.74
DIFF. S.P. in. w.g. @ DPR	-	0.38
DIFF. S.P. in. w.g. @ FF	-	0.23
DIFF. S.P. in. w.g. @ EW	-	0.76
TOTAL S.P. in. w.g.	2.88	3.11
FAN RPM	2029	2037

OTHER DATA	DESIGN	ACTUAL

Rite T & B

ADDITIONAL INFORMATION

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

ADDITIONAL INFORMATION				
TERMINAL NUMBER	AIRFLOW SETPOINT	ACTUAL AIRFLOW	DAMPER POSITION	NOTES
VAV-3-1	1575 (MAX)	1520	100	
VAV-3-2	330 (MAX)	310	100	
VAV-3-3	370 (MAX)	340	100	
VAV-3-4	370 (MAX)	350	100	
VAV-3-5	220 (MAX)	205	100	
VAV-3-6	360 (MAX)	350	100	
VAV-3-7	630 (MAX)	600	100	
VAV-3-8	630 (MAX)	605	100	
VAV-3-9	1250 (SET)	1280	12	
VAV-3-10	800 (MAX)	780	100	
VAV-3-11	800 (MAX)	760	100	
VAV-3-12	510 (MAX)	491	100	
VAV-3-13	250 (MAX)	248	95	
VAV-3-14	280 (MAX)	278	84	
VAV-3-15	225 (MAX)	215	100	

VAVS COMMANDED TO NOTED AIRFLOW SETPOINT TO SIMULATE RTU DESIGN AIRFLOW DUE TO DIVERSITY.

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-1	**PRIMARY MAXIMUM AIRFLOW CFM**	1575	1565	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	300	302	
SIZE	12Ø				
K STAND. / OFFSET	2062 / 88.85				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
COMMONS 111	1	4WCD	24X24	-	-	395	-	425	
COMMONS 111	2	4WCD	24X24	-	-	395	-	405	
COMMONS 111	3	4WCD	24X24	-	-	395	-	371	
COMMONS 111	4	4WCD	24X24	-	-	395	-	364	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-2	**PRIMARY MAXIMUM AIRFLOW CFM**	330	335	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	100	104	
SIZE	5Ø				
K STAND. / OFFSET	358 / 105.59				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 114	1	4WCD	24X24	-	-	165	-	162	
ROOM 114	2	4WCD	24X24	-	-	165	-	173	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

MANUFACTURER	PRICE		**DESIGN**	**ACTUAL**	
NUMBER	VAV-3-3	**PRIMARY MAXIMUM AIRFLOW CFM**	370	371	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	190	192	
SIZE	6Ø				
K STAND. / OFFSET	515 / -1.9				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 116	1	4WCD	24X24	-	-	185	-	182	
ROOM 116	2	4WCD	24X24	-	-	185	-	189	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-4	**PRIMARY MAXIMUM AIRFLOW CFM**	370	369	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	190	191	
SIZE	6Ø				
K STAND. / OFFSET	515 / -39.41				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 118	1	4WCD	24X24	-	-	185	-	180	
ROOM 118	2	4WCD	24X24	-	-	185	-	189	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-5	**PRIMARY MAXIMUM AIRFLOW CFM**	220	227	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	80	81	
SIZE	4Ø				
K STAND. / OFFSET	229 / 84.83				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
CORRIDOR	1	4WCD	24X24	-	-	170	-	175	
STORAGE 115	2	OED	6ϕ	-	-	50	-	52	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-6	**PRIMARY MAXIMUM AIRFLOW CFM**	360	350	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	100	102	
SIZE	6Ø				
K STAND. / OFFSET	515 / -16.37				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
OFFICE 119	1	4WCD	24X24	-	-	180	-	170	
OFFICE 119	2	4WCD	24X24	-	-	180	-	180	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-7	**PRIMARY MAXIMUM AIRFLOW CFM**	630	633	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	330	332	
SIZE	7Ø				
K STAND. / OFFSET	702 / -6.72				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 117	1	4WCD	24X24	-	-	210	-	212	
ROOM 117	2	4WCD	24X24	-	-	210	-	218	
ROOM 117	3	4WCD	24X24	-	-	210	-	203	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-8	**PRIMARY MAXIMUM AIRFLOW CFM**	630	624	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	330	333	
SIZE	7Ø				
K STAND. / OFFSET	702 / 14.72				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 113	1	4WCD	24X24	-	-	210	-	218	
ROOM 113	2	4WCD	24X24	-	-	210	-	208	
ROOM 113	3	4WCD	24X24	-	-	210	-	198	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-9	**PRIMARY MAXIMUM AIRFLOW CFM**	3750	3799	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	770	775	
SIZE	24X16				
K STAND. / OFFSET	6358 / 1191.47				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
OPEN AREA	1	LD	4'-0"	-	-	190	-	195	
OPEN AREA	2	LD	4'-0"	-	-	190	-	191	
OPEN AREA	3	LD	4'-0"	-	-	190	-	186	
OPEN AREA	4	LD	4'-0"	-	-	190	-	187	
OPEN AREA	5	LD	4'-0"	-	-	190	-	190	
OPEN AREA	6	LD	4'-0"	-	-	190	-	196	
OPEN AREA	7	LD	4'-0"	-	-	190	-	186	
OPEN AREA	8	LD	4'-0"	-	-	190	-	188	
OPEN AREA	9	LD	4'-0"	-	-	190	-	189	
OPEN AREA	10	LD	4'-0"	-	-	190	-	184	
OPEN AREA	11	LD	4'-0"	-	-	190	-	192	
OPEN AREA	12	LD	4'-0"	-	-	190	-	193	
OPEN AREA	13	LD	4'-0"	-	-	190	-	194	
OPEN AREA	14	LD	4'-0"	-	-	190	-	197	
OPEN AREA	15	LD	4'-0"	-	-	190	-	198	
OPEN AREA	16	LD	4'-0"	-	-	180	-	191	
OPEN AREA	17	LD	4'-0"	-	-	180	-	183	
OPEN AREA	18	LD	4'-0"	-	-	180	-	184	
OPEN AREA	19	LD	4'-0"	-	-	180	-	186	
OPEN AREA	20	LD	4'-0"	-	-	180	-	189	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-10	**PRIMARY MAXIMUM AIRFLOW CFM**	800	810	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	385	388	
SIZE	8Ø				
K STAND. / OFFSET	916 / 1.38				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 214	1	4WCD	24X24	-	-	270	-	260	
ROOM 214	2	4WCD	24X24	-	-	265	-	272	
ROOM 214	3	4WCD	24X24	-	-	265	-	278	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-11	**PRIMARY MAXIMUM AIRFLOW CFM**	800	809	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	385	386	
SIZE	8Ø				
K STAND. / OFFSET	916 / 56.59				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 216	1	4WCD	24X24	-	-	270	-	280	
ROOM 216	2	4WCD	24X24	-	-	265	-	256	
ROOM 216	3	4WCD	24X24	-	-	265	-	273	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-12	**PRIMARY MAXIMUM AIRFLOW CFM**	510	500	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	170	172	
SIZE	6Ø				
K STAND. / OFFSET	515 / -9.4				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 217	1	4WCD	24X24	-	-	255	-	260	
ROOM 217	2	4WCD	24X24	-	-	255	-	240	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-13	**PRIMARY MAXIMUM AIRFLOW CFM**	250	243	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	80	82	
SIZE	4Ø				
K STAND. / OFFSET	229 / 144.83				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
CORRIDOR	1	4WCD	24X24	-	-	200	-	190	
J.C. 215	2	OED	6ϕ	-	-	50	-	53	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-14	**PRIMARY MAXIMUM AIRFLOW CFM**	280	278	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	90	92	
SIZE	5Ø				
K STAND. / OFFSET	358 / 28.64				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
ROOM 209	1	4WCD	24X24	-	-	280	-	278	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

VAV TERMINAL UNIT TEST REPORT

(Pressure Independent)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

VAV TERMINAL DATA

			DESIGN	ACTUAL	
MANUFACTURER	PRICE				
NUMBER	VAV-3-15	**PRIMARY MAXIMUM AIRFLOW CFM**	200	205	
TYPE	SUPPLY	**PRIMARY MINIMUM AIRFLOW CFM**	80	82	
SIZE	4Ø				
K STAND. / OFFSET	229 / 133.41				

VAV OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
TOILET 200C	1	4WCD	24X24	-	-	50	-	52	
ROOM 212	2	4WCD	24X24	-	-	150	-	153	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: LEFRAK CITY BRANCH LIBRARY

SYSTEM / UNIT: RTU-4 (SUPPLY)

LOCATION: 95-15 HORACE HARDING EXPY
CORONA, NY 11368

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-4
MANUFACTURER	GREENHECK
MODEL NUMBER	RT-40-6.5L-0-G0
SERIAL NUMBER	28137415
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 56H
HP (KW)		2.0
RPM		1770
RATED VOLTS		460
RATED AMPS		2.9
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz AT VFD #1	60	59
OPERA. VOLTS L1/L2/L3 VFD #1	460	490/491/490
OPERA. AMPS L1/L2/L3 VFD #2	2.9	2.1/2.0/2.1

FAN DATA	DESIGN	ACTUAL
SUPPLY AIR CFM	2400	2467
OUTSIDE AIR CFM	1000	1050
EXTERNAL DISCHARGE S.P. in. w.g.	-	0.53
EXTERNAL SUCTION S.P. in. w.g.	-	-0.24
EXTERNAL S.P. in. w.g.	1.00	0.77
DIFF. S.P. in. w.g. @ FF/CC	-	0.42
TOTAL S.P. in. w.g.	1.79	1.19
FAN RPM #1	1717	1749

OTHER DATA	DESIGN	ACTUAL

NOTE: OAD: 35% OPEN, RAD: 65% OPEN AT BMS.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-4 (EXHAUST)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-4
MANUFACTURER	GREENHECK
MODEL NUMBER	AER-20-03-625-1.5HP
SERIAL NUMBER	206385536-0001 25K
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 145T
HP (KW)		1.5
RPM		1770
RATED VOLTS		460
RATED AMPS		2.3
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	24
OPERA. VOLTS L1/L2/L3	460	490/489/490
OPERA. AMPS L1/L2/L3	2.3	0.8/0.7/0.8

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	1000	1040
DISCHARGE S.P. in. w.g.	-	0.01
SUCTION S.P. in. w.g.	-	-0.12
TOTAL S.P. in. w.g.	0.50	0.13
FAN RPM	1380	708

OTHER DATA	DESIGN	ACTUAL

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-4 (EXHAUST-ECONOMIZER MODE)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-4
MANUFACTURER	GREENHECK
MODEL NUMBER	AER-20-03-625-1.5HP
SERIAL NUMBER	206385536-0001 25K
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 145T
HP (KW)		1.5
RPM		1770
RATED VOLTS		460
RATED AMPS		2.3
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	47
OPERA. VOLTS L1/L2/L3	460	490/489/490
OPERA. AMPS L1/L2/L3	2.3	1.5/1.6/1.5

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	2400	2430
DISCHARGE S.P. in. w.g.	-	0.01
SUCTION S.P. in. w.g.	-	-0.29
TOTAL S.P. in. w.g.	0.50	0.30
FAN RPM	1380	1387

OTHER DATA	DESIGN	ACTUAL

Rite T & B

AIR OUTLET TEST REPORT

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-4

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

AIR OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
FLEX SCI. LAB 205	1	SG	20X10	-	-	600	-	610	
FLEX SCI. LAB 205	2	SG	20X10	-	-	600	-	625	
FLEX SCI. LAB 205	3	SG	20X10	-	-	600	-	621	
FLEX SCI. LAB 205	4	SG	20X10	-	-	600	-	611	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: LEFRAK CITY BRANCH LIBRARY

SYSTEM / UNIT: RTU-5 (SUPPLY)

LOCATION: 95-15 HORACE HARDING EXPY
CORONA, NY 11368

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-5
MANUFACTURER	GREENHECK
MODEL NUMBER	RT-40-6.5L-0-G0
SERIAL NUMBER	28137490
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	WEG / 56H
HP (KW)		1.5
RPM		1760
RATED VOLTS		460
RATED AMPS		2.3
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz AT VFD #1	60	54
OPERA. VOLTS L1/L2/L3 VFD #1	460	490/491/490
OPERA. AMPS L1/L2/L3 VFD #2	2.3	1.9/2.0/1.9

FAN DATA	DESIGN	ACTUAL
SUPPLY AIR CFM	2000	2093
OUTSIDE AIR CFM	800	863
EXTERNAL DISCHARGE S.P. in. w.g.	-	0.74
EXTERNAL SUCTION S.P. in. w.g.	-	-0.19
EXTERNAL S.P. in. w.g.	1.00	0.93
DIFF. S.P. in. w.g. @ FF/CC	-	0.20
TOTAL S.P. in. w.g.	1.69	1.13
FAN RPM	1568	1592

OTHER DATA	DESIGN	ACTUAL

NOTE: OAD: 30% OPEN, RAD: 70% OPEN AT BMS.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-5 (EXHAUST)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-5
MANUFACTURER	GREENHECK
MODEL NUMBER	AER-20-03-625-1.5HP
SERIAL NUMBER	206386753-0001 25K
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 145T
HP (KW)		1.5
RPM		1770
RATED VOLTS		460
RATED AMPS		2.3
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	22
OPERA. VOLTS L1/L2/L3	460	490/489/490
OPERA. AMPS L1/L2/L3	2.3	0.8/0.7/0.8

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	800	832
DISCHARGE S.P. in. w.g.	-	0.01
SUCTION S.P. in. w.g.	-	-0.14
TOTAL S.P. in. w.g.	0.47	0.15
FAN RPM	1285	649

OTHER DATA	DESIGN	ACTUAL

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-5 (EXHAUST-ECOMIZER MODE)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-5
MANUFACTURER	GREENHECK
MODEL NUMBER	AER-20-03-625-1.5HP
SERIAL NUMBER	206386753-0001 25K
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 145T
HP (KW)		1.5
RPM		1770
RATED VOLTS		460
RATED AMPS		2.3
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	44
OPERA. VOLTS L1/L2/L3	460	490/489/490
OPERA. AMPS L1/L2/L3	2.3	1.3/1.4/1.3

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	2000	2032
DISCHARGE S.P. in. w.g.	-	0.01
SUCTION S.P. in. w.g.	-	-0.37
TOTAL S.P. in. w.g.	0.47	0.38
FAN RPM	1285	1300

OTHER DATA	DESIGN	ACTUAL

Rite T & B

AIR OUTLET TEST REPORT

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-5

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

AIR OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
SCI. LAB 207	1	SG	18X8	-	-	500	-	521	
SCI. LAB 207	2	SG	18X8	-	-	500	-	518	
SCI. LAB 207	3	SG	18X8	-	-	500	-	526	
SCI. LAB 207	4	SG	18X8	-	-	500	-	528	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: LEFRAK CITY BRANCH LIBRARY

SYSTEM / UNIT: RTU-6 (SUPPLY)

LOCATION: 95-15 HORACE HARDING EXPY CORONA, NY 11368

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-6
MANUFACTURER	GREENHECK
MODEL NUMBER	RT-40-6.5L-0-G0
SERIAL NUMBER	28137535
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	WEG / 56H
HP (KW)		2.0
RPM		1770
RATED VOLTS		460
RATED AMPS		2.9
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz AT VFD #1	60	59
OPERA. VOLTS L1/L2/L3 VFD #1	460	490/491/491
OPERA. AMPS L1/L2/L3 VFD #2	2.9	2.0/2.1/2.0

FAN DATA	DESIGN	ACTUAL
SUPPLY AIR CFM	2400	2496
OUTSIDE AIR CFM	800	871
EXTERNAL DISCHARGE S.P. in. w.g.	-	0.74
EXTERNAL SUCTION S.P. in. w.g.	-	-0.38
EXTERNAL S.P. in. w.g.	1.00	1.12
DIFF. S.P. in. w.g. @ FF/CC	-	0.20
TOTAL S.P. in. w.g.	1.79	1.32
FAN RPM	1717	1749

OTHER DATA	DESIGN	ACTUAL

NOTE: OAD: 30% OPEN, RAD: 70% OPEN AT BMS.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-6 (EXHAUST)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-6
MANUFACTURER	GREENHECK
MODEL NUMBER	AER-20-03-625-1.5HP
SERIAL NUMBER	206385719-0001 25K
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 145T
HP (KW)		1.5
RPM		1770
RATED VOLTS		460
RATED AMPS		2.3
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	28.5
OPERA. VOLTS L1/L2/L3	460	490/489/490
OPERA. AMPS L1/L2/L3	2.3	0.8/0.9/0.8

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	800	842
DISCHARGE S.P. in. w.g.	-	0.01
SUCTION S.P. in. w.g.	-	-0.26
TOTAL S.P. in. w.g.	0.50	0.27
FAN RPM	1380	842

OTHER DATA	DESIGN	ACTUAL

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-6 (EXHAUST-ECOMIZER MODE)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-6
MANUFACTURER	GREENHECK
MODEL NUMBER	AER-20-03-625-1.5HP
SERIAL NUMBER	206385719-0001 25K
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 145T
HP (KW)		1.5
RPM		1770
RATED VOLTS		460
RATED AMPS		2.3
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	47
OPERA. VOLTS L1/L2/L3	460	490/489/490
OPERA. AMPS L1/L2/L3	2.3	1.4/1.5/1.5

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	2400	2460
DISCHARGE S.P. in. w.g.	-	0.01
SUCTION S.P. in. w.g.	-	0.49
TOTAL S.P. in. w.g.	0.50	0.50
FAN RPM	1380	1390

OTHER DATA	DESIGN	ACTUAL

Rite T & B

AIR OUTLET TEST REPORT

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-6

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

AIR OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
SCI. LAB 211	1	SG	20X10	-	-	600	-	613	
SCI. LAB 211	2	SG	20X10	-	-	600	-	621	
SCI. LAB 211	3	SG	20X10	-	-	600	-	628	
SCI. LAB 211	4	SG	20X10	-	-	600	-	634	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: LEFRAK CITY BRANCH LIBRARY

SYSTEM / UNIT: RTU-7 (SUPPLY)

LOCATION: 95-15 HORACE HARDING EXPY
CORONA, NY 11368

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-7
MANUFACTURER	GREENHECK
MODEL NUMBER	RT-40-6.5L-0-G0
SERIAL NUMBER	28137433
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 56H
HP (KW)		2.0
RPM		1770
RATED VOLTS		460
RATED AMPS		2.9
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz AT VFD #1	60	59
OPERA. VOLTS L1/L2/L3 VFD #1	460	490/491/490
OPERA. AMPS L1/L2/L3 VFD #2	2.9	2.1/2.0/2.0

FAN DATA	DESIGN	ACTUAL
SUPPLY AIR CFM	2400	2502
OUTSIDE AIR CFM	1000	1075
EXTERNAL DISCHARGE S.P. in. w.g.	-	0.64
EXTERNAL SUCTION S.P. in. w.g.	-	-0.23
EXTERNAL S.P. in. w.g.	1.00	0.87
DIFF. S.P. in. w.g. @ FF/CC	-	0.37
TOTAL S.P. in. w.g.	1.79	1.24
FAN RPM	1717	1750

OTHER DATA	DESIGN	ACTUAL

NOTE: OAD: 35% OPEN, RAD: 65% OPEN AT BMS.

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-7 (EXHAUST)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-7
MANUFACTURER	GREENHECK
MODEL NUMBER	AER-20-03-625-1.5HP
SERIAL NUMBER	206385479-0001 25K
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 145T
HP (KW)		1.5
RPM		1770
RATED VOLTS		460
RATED AMPS		2.3
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	23.5
OPERA. VOLTS L1/L2/L3	460	490/489/490
OPERA. AMPS L1/L2/L3	2.3	0.8/0.9/0.8

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	1000	1067
DISCHARGE S.P. in. w.g.	-	0.01
SUCTION S.P. in. w.g.	-	-0.15
TOTAL S.P. in. w.g.	0.50	0.16
FAN RPM	1380	695

OTHER DATA	DESIGN	ACTUAL

Rite T & B

AIR HANDLING UNIT TEST REPORT

(Packaged / Unitary Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: RTU-7 (EXHAUST-ECONOMIZER MODE)

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

UNIT DATA	
UNIT DESIGNATION	RTU-7
MANUFACTURER	GREENHECK
MODEL NUMBER	AER-20-03-625-1.5HP
SERIAL NUMBER	206385479-0001 25K
LOCATION	ROOF

MOTOR DATA	DESIGN	ACTUAL
MAKE / FRAME	MOTOR NAME PLATE DATA ➔	BALDOR / 145T
HP (KW)		1.5
RPM		1770
RATED VOLTS		460
RATED AMPS		2.3
RATED PHASE		3
RATED Hz		60
SERVICE FACTOR		1.15
OPERATING Hz	60	47
OPERA. VOLTS L1/L2/L3	460	490/489/490
OPERA. AMPS L1/L2/L3	2.3	1.6/1.7/1.6

FAN DATA	DESIGN	ACTUAL
EXHAUST AIR CFM	2400	2496
DISCHARGE S.P. in. w.g.	-	0.01
SUCTION S.P. in. w.g.	-	-0.50
TOTAL S.P. in. w.g.	0.50	0.51
FAN RPM	1380	1388

OTHER DATA	DESIGN	ACTUAL

Rite T & B

AIR OUTLET TEST REPORT

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: RTU-7

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

AIR OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
SCI. LAB 213	1	SG	20X10	-	-	600	-	616	
SCI. LAB 213	2	SG	20X10	-	-	600	-	625	
SCI. LAB 213	3	SG	20X10	-	-	600	-	627	
SCI. LAB 213	4	SG	20X10	-	-	600	-	634	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

FAN TEST REPORT
(Belt Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: LHEF-1, LHEF-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

FAN DATA	FAN NO.		FAN NO.		FAN NO.	
UNIT DESIGNATION	LHEF-1		LHEF-2			
TYPE OF SERVICE	EXHAUST		EXHAUST			
MANUFACTURER	GREENHECK		GREENHECK			
MODEL NUMBER	FJI-07-BI-21-10-0-M10-X		FJI-07-BI-21-10-0-M10-X			
SERIAL NUMBER	28707971 26B		28707979 26B			
TEST DATA	**DESIGN**	**ACTUAL**	**DESIGN**	**ACTUAL**	**DESIGN**	**ACTUAL**
TOTAL AIRFLOW CFM	475	498	475	513		
FAN SUCTION SP in. w.g.		-0.38		-0.39		
FAN DISCHARGE SP in. w.g.		0.18		0.19		
TOTAL SP or ESP in. w.g.	1.00	0.56	1.00	0.57		
MOTOR HP (KW)	MOTOR NAME PLATE DATA ➔	1.0	MOTOR NAME PLATE DATA ➔	1.0	MOTOR NAME PLATE DATA ➔	
MOTOR RPM		3450		3450		
MOTOR RATED VOLTS		208		208		
MOTOR RATED AMPS		3.1		3.1		
MOTOR RATED PHASE		3		3		
MOTOR RATED HZ		60		60		
MOTOR SERVICE FACTOR		1.15		1.15		
FRAME		56H		56H		
MOTOR SHEAVE OD	ACTUAL INSTALLED DRIVE DATA ➔	2 3/4"	ACTUAL INSTALLED DRIVE DATA ➔	2 3/4"	ACTUAL INSTALLED DRIVE DATA ➔	
MOTOR SHEAVE BORE		5/8"		5/8"		
FAN SHEAVE OD		3 1/2"		3 1/2"		
FAN SHEAVE BORE		1"		1"		
SHEAVE CENTER DISTANCE		9"		9"		
NUMBER OF BELTS		1		1		
BELT SIZE		AX27		AX27		
FAN RPM	2734	2743	2734	2740		
OPERATING VOLTAGE L1/L2/L3	208	209/208/209	208	209/208/209		
OPERATING AMPS T1/T2/T3	3.1	2.2/2.1/2.2	3.1	2.1/2.1/2.2		
VFD OPERATING HZ	60	60	60	60		

Rite T & B

FUME HOOD TEST REPORT

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: LHEF-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

FUME HOOD DATA

AREA SERVED	OUTLET				DESIGN	FINAL	
	NO	TYPE	SIZE	SASH	VEL (FPM)	VEL (FPM)	
SCI. LAB 207	1	HOOD	38"	18"	100	105	

Rite T & B

FUME HOOD TEST REPORT

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: LHEF-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

FUME HOOD DATA

AREA SERVED	OUTLET				DESIGN	FINAL	
	NO	TYPE	SIZE	SASH	VEL (FPM)	VEL (FPM)	
SCI. LAB 211	1	HOOD	38"	18"	100	108	

Rite T & B

FAN TEST REPORT

(Direct Drive) > 1/8 hp

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: LHEF-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

FAN DATA	FAN NO.		FAN NO.		FAN NO.	
UNIT DESIGNATION	LHEF-3					
TYPE OF SERVICE	EXHAUST					
MANUFACTURER	GREENHECK					
MODEL NUMBER	USF-15-5-B7-00-02-02					
SERIAL NUMBER	28853974 26B					
TEST DATA	**DESIGN**	**ACTUAL**	**DESIGN**	**ACTUAL**	**DESIGN**	**ACTUAL**
TOTAL AIRFLOW CFM	1900	2004				
FAN SUCTION SP in. w.g.	-	-0.45	-		-	
FAN DISCHARGE SP in. w.g.	-	0.19	-		-	
TOTAL SP or ESP in. w.g.	1.00	0.64				
MOTOR HP (KW)	MOTOR NAME PLATE DATA ➔	1.5	MOTOR NAME PLATE DATA ➔		MOTOR NAME PLATE DATA ➔	
MOTOR RPM		1755				
MOTOR RATED VOLTS		230				
MOTOR RATED AMPS		4.1				
MOTOR RATED PHASE		3				
MOTOR RATED HZ		60				
OPERATING VOLTAGE L1/L2/L3	230	208/209/209				
OPERATING AMPS T1/T2/T3	4.1	3.6/3.7/3.7				
OPERATING HZ	60	60				
FAN RPM	1309	1713				

Rite T & B

FUME HOOD TEST REPORT

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: LHEF-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

FUME HOOD DATA

AREA SERVED	OUTLET				DESIGN	FINAL	
	NO	TYPE	SIZE	SASH	VEL (FPM)	VEL (FPM)	
SCI. LAB 213	1	HOOD	38"	18"	100	108	
SCI. LAB 213	2	HOOD	38"	18"	100	107	
SCI. LAB 213	3	HOOD	38"	18"	100	106	
SCI. LAB 213	4	HOOD	38"	18"	100	101	

Rite T & B

FAN TEST REPORT
(Direct Drive)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: EF-1, EF-2, EF-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

FAN DATA	FAN NO.		FAN NO.		FAN NO.	
UNIT DESIGNATION	EF-1		EF-2		EF-3	
TYPE OF SERVICE	EXHAUST		EXHAUST		EXHAUST	
MANUFACTURER	GREENHECK		GREENHECK		GREENHECK	
MODEL NUMBER	G-095-VG-1-17-X		G-070-VG-1-17-X		G-060-VG-1-17-X	
SERIAL NUMBER	28394929 25L		28394930 25L		28394931 25L	
TEST DATA	**DESIGN**	**ACTUAL**	**DESIGN**	**ACTUAL**	**DESIGN**	**ACTUAL**
TOTAL AIRFLOW CFM	525	495	200	186	60	55
FAN SUCTION SP in. w.g.	-	-0.58	-	-0.06	-	-0.05
FAN DISCHARGE SP in. w.g.	-	0.00	-	0.00	-	0.00
TOTAL SP or ESP in. w.g.	0.38	0.58	0.38	0.06	0.30	0.05
MOTOR HP (KW)	MOTOR NAME PLATE DATA ➔	1/6	MOTOR NAME PLATE DATA ➔	1/15	MOTOR NAME PLATE DATA ➔	1/15
MOTOR RPM		1750		1750		1750
MOTOR RATED VOLTS		115		115		115
MOTOR RATED AMPS		2.2		1.3		1.3
MOTOR RATED PHASE		1		1		1
MOTOR RATED HZ		60		60		60
OPERATING VOLTAGE L1/L2/L3	115	121	115	120	115	121
OPERATING AMPS T1/T2/T3	2.2	1.7	2.2	0.4	2.2	0.3
FAN RPM	1335	1380	1580	1598	1449	1486

Rite T & B

AIR OUTLET TEST REPORT

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: EF-1

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

AIR OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
BOYS TOI. G-100C	1	EG	12X12	-	-	200	-	182	
GIRLS TOI. G-100B	2	EG	12X12	-	-	200	-	187	
STORAGE G-105	3	EG	6X6	-	-	25	-	27	
DATA G-106	4	EG	6X6	-	-	25	-	26	
ELECTRICAL G-107	5	EG	6X6	-	-	25	-	25	
J.C. RM. 112	6	EG	8X8	-	-	50	-	48	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

AIR OUTLET TEST REPORT

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: EF-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

AIR OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
STAFF TOI. A-200B	1	EG	12X12	-	-	50	-	46	
NEU. TOI. A-200A	2	EG	12X12	-	-	50	-	48	
STAFF TOI. 100A	3	EG	12X12	-	-	50	-	47	
TOILET	4	EG	12X12	-	-	50	-	45	

* NOTE: IF AK=1.00, velocity information and measurement are not required.

Rite T & B

AIR OUTLET TEST REPORT

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: EF-3

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 06/17/2026

AIR OUTLET DATA

AREA SERVED	OUTLET				DESIGN		FINAL		
	NO	TYPE	SIZE	AK*	VEL	FLOW	VEL	FLOW	
STAFF TOI. A-200C	1	EG	12X12	-	-	60	-	55	


* NOTE: IF AK=1.00, velocity information and measurement are not required.

SKETCHING NOTES

XXxXX NEW DUCTWORK

KEYED-IN NOTES

1. INSTALL UH AS HIGH AS POSSIBLE.
2. 6" BOILER FLUE UP. PROVIDE AL-29C STAINLESS STEEL VENT SUITABLE FOR POSITIVE PRESSURE VENT SYSTEMS AND CONDENSING APPLICATIONS MODEL SSID MANUFACTURED BY SECURITY CHIMNEYS. FLUE SHALL BE INSTALLED IN STRICT ACCORDANCE WITH THE MANUFACTURER'S INSTALLATION MANUAL (TYP 2)
3. 4" PVC BOILER COMBUSTION AIR UP. PROVIDE OFFSETS AS REQUIRED. (TYP 2)
4. 3" HOT WATER HEATER FLUE UP. PROVIDE AL-29C STAINLESS STEEL VENT SUITABLE FOR POSITIVE PRESSURE VENT SYSTEMS AND CONDENSING APPLICATIONS MODEL SSID MANUFACTURED BY SECURITY CHIMNEYS. FLUE SHALL BE INSTALLED IN STRICT ACCORDANCE WITH THE MANUFACTURER'S INSTALLATION MANUAL. (TYP 2)
5. 3" PVC HOT WATER HEATER COMBUSTION AIR UP. PROVIDE OFFSETS AS REQUIRED. (TYP 2)

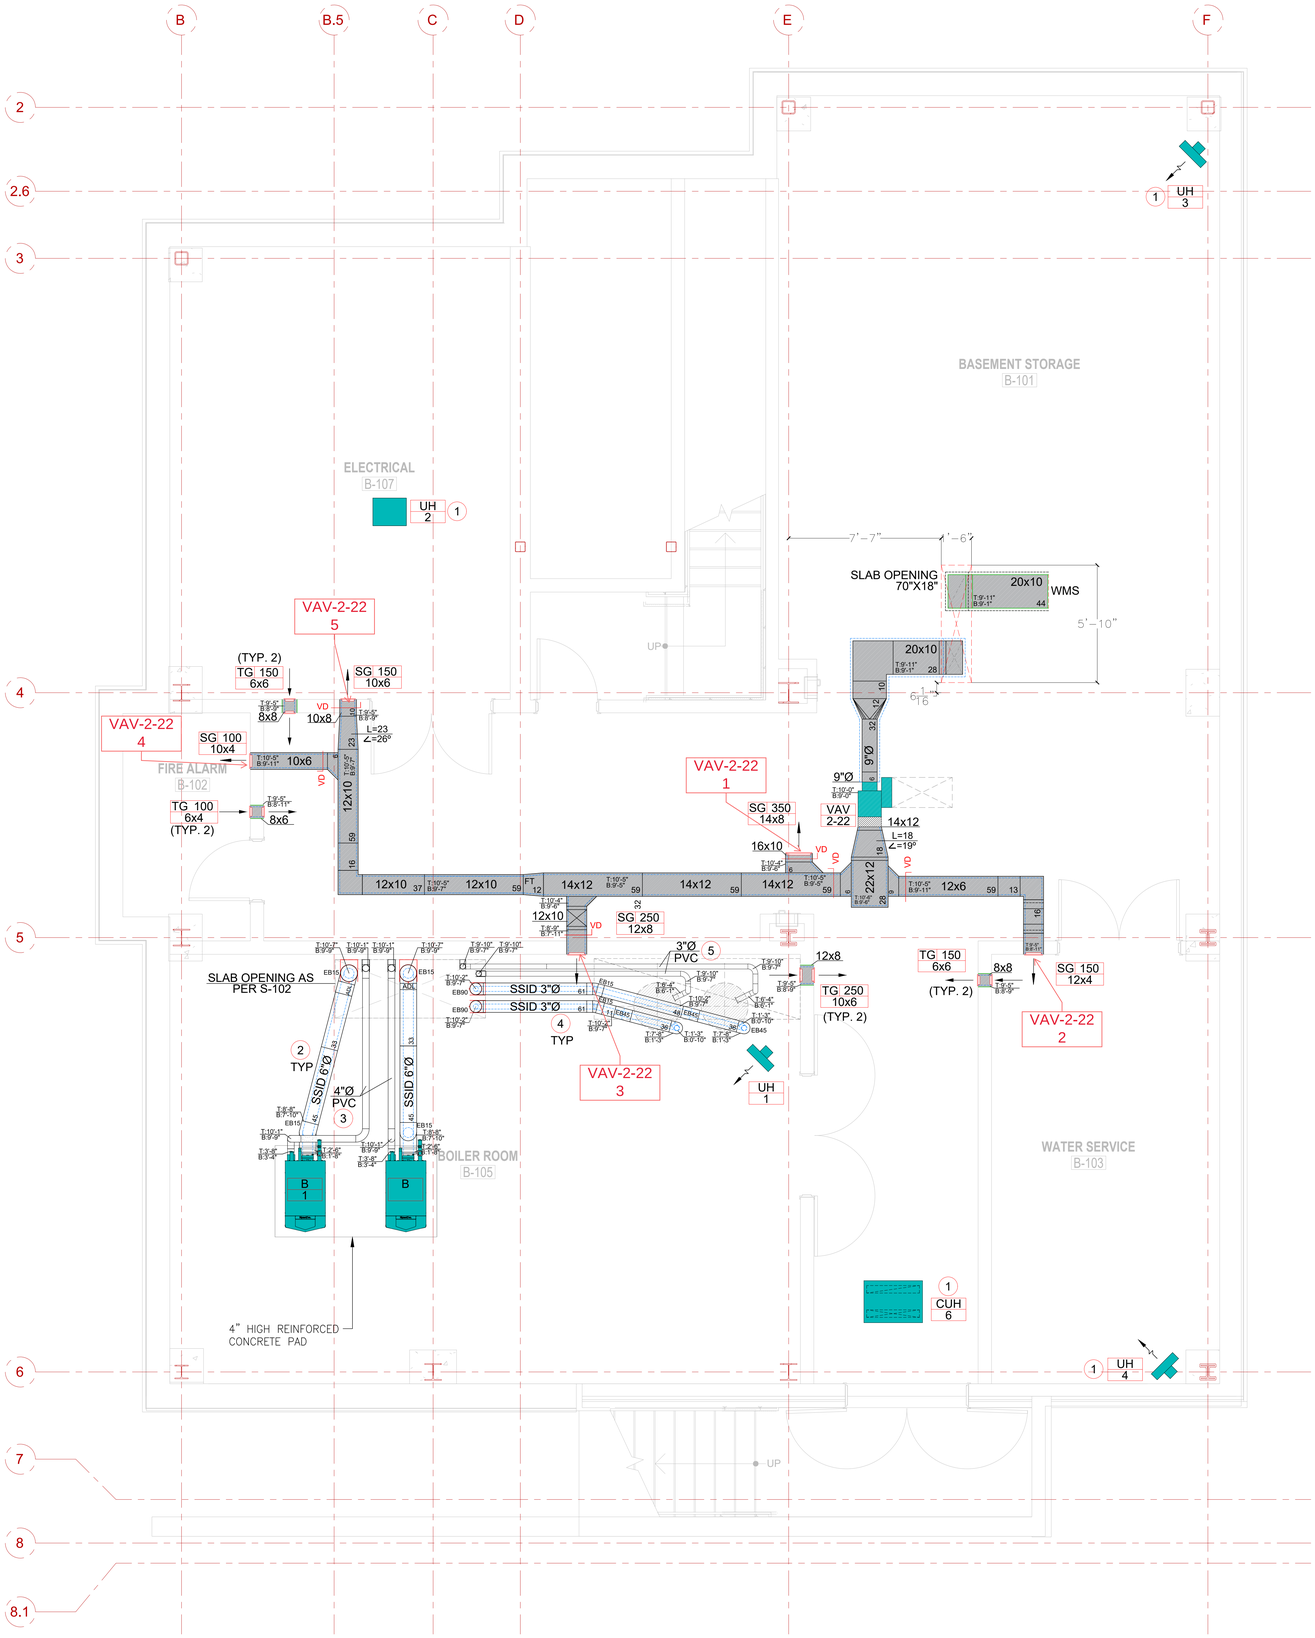

1 MECHANICAL DUCTWORK PLAN - BASEMENT PLAN
3/8" = 1'-0"

NORTHERN WOLVES AIR CONDITIONING


NORTHERN WOLVES AC
55 9TH STREET, 55A2
SUITE 182
BROOKLYN, NY 11215

Revisions
REV-1 – REVIEW AS PER ENGINEER'S COMMENTS – 09/23/2025

SADDLE RIVER DAY SCHOOL
147 CHESTBUT RIDGE RD
SADDLE RIVER, NJ 07458

M-101.SD
MECHANICAL
BASEMENT PLAN
DUCTWORK

Proj. No.
Drawn By
Date 10/22/2025
Checked By

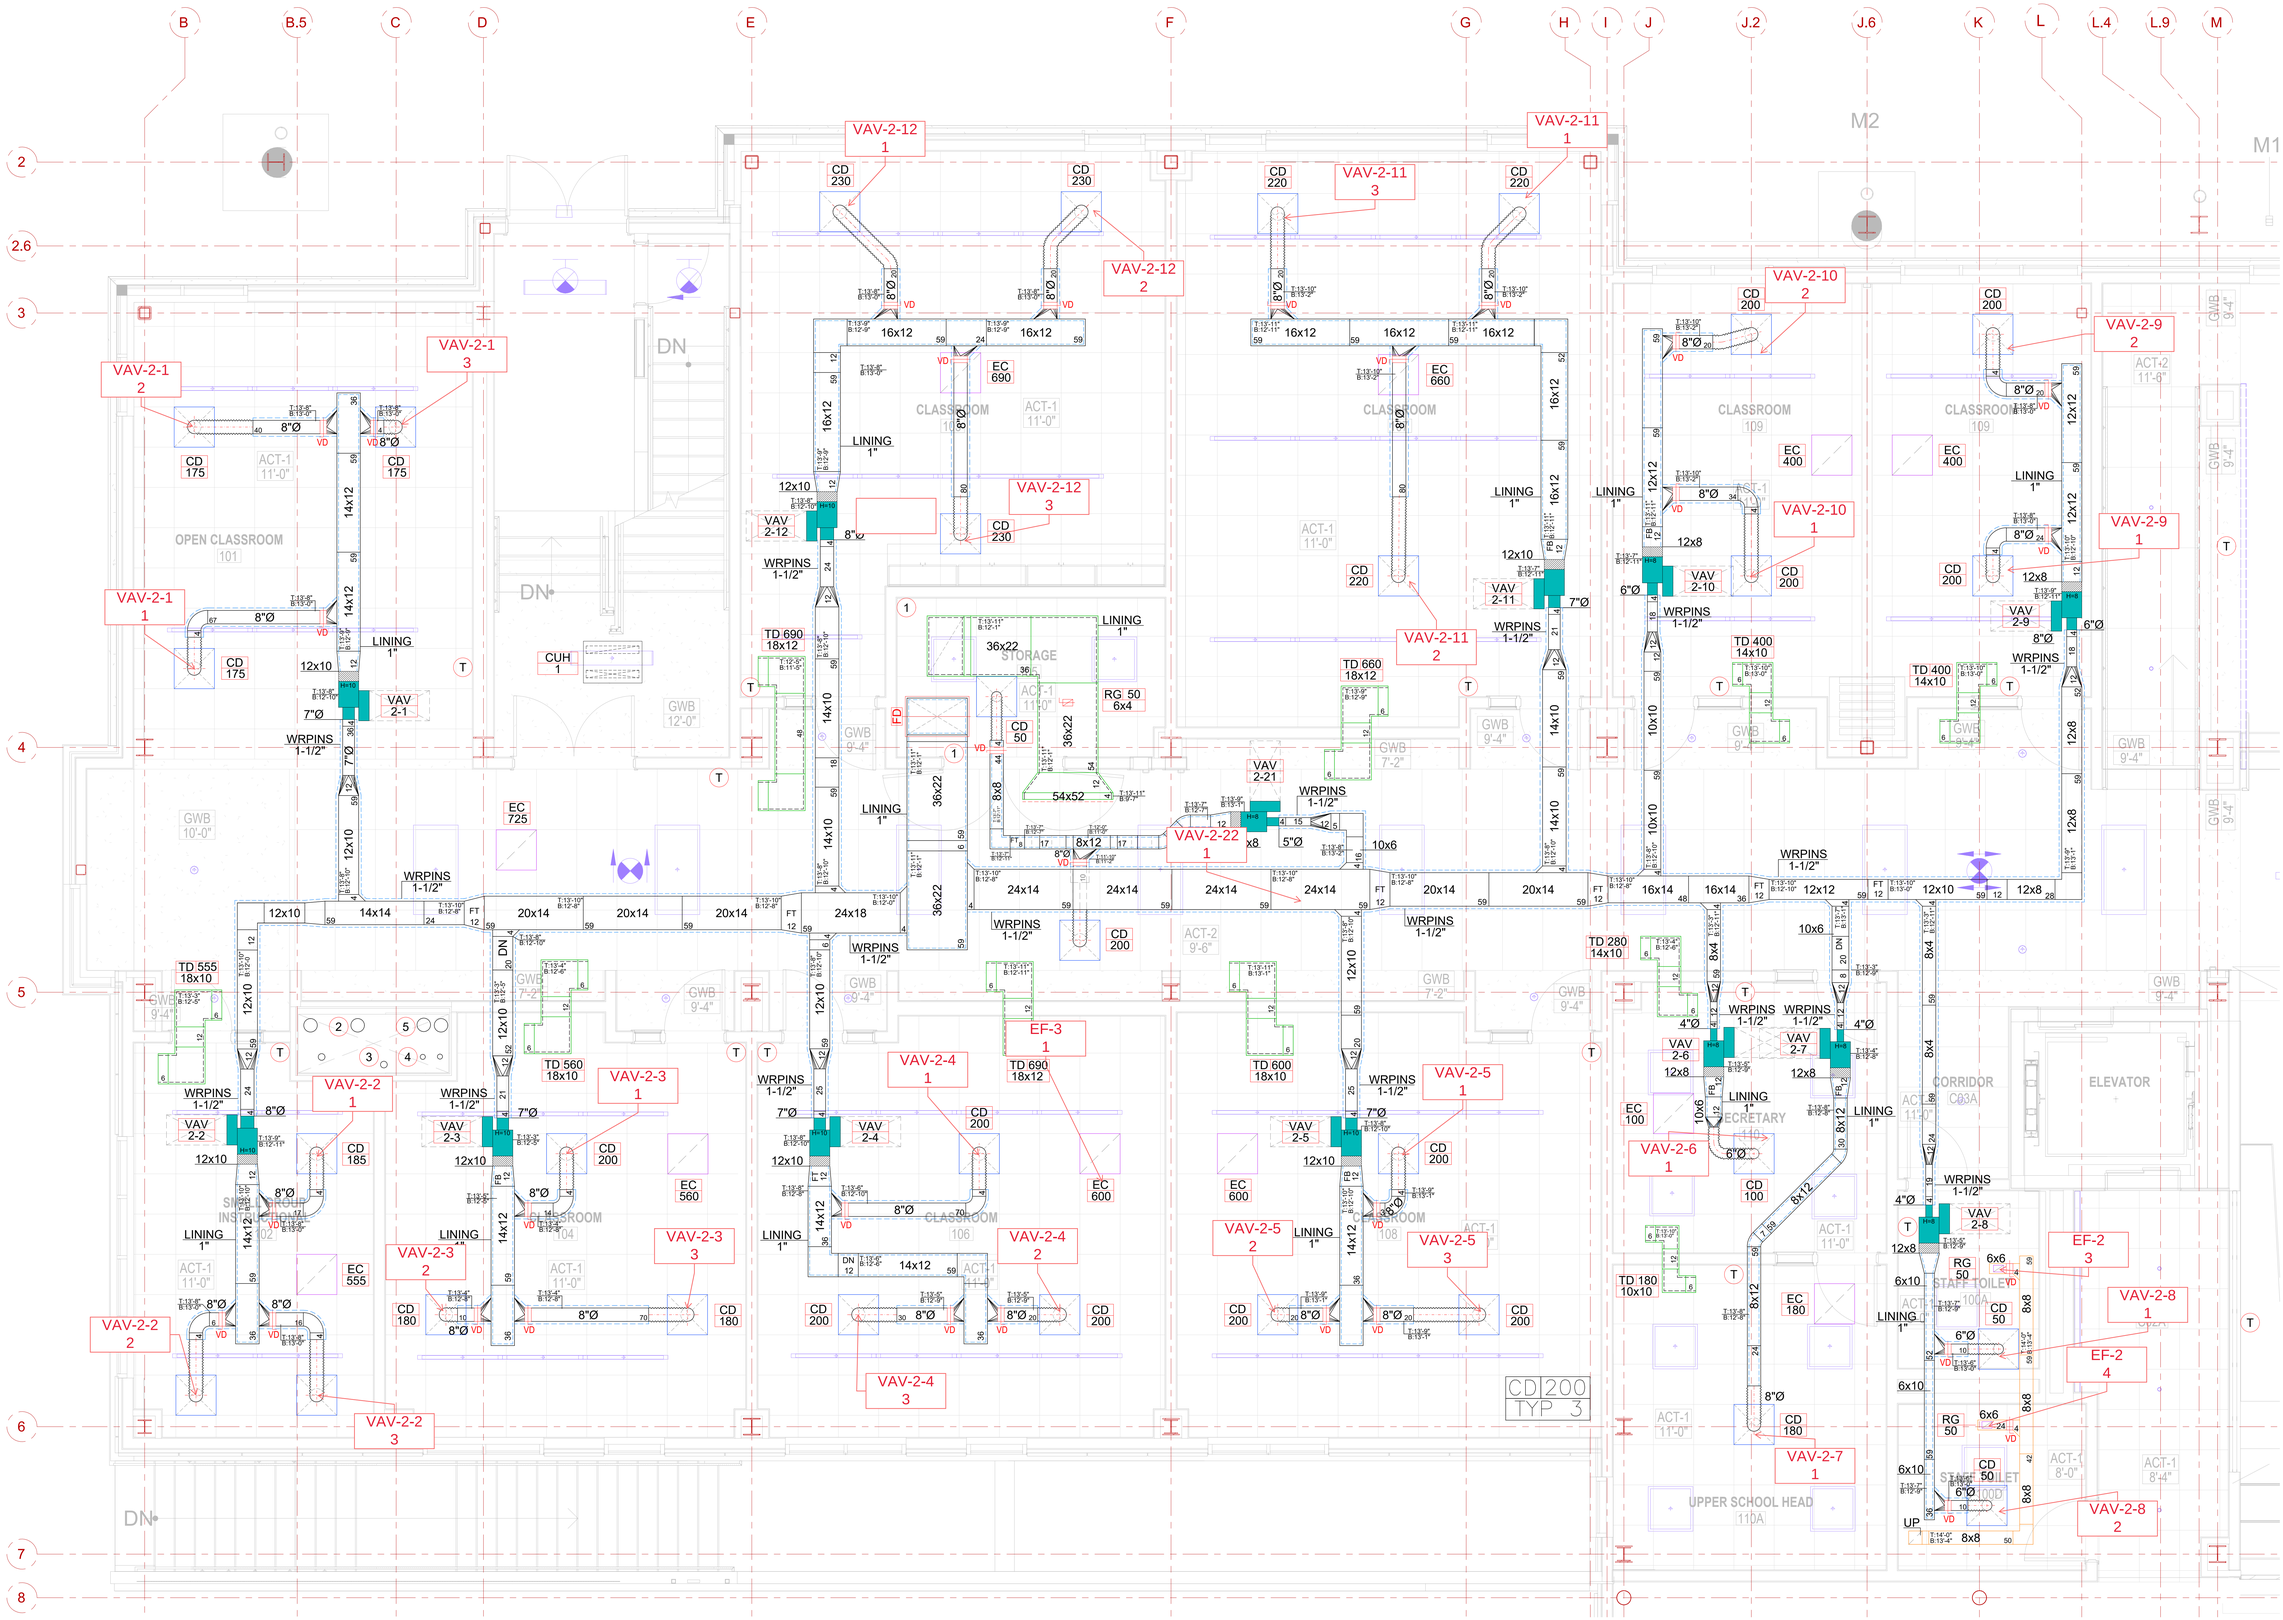

1 MECHANICAL DUCTWORK PLAN - LOWER LEVEL FLOOR PLAN
3/8" = 1'-0"

GENERAL NOTES:

1. 1" ACOUSTIC LINING 15FT DOWNSTREAM FOR VAV'S
2. 1 1/2" R6 WRAP INSULATION FOR SUPPLY AND RETURN DUCTWORK.
3. 1" ACOUSTIC LINING FOR TRANSFER DUCTS.


NORTHERN WOLVES AIR CONDITIONING
NORTHERN WOLVES AC
55 9TH STREET, 55A2
SUITE 182
BROOKLYN, NY 11215

Revisions
REV-1 – REVIEW AS PER ARCHITECT AND ENGINEER COMMENTS 09/29/2025 AND COORDINATION DRAWINGS 10/20/2025
REV-2 – AS PER SPECIALTY CLASSROOM DUCT REV. 11/05/2025

SADDLE RIVER DAY SCHOOL
147 CHESTNUT RIDGE RD.
SADDLE RIVER, NJ 07458

M-102A.SD
MECHANICAL
LOWER LEVEL FLOOR PLAN
DUCTWORK

Proj. No. | Drawn By:
Date: 11/24/2025 | Checked By:

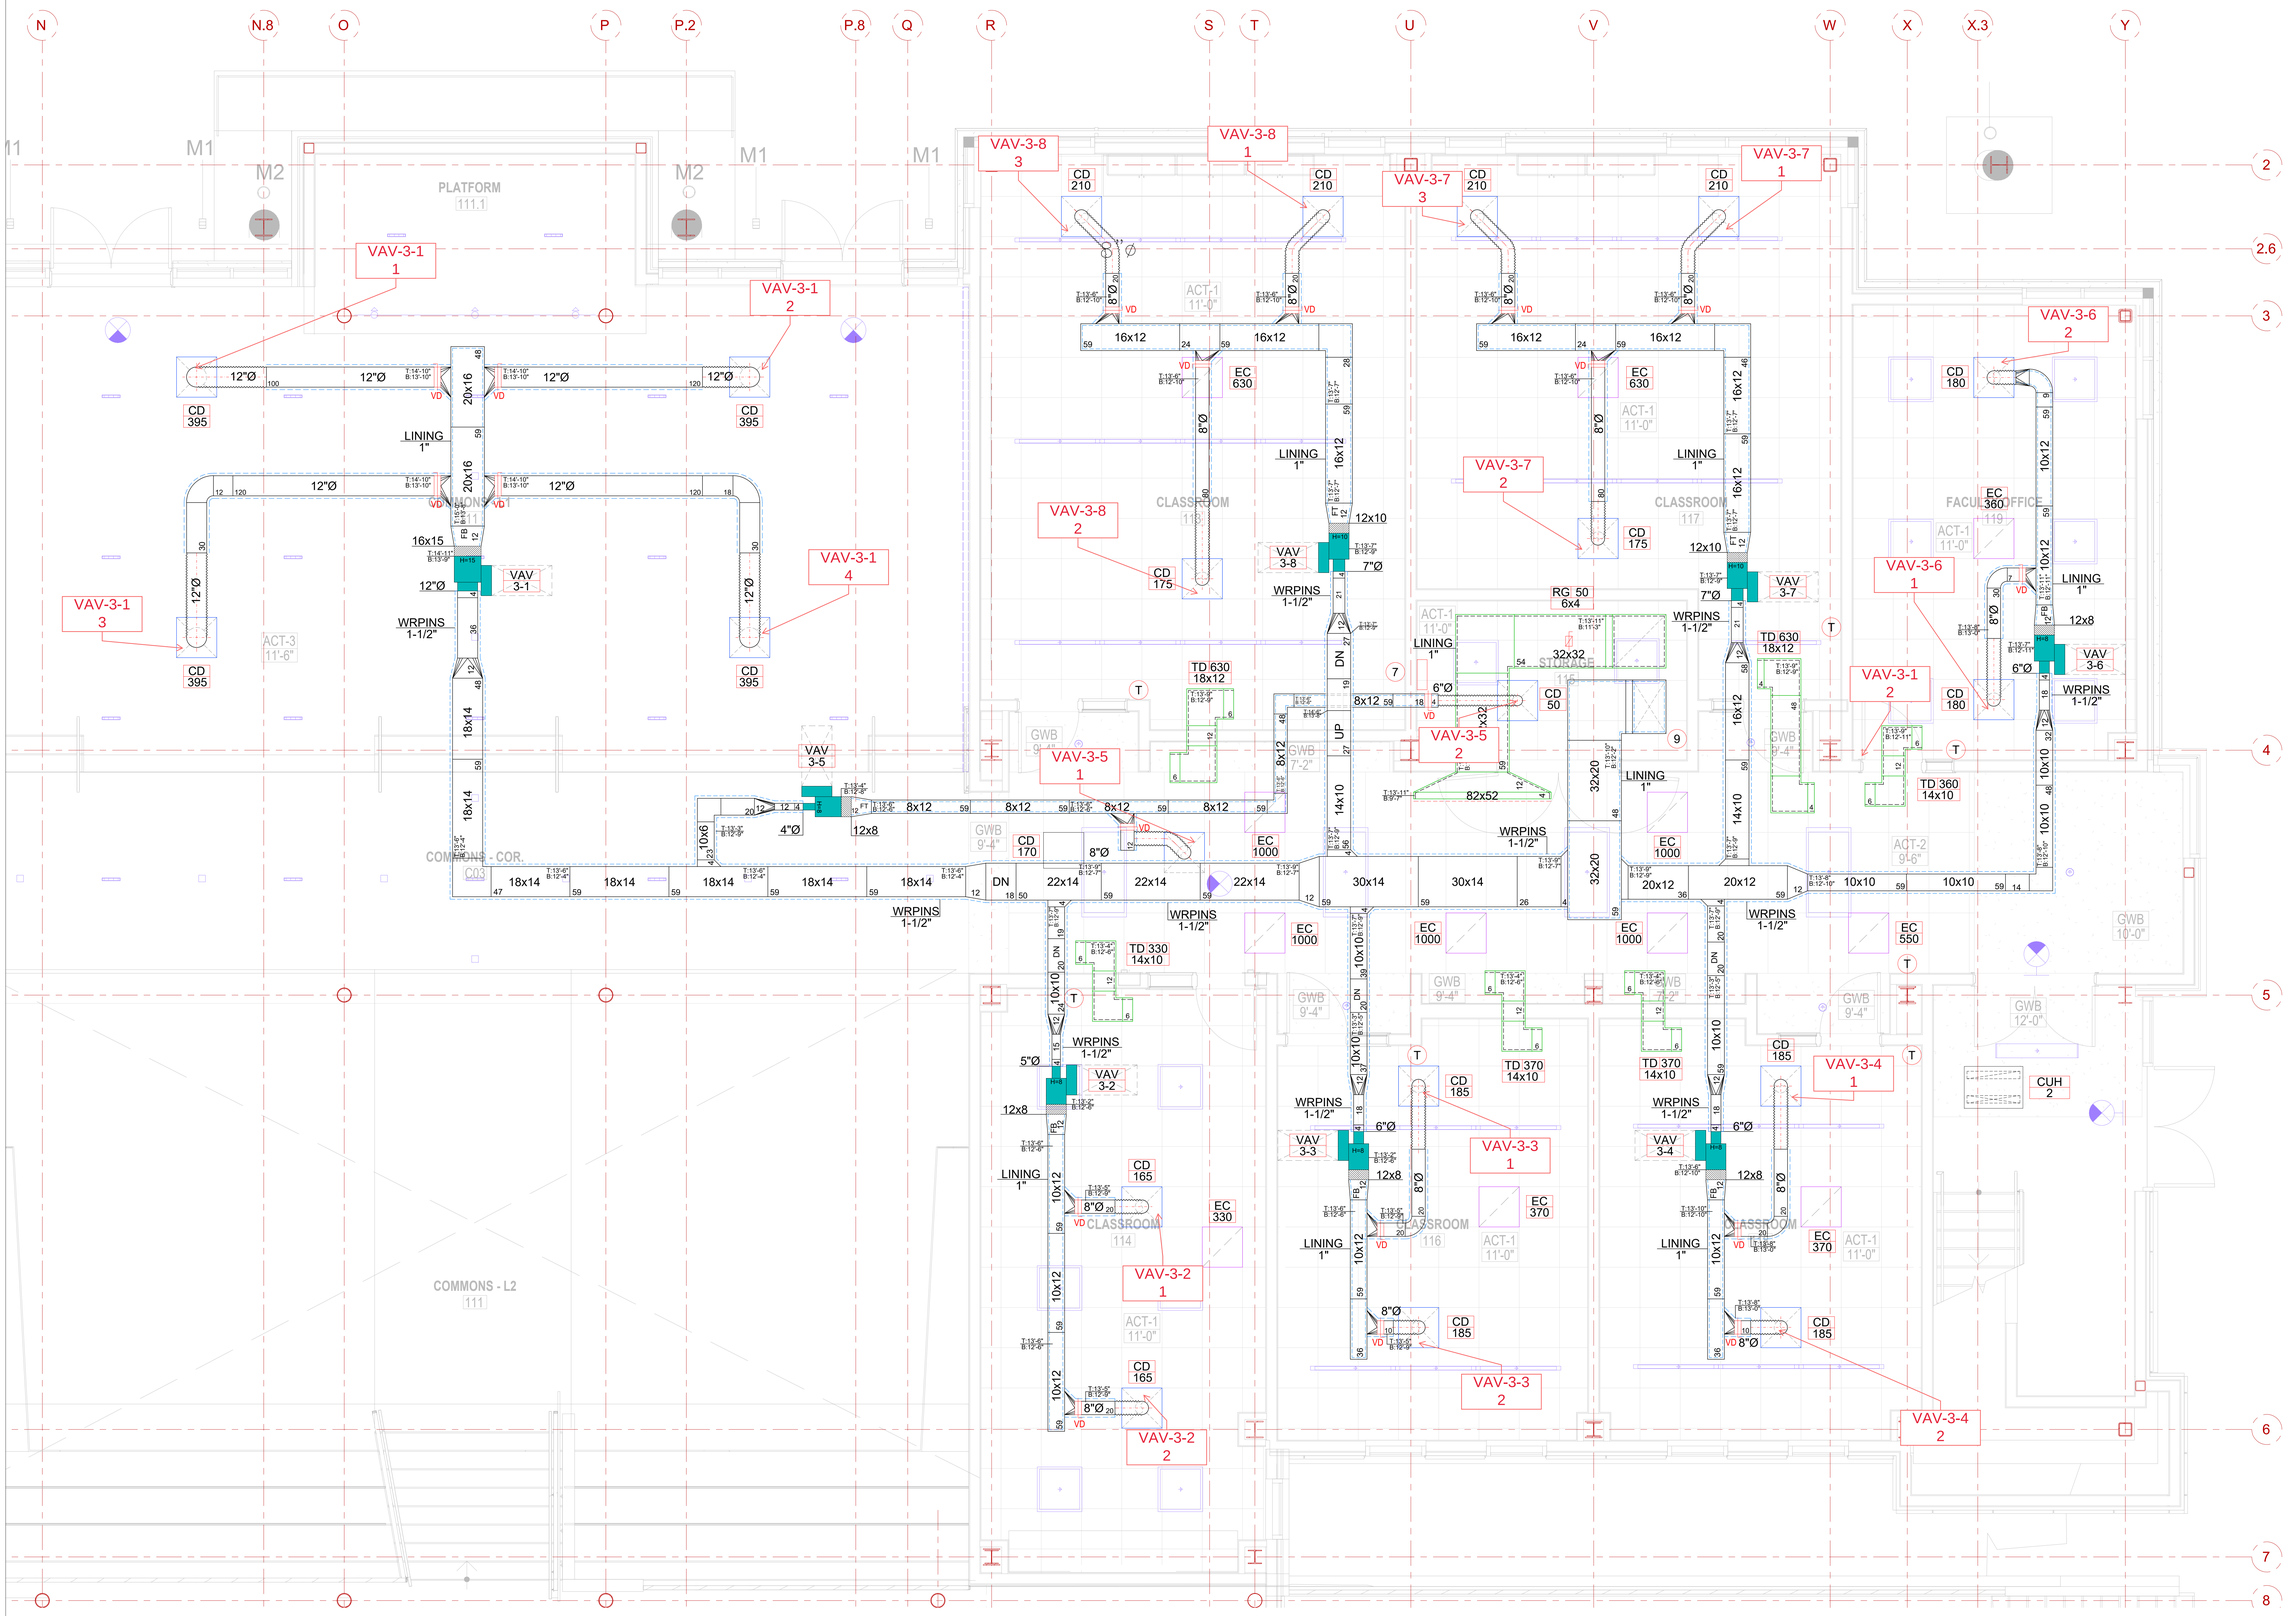

2 MECHANICAL DUCTWORK PLAN - LOWER LEVEL FLOOR PLAN
3/8" = 1'-0"

GENERAL NOTES:

1. 1" ACOUSTIC LINING 15FT DOWNSTREAM FOR VAV'S
2. 1 1/2" R6 WRAP INSULATION FOR SUPPLY AND RETURN DUCTWORK.
3. 1" ACOUSTIC LINING FOR TRANSFER DUCTS.

NORTHERN WOLVES AIR CONDITIONING


NORTHERN WOLVES AC
55 9TH STREET, 55A2
SUITE 182
BROOKLYN, NY 11215

Revisions
REV-1 – REVIEW AS PER ARCHITECT AND ENGINEER COMMENTS 09/29/2025 AND COORDINATION DRAWINGS 10/20/2025
REV-2 – AS PER SPECIALTY CLASSROOM DUCT REV. 11/05/2025

SADDLE RIVER DAY SCHOOL
147 CHESTNUT RIDGE RD.
SADDLE RIVER, NJ 07458

M-102B.SD
MECHANICAL
LOWER LEVEL FLOOR PLAN
DUCTWORK

Proj. No. | Drawn By
Date 11/24/2025 | Checked By

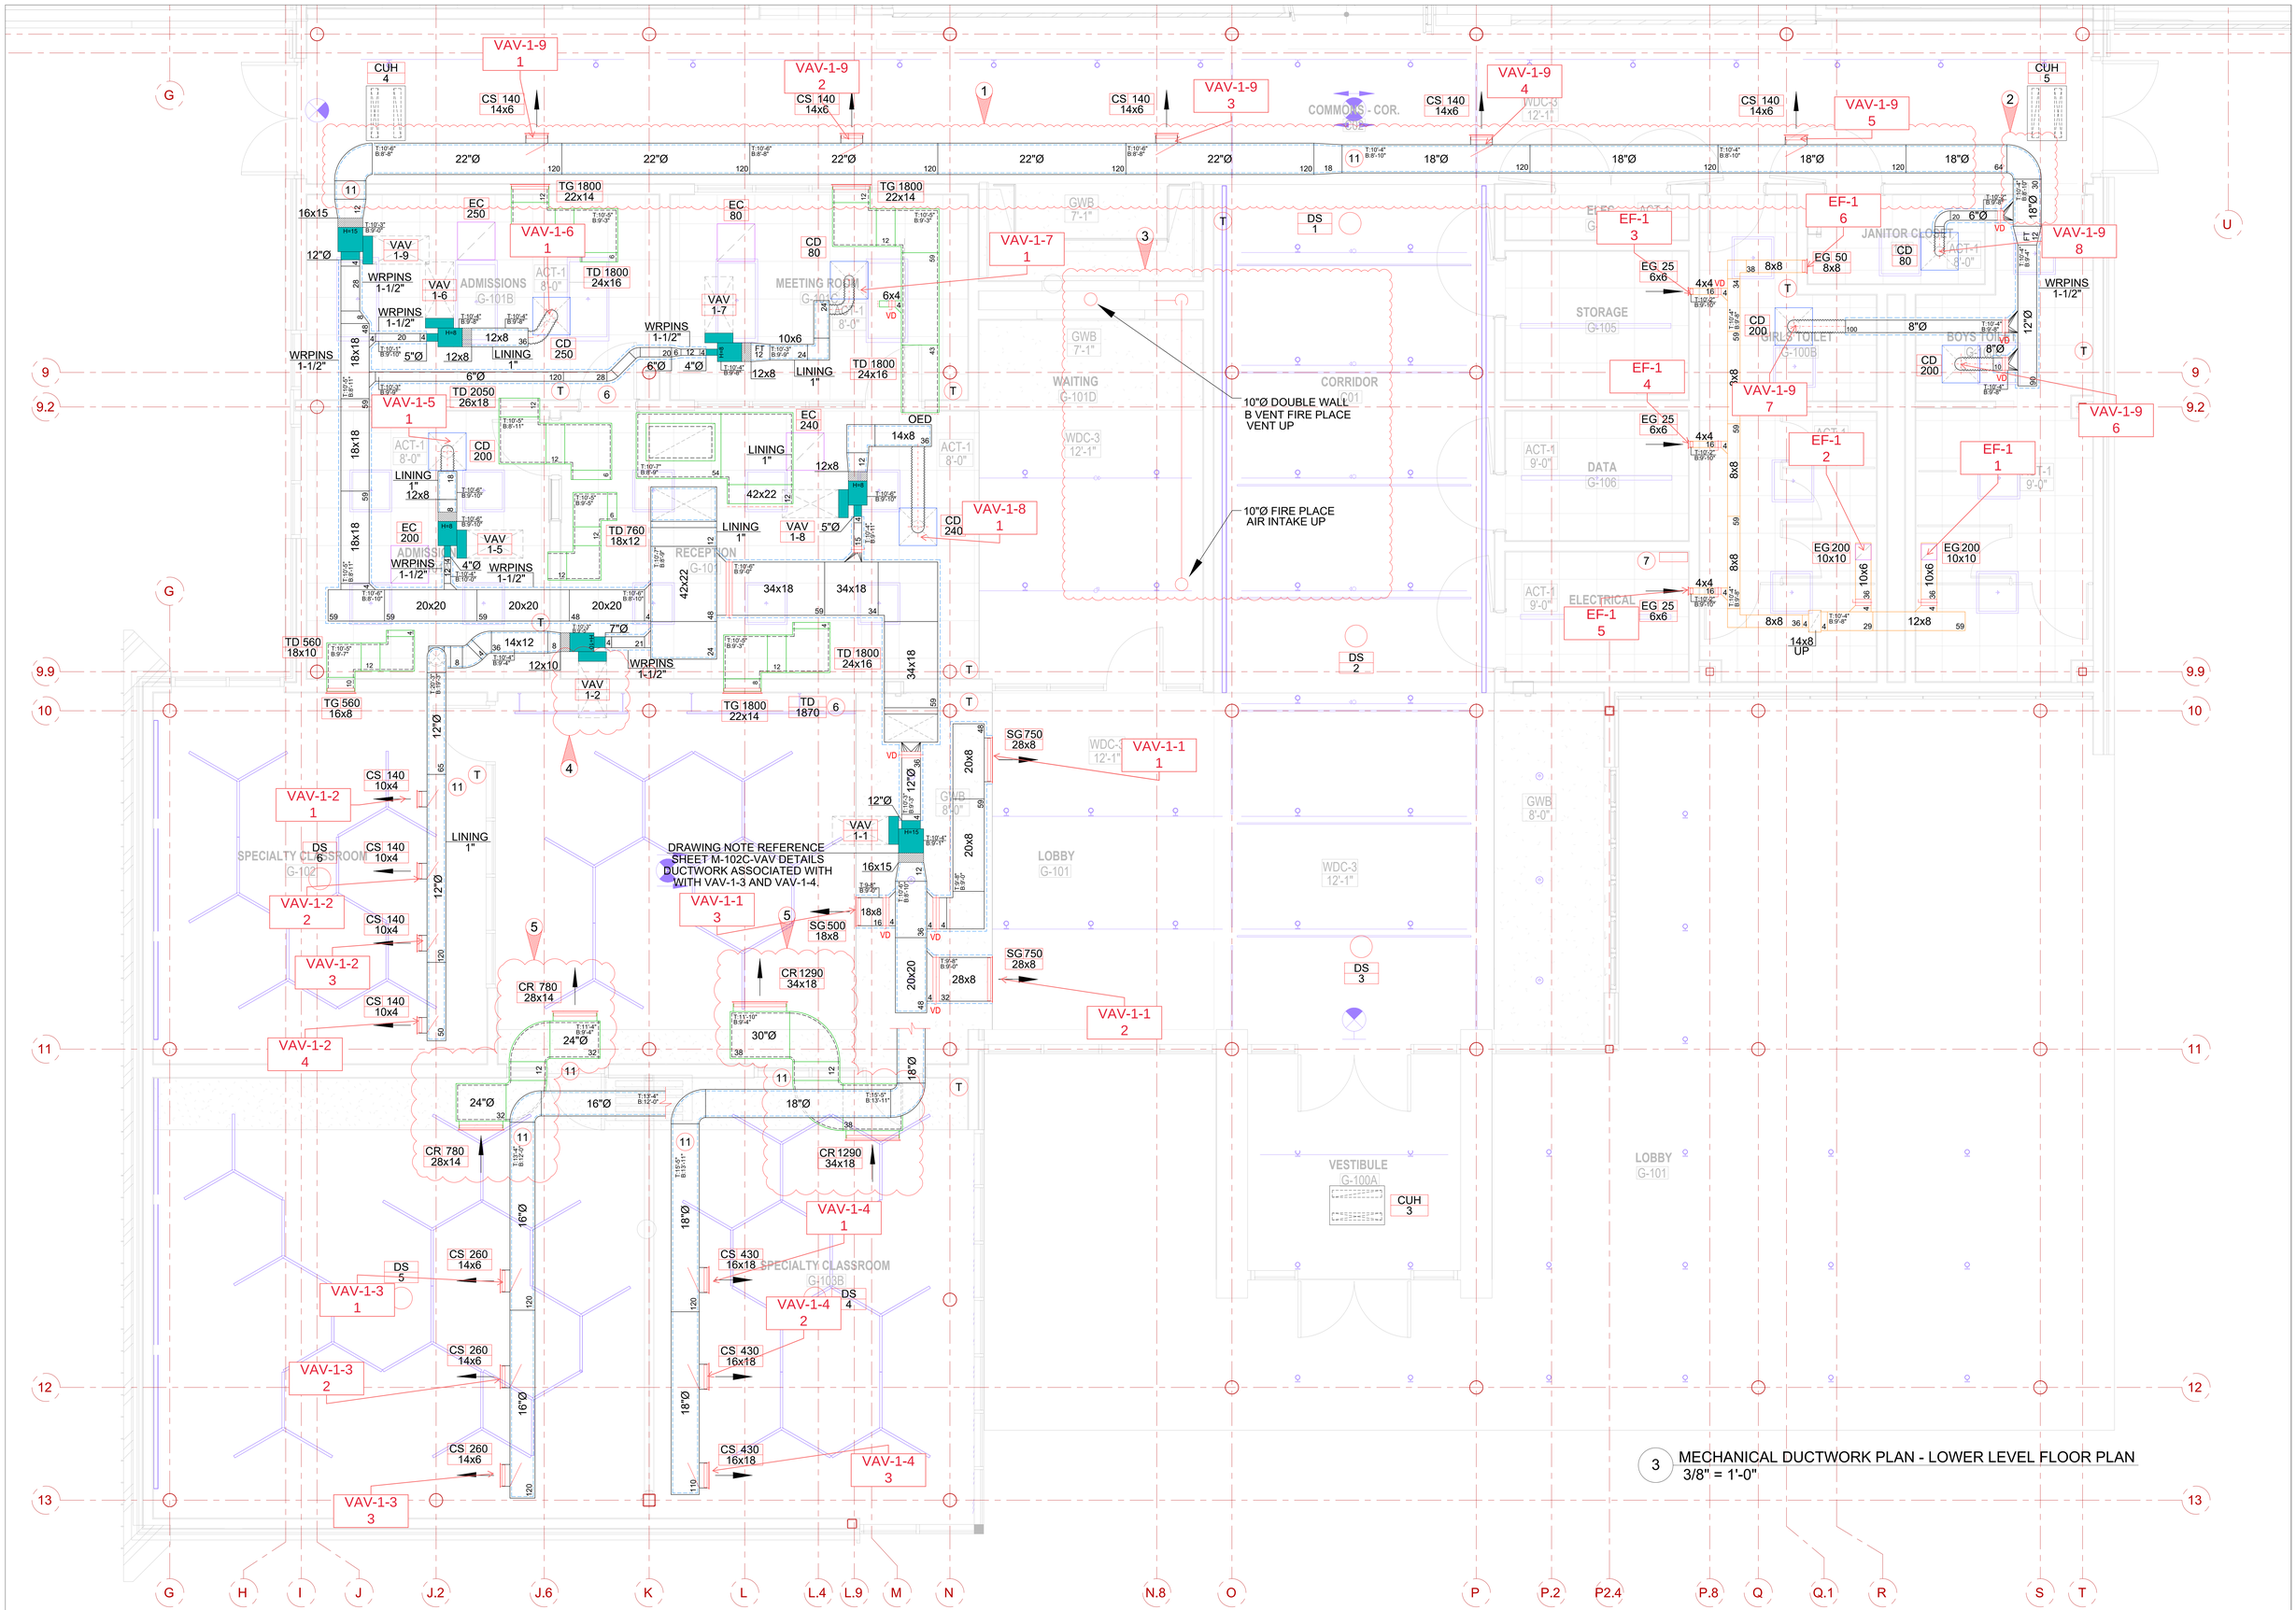

3 MECHANICAL DUCTWORK PLAN - LOWER LEVEL FLOOR PLAN
3/8" = 1'-0"

FLAG NOTES:

1. THE SUPPLY DUCT FROM ROOM G-101B TO THE CORRIDOR LIMITS THE HEIGHT OF THE EXPOSED SPIRAL DUCTWORK TO 10'-6", WHICH BRINGS THE BOTTOM OF THE DUCT TO 8'-8". PLEASE ADVISE IF THIS HEIGHT IS ACCEPTABLE, OR RECOMMEND A SOLUTION TO INCREASE THE HEIGHT BENEATH THE DUCTWORK.
2. PLEASE ADVISE ON THE CONFLICT BETWEEN THE EXPOSED SPIRAL DUCT AND THE CEILING HEIGHT IN THE ROOM G-100C
3. THE FIREPLACE SPECS ARE STILL UNDER REVIEW, WHICH COULD INFLUENCE THE POSITIONS OF THE VENT AND INTAKE. ONCE THE SPECS ARE APPROVED, A DEDICATED FIREPLACE SHOP DRAWING WILL BE SUBMITTED FOR APPROVAL .
4. MINIMUM CLEARANCE REQUIRED FOR SERVICE ACCESS HAS NOT BEEN ACHIEVED IN THE CURRENT DUCT LAYOUT. PLEASE ADVISE ON.
5. A CONFLICT HAS BEEN IDENTIFIED BETWEEN THE TRANSFER DUCTS AND THE NEW SOFFIT LAYOUT. PLEASE ADVISE ON.

GENERAL NOTES:

1. 1" ACOUSTIC LINING 15FT DOWNSTREAM FOR VAVS
2. 1 1/2" R6 WRAP INSULATION FOR SUPPLY AND RETURN DUCTWORK.
3. 1" ACOUSTIC LINING FOR TRANSFER DUCTS.


NORTHERN WOLVES AIR CONDITIONING
NORTHERN WOLVES AC
55 9TH STREET, 55A2
SUITE 182
BROOKLYN, NY 11215

Revisions
REV-1 – REVIEW AS PER ARCHITECT AND ENGINEER COMMENTS 09/29/2025 AND COORDINATION DRAWINGS 10/20/2025
REV-2 – AS PER SPECIALTY CLASSROOM DUCT REV. 11/05/2025


SADDLE RIVER DAY SCHOOL
147 CHESTNUT RIDGE RD.
SADDLE RIVER, NJ 07458

M-102C.SD
MECHANICAL
LOWER LEVEL FLOOR PLAN
DUCTWORK

Proj. No.
Drawn By:
Date: 11/24/2025
Checked By:

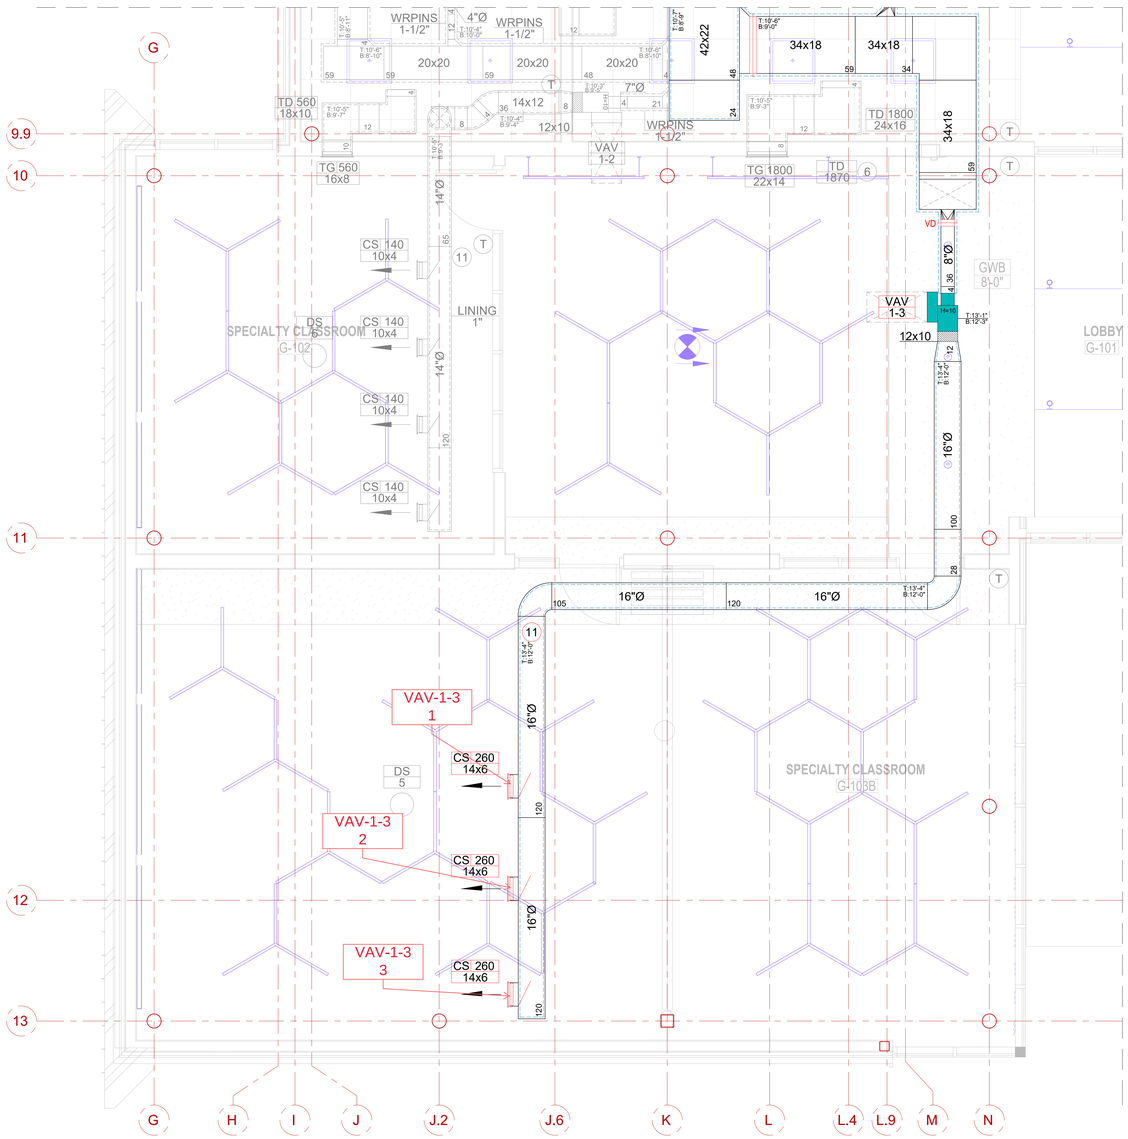

1 MECHANICAL DUCTWORK PLAN - LOWER LEVEL - VAV-1-3
3/8" = 1'-0"

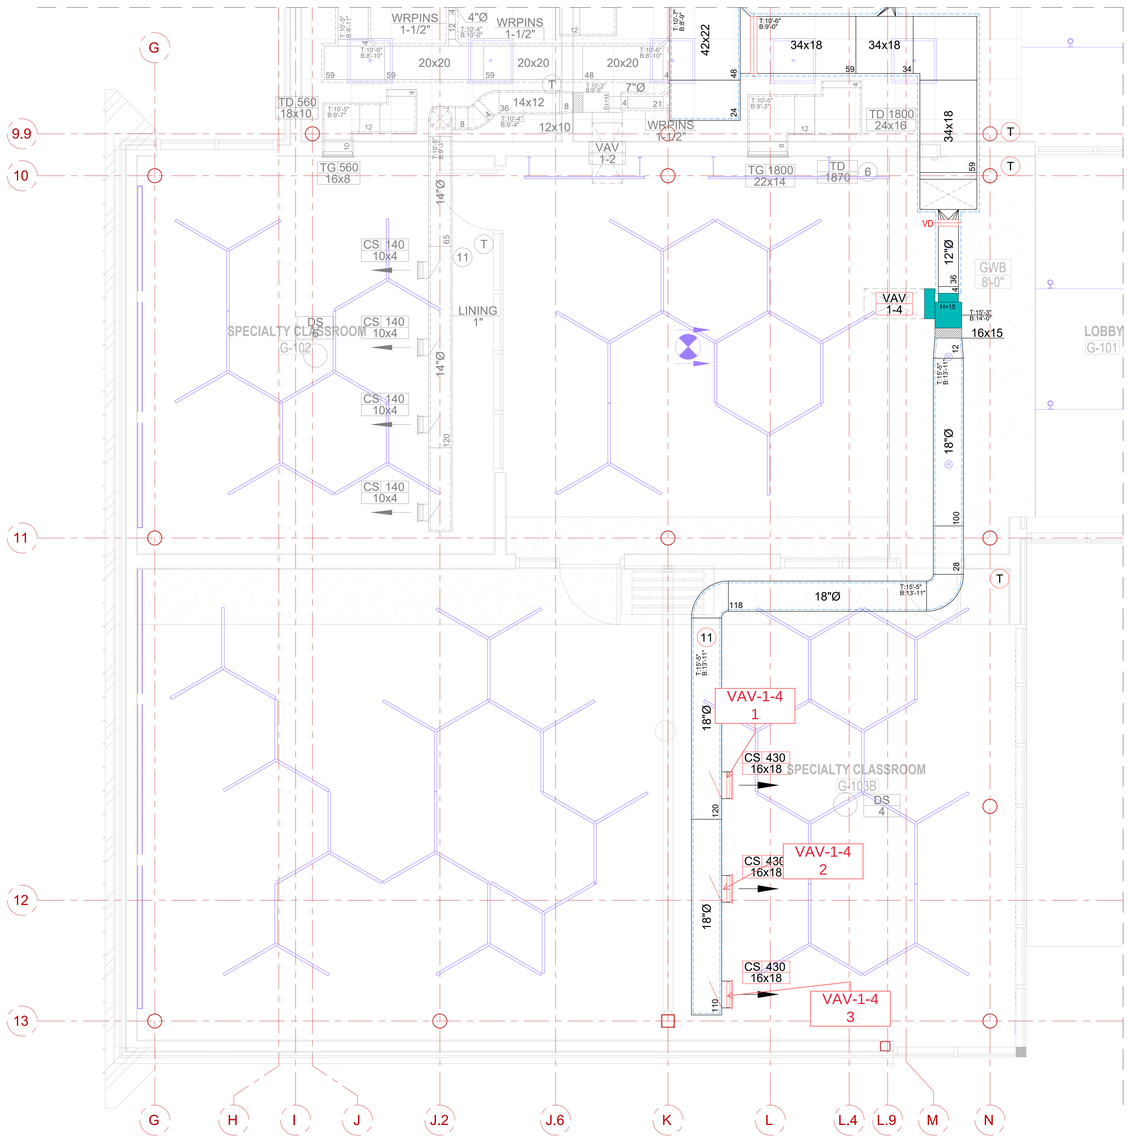

2 MECHANICAL DUCTWORK PLAN - LOWER LEVEL - VAV-1-4
3/8" = 1'-0"

GENERAL NOTES:

1. 1" ACOUSTIC LINING 15FT DOWNSTREAM FOR VAV'S
2. 1 1/2" R6 WRAP INSULATION FOR SUPPLY AND RETURN DUCTWORK.
3. 1" ACOUSTIC LINING FOR TRANSFER DUCTS.

NORTHERN WOLVES AIR CONDITIONING

NORTHERN WOLVES AC
55 9TH STREET, 55A2
SUITE 182
BROOKLYN, NY 11215


Revisions

SADDLE RIVER DAY SCHOOL
147 CHESTNUT RIDGE RD.
SADDLE RIVER, NJ 07458

M-102C-VAV.SD

MECHANICAL
LOWER LEVEL
VAV DETAIL

Proj. No.
Drawn By:
Date
11/24/2025
Checked By:

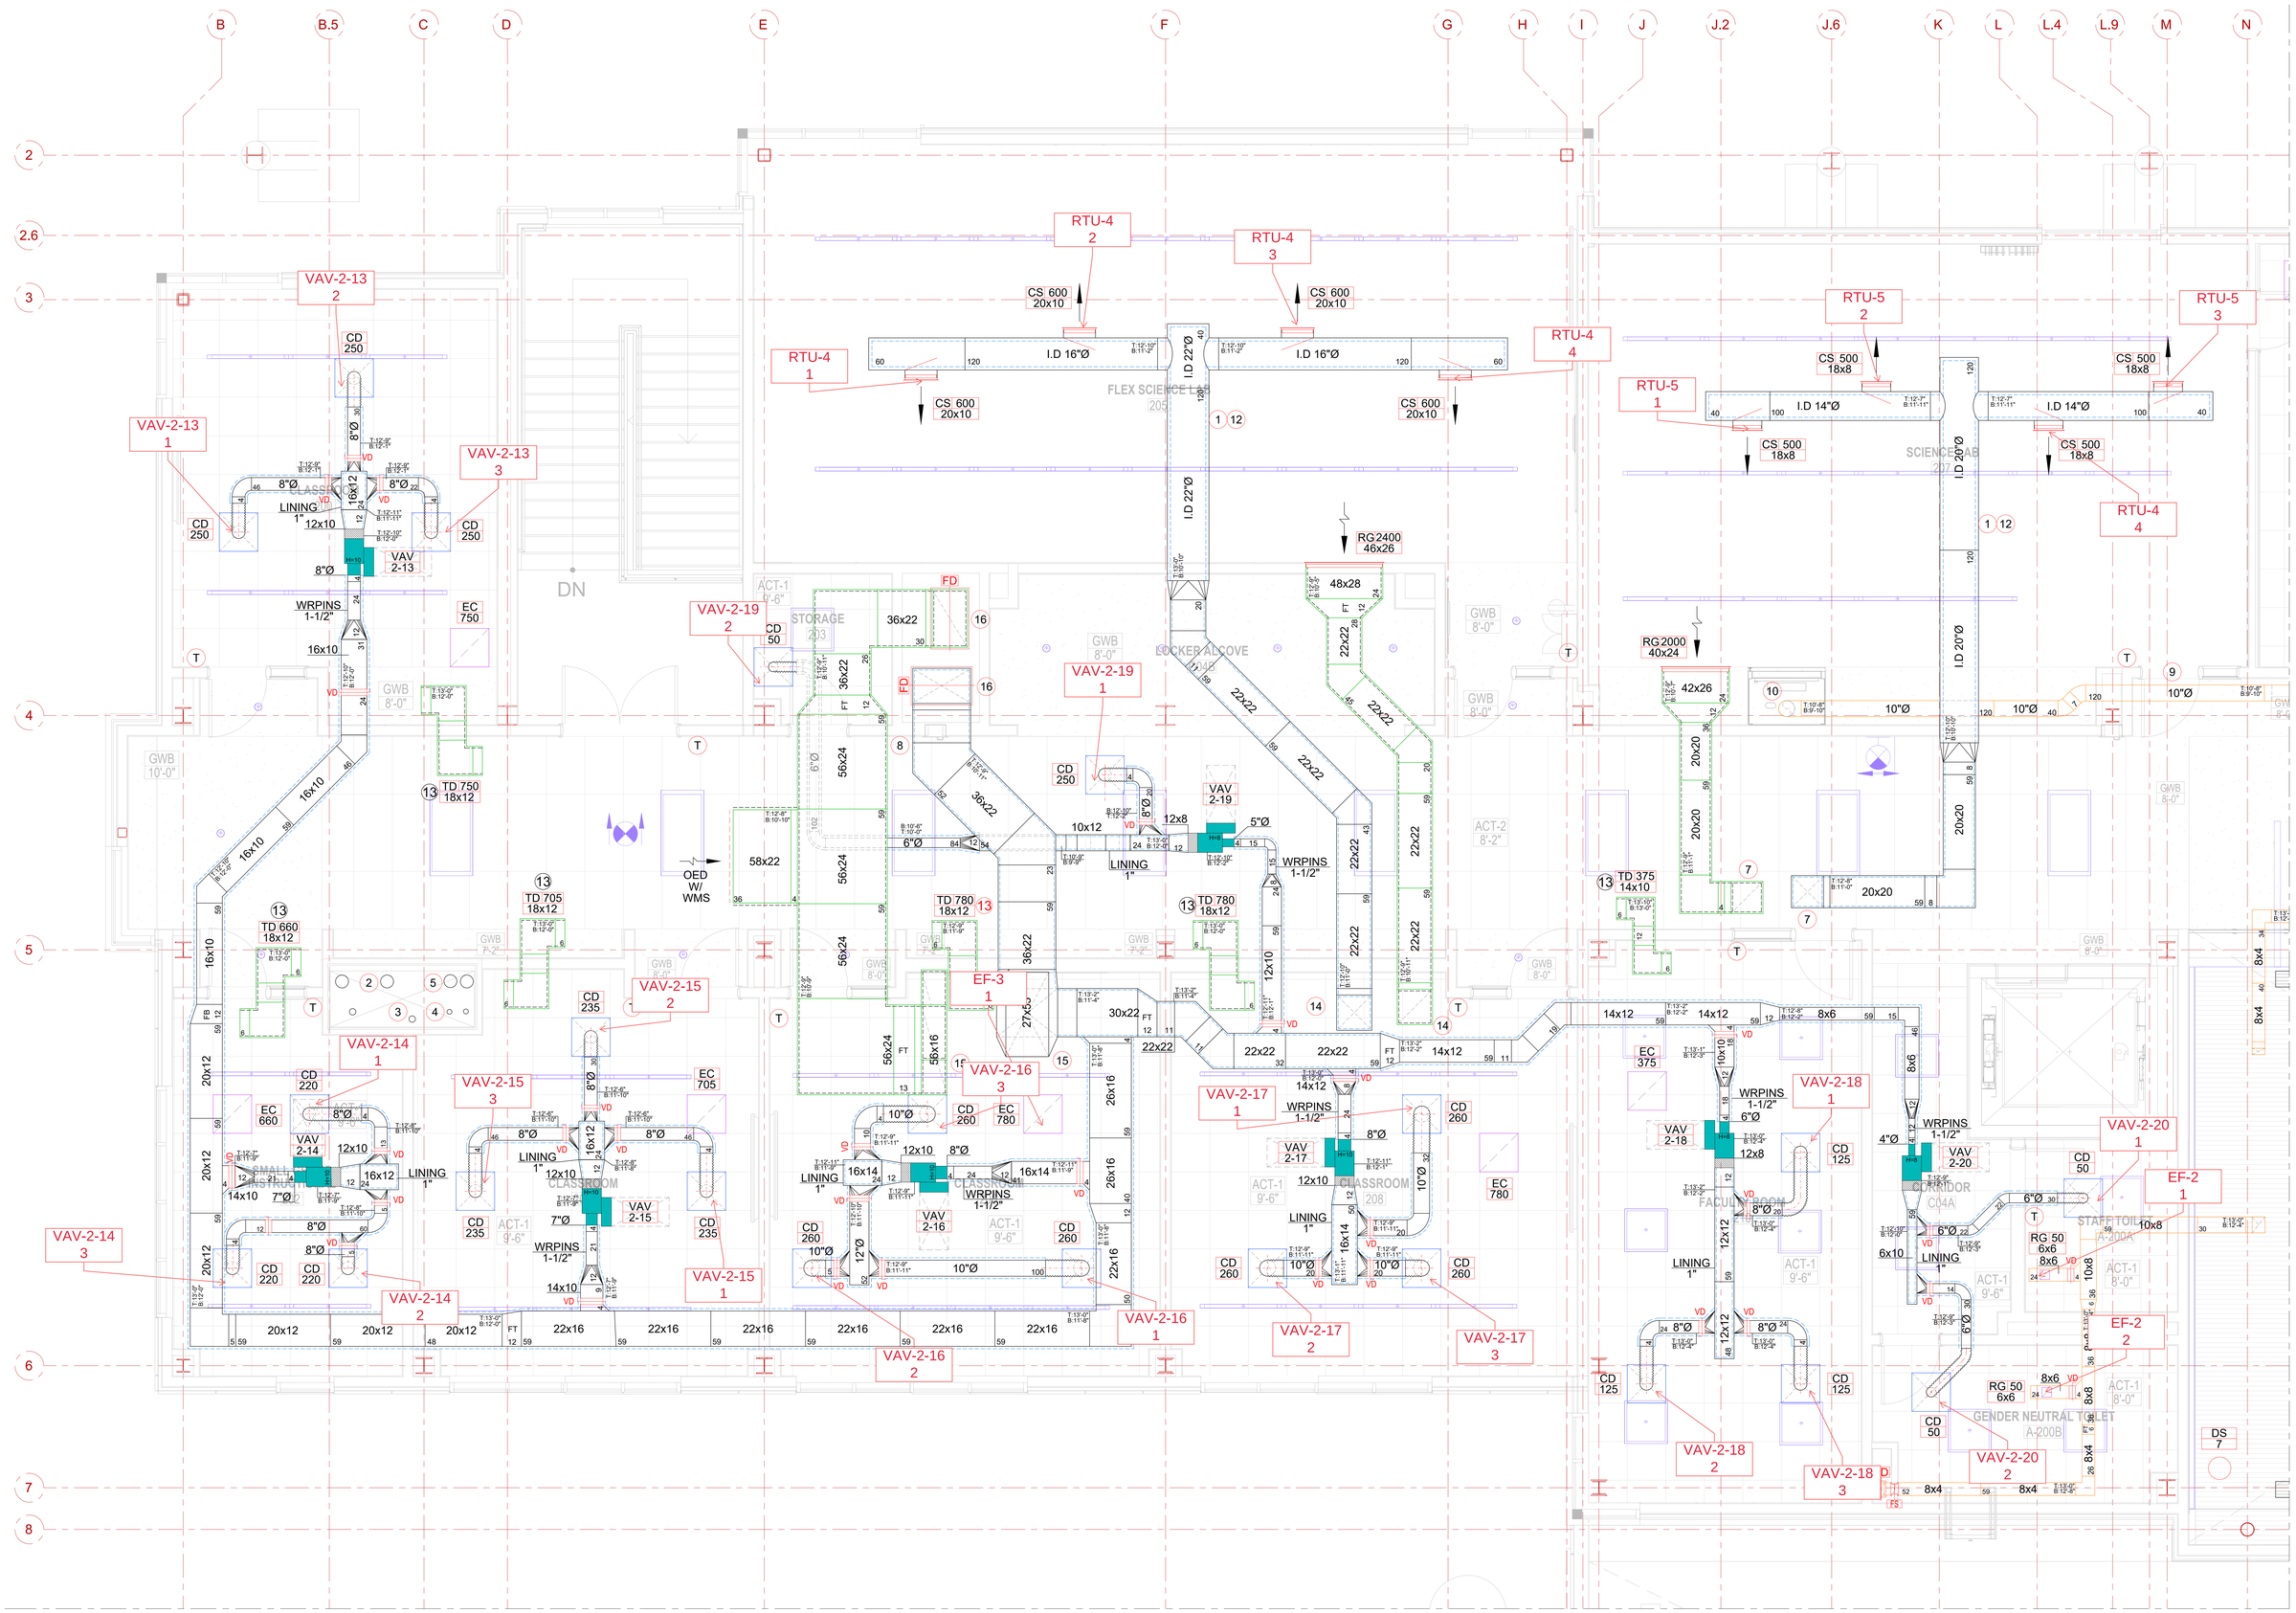

1 MECHANICAL DUCTWORK PLAN - UPPER LEVEL FLOOR PLAN
3/8" = 1'-0"

GENERAL NOTES:

1. 1" ACOUSTIC LINING 15FT DOWNSTREAM FOR VAV'S
2. 1 1/2" R6 WRAP INSULATION FOR SUPPLY AND RETURN DUCTWORK.
3. 1" ACOUSTIC LINING FOR TRANSFER DUCTS.


NORTHERN WOLVES AIR CONDITIONING
NORTHERN WOLVES AC
55 9TH STREET, 55A2
SUITE 182
BROOKLYN, NY 11215

Revisions
REV-1 – REVIEW AS PER ENGINEER COMMENTS 09/19/2025
REV-2 – REVIEW AS PER COORDINATION MEETING AND MECHANICAL DRAWINGS UPDATE – 10/31/2025 – REV-7

SADDLE RIVER DAY SCHOOL
147 CHESTNUT RIDGE RD.
SADDLE RIVER, NJ 07458

M-103A.SD
MECHANICAL
UPPER LEVEL FLOOR PLAN
DUCTWORK

Proj. No.
Drawn By
Date 11/17/2025
Checked By

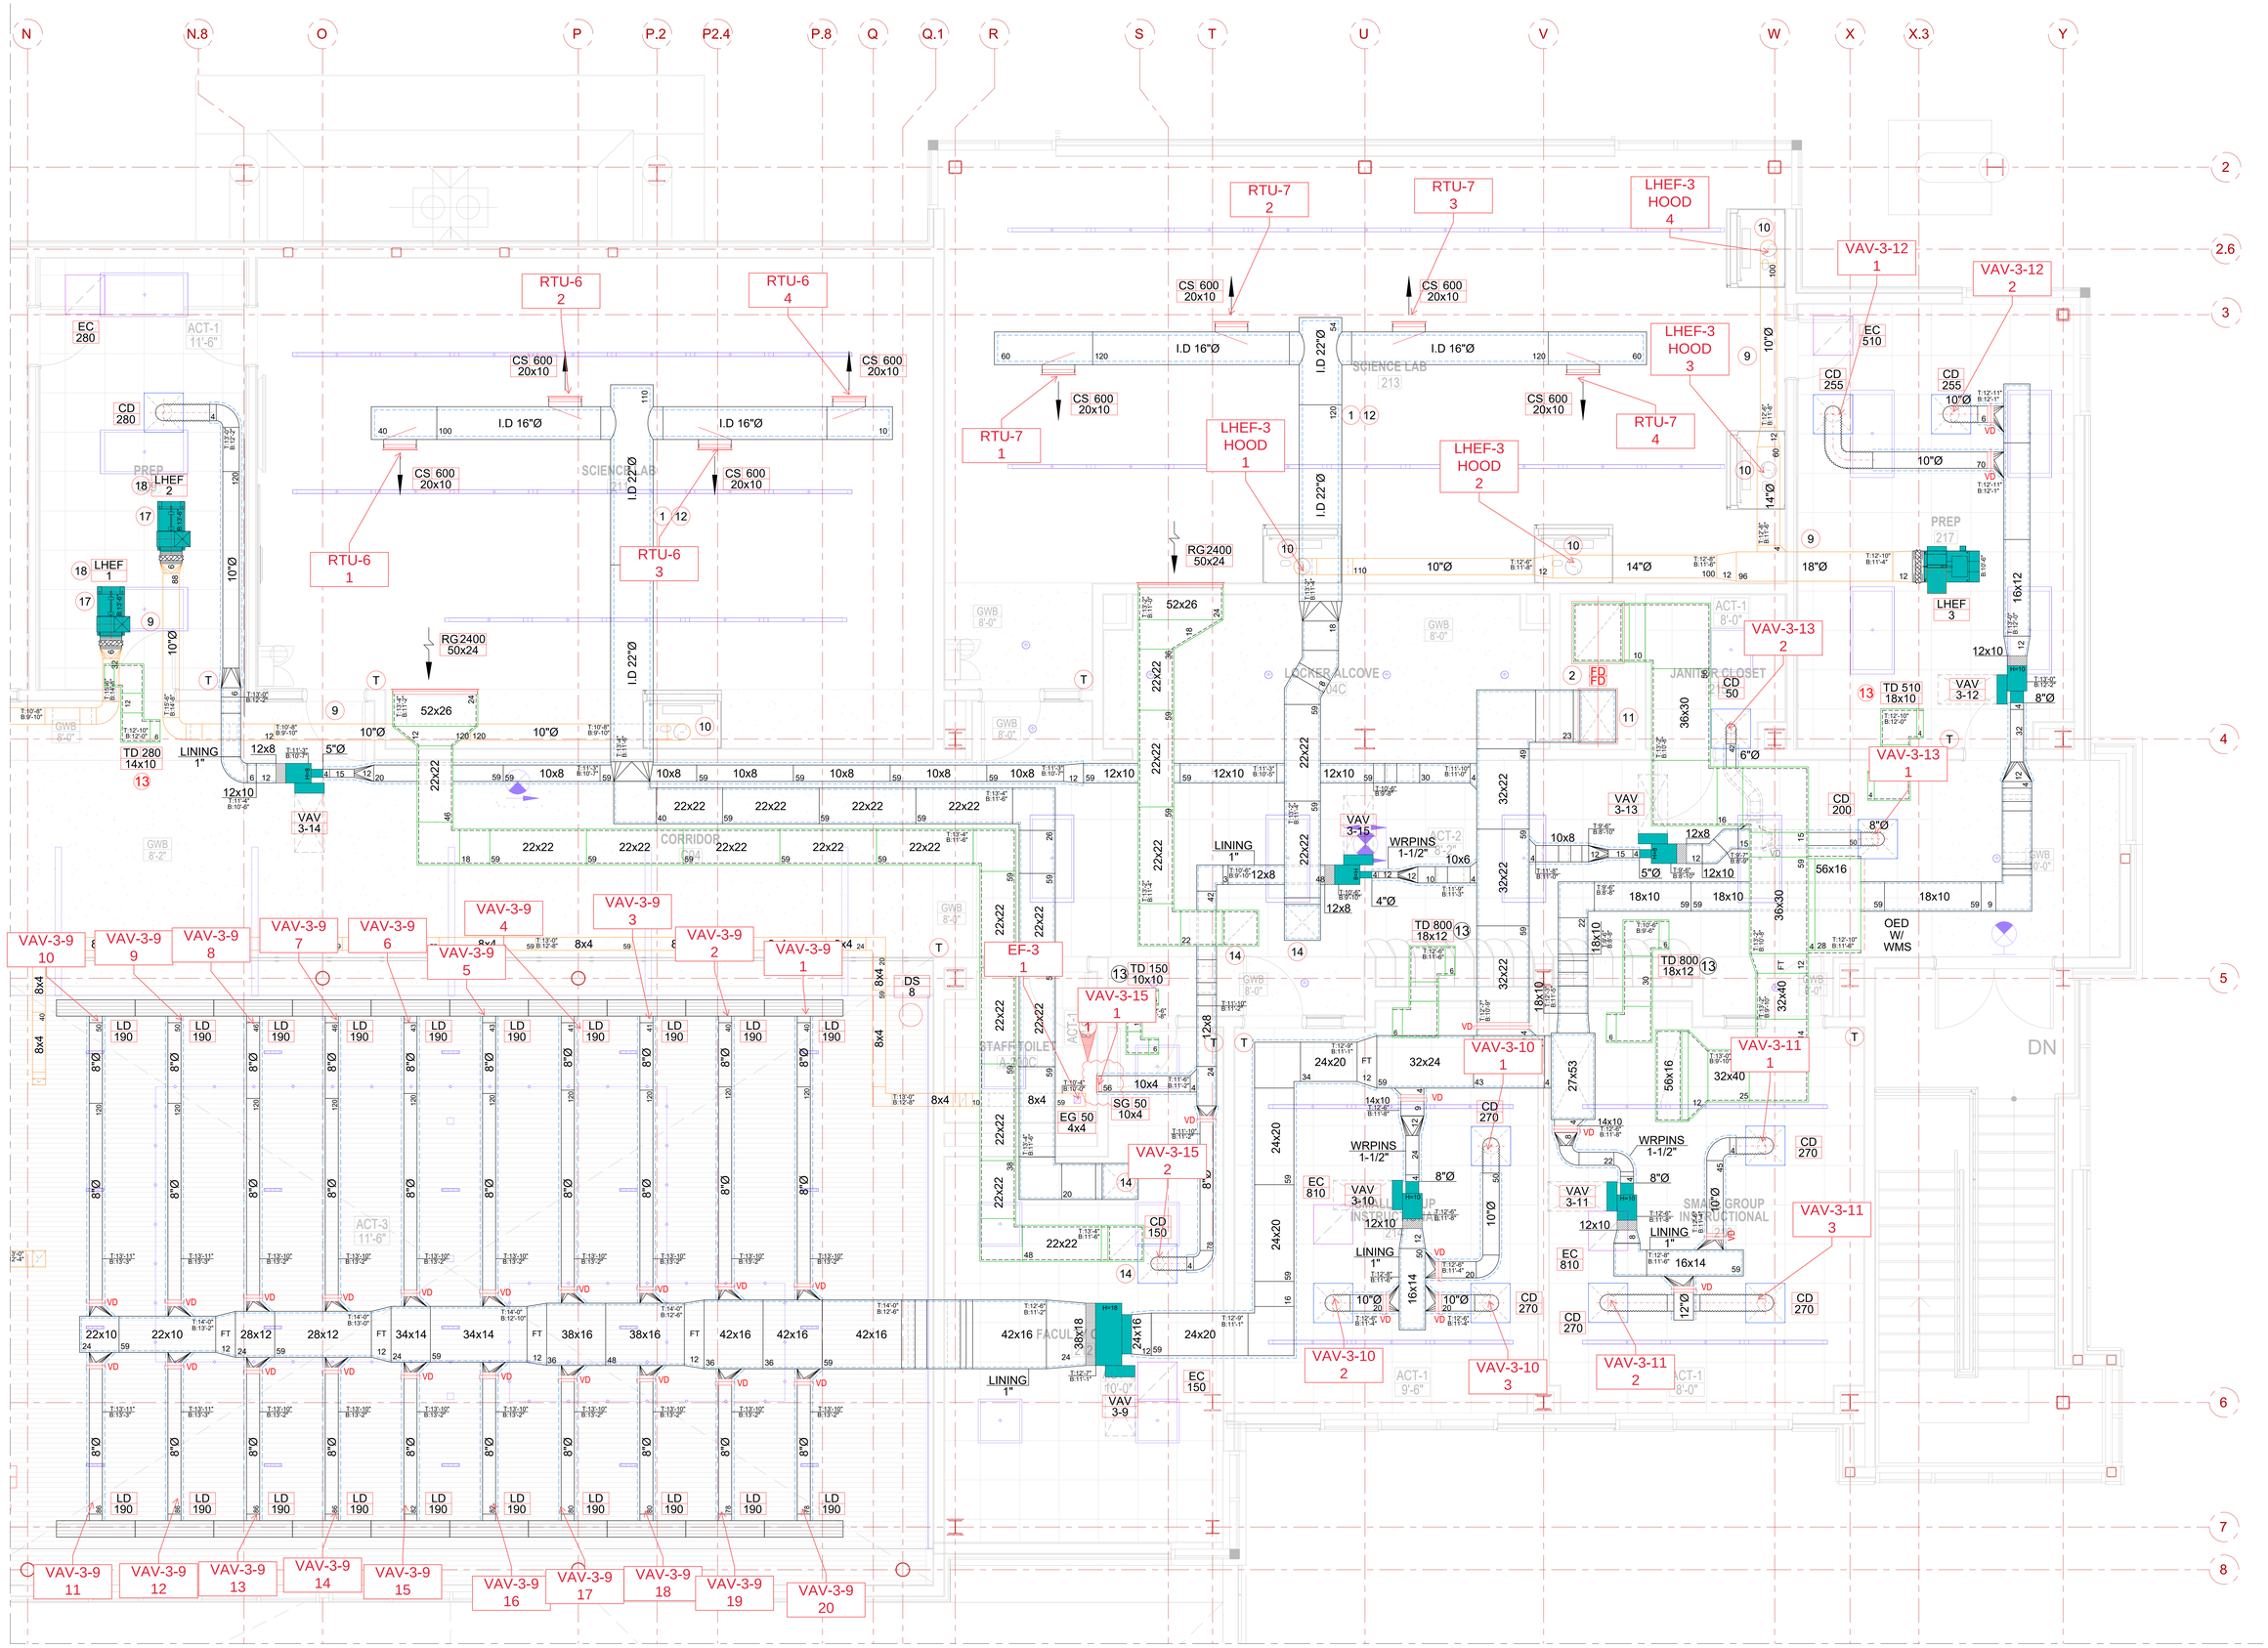

2 MECHANICAL DUCTWORK PLAN - UPPER LEVEL FLOOR PLAN

3/8" = 1'-0"

FLAG NOTES:

1. THE STAFF TOILET CEILING IS AT 8'-0" AFF, WHILE THE FACILITY OFFICE CEILING IS AT 10'-0" AFF. A SUPPLY DUCT FROM THE OFFICE DISCHARGES VIA A SIDEWALL GRILLE ABOVE THE TOILET CEILING, NOT INTO THE OCCUPIED SPACE. THIS DUCT APPEARS INTENDED TO PROVIDE MAKEUP AIR FOR THE 50 CFM TOILET EXHAUST. PLEASE CONFIRM IF THIS DISCHARGE LOCATION IS ACCEPTABLE, OR IF THE GRILLE SHOULD BE RELOCATED TO DELIVER AIR DIRECTLY INTO THE STAFF TOILET.

GENERAL NOTES:

1. 1" ACOUSTIC LINING 15FT DOWNSTREAM FOR VAV'S
2. 1 1/2" R6 WRAP INSULATION FOR SUPPLY AND RETURN DUCTWORK.
3. 1" ACOUSTIC LINING FOR TRANSFER DUCTS.

NORTHERN WOLVES AIR CONDITIONING

NORTHERN WOLVES AC
55 9TH STREET, 55A2
SUITE 182
BROOKLYN, NY 11215

Revisions

- REV-1 – REVIEW AS PER ENGINEER COMMENTS 09/19/2025
- REV-2 – REVIEW AS PER COORDINATION MEETING AND MECHANICAL DRAWINGS UPDATE – 10/31/2025 – REV-7
- REV-3 – REVIEW AS PER COORDINATION MEETING – 11/18/2025

SADDLE RIVER DAY SCHOOL
147 CHESTNUT RIDGE RD.
SADDLE RIVER, NJ 07458

M-103B.SD

MECHANICAL
UPPER LEVEL FLOOR PLAN
DUCTWORK

Proj. No. | Drawn By:
Date: 11/18/2025 | Checked By:

ABBREVIATIONS AND DEFINITIONS

1WCD	ONE WAY BLOW PATTERN CEILING DIFFUSER
2WCD	TWO WAY BLOW PATTERN CEILING DIFFUSER
3WCD	THREE WAY BLOW PATTERN CEILING DIFFUSER
4WCD	FOUR WAY BLOW PATTERN CEILING DIFFUSER
BHP	BRAKE HORSEPOWER
CAV	CONSTANT AIR VOLUME
CFM	CUBIC FEET PER MINUTE AIR FLOW
CG, CR	CEILING GRILL, CELING REGISTER
CC	COOLING COIL
DIA	DIAMETER
DNL	DATA NOT LEGIBLE OR AVAILABLE ON EQUIPMENT
DPR	DAMPER
EA	EXHAUST AIR
EFF	EFFICIENCY
EG, ER	EXHAUST GRILLE, EXHAUST REGISTER
E.S.P.	EXTERNAL STATIC PRESSURE
EXIST	EXISTING
FF	FINAL FILTER
FPM	FEET PER MINUTE AIR VELOCITY
FPS	FEET PER SECOND WATER VELOCITY
FT	FOOT (FEET) LENGTH
GPM	GALLONS PER MINUTE FLOW
HC	HEATING COIL
HF	HEPA FILTER
HP	HORSEPOWER
HRC, HRW	HEAT RECOVERY CORE, HEAT RECOVERY WHEEL
IN. WC	INCHES WATER COLUMN PRESSURE
LBG	LINEAR BAR GRILL
LD	LINEAR DIFFUSER
N.A., N.APP.	DEVICE NOT ACCESSIBLE, NOT APPLICABLE
N.I., N.S.	NOT INSTALLED, NOT SPECIFIED
OA	OUTSIDE AIR
OED	OPEN ENDED DUCT
PFAC	POWER FACTOR
PF	PREFILTER
PSI	POUNDS PER SQUARE INCH PRESSURE
PSID	POUNDS PER SQUARE INCH DIFFERENTIAL PERSSURE
PSIG	POUNDS PER SQUARE INCH GAUGE PRESSURE
RA	RETURN AIR
RG, RR, RCD	RETURN GRILLE, RETURN REGISTER, ROUND CEILING DIFFUSER
RND	ROUND
RPM	REVOLUTIONS PER MINUTE ROTATIONAL SPEED
SA	SUPPLY AIR
SG, SR	SUPPLY GRILL, SUPPLY REGISTER
SQFT	SQUARE FEET AREA
S.P.	STATIC PRESSURE
T.S.P.	TOTAL STATIC PRESSURE
VAV	VARIABLE AIR VOLUME BOX
V.P.	VELOCITY PRESSURE
VD	VOLUME DAMPER
WMS	WIRE MESH SCREEN

EXHIBIT 5-B

Water balancing report, Rite Technical Services, 7/14/2026

Rite Technical Services, Inc.
183 Broadway, Ste 216, Hicksville, NY 11801
Tel: (718) 576 1786

TESTING AND BALANCING REPORT

FOR

SADDLE RIVER DAY SCHOOL

147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

PREPARED FOR

NORTHERN WOLVES INC
55 9TH STREET, UNIT 55A-2
BROOKLYN, NY 11215

07/14/2026

CERTIFICATION

PROJECT NAME: SADDLE RIVER DAY SCHOOL

LOCATION: 147 CHESTNUT RIDGE ROAD, SADDLE RIVER, NJ 07458

The data presented in this report is a record of system measurements and final adjustments that have been obtained in accordance with the current edition of the NEBB procedural standards for testing, adjusting and balancing of environmental systems. Any variances from the design quantities, which exceed NEBB tolerances, are noted in the testing and balancing report.

STAMP



DATE:

07/14/2026

RITE TECHNICAL SERVICES, INC.

183 BROADWAY, STE 216
HICKSVILLE, NY 11801

AIR & HYDRONIC SYSTEMS
ROHIT ARORA
CERTIFICATON # 3540
EXPIRATION DATE: 12/31/2026

INSTRUMENTATION LIST

AND

CALIBRATION DATES

Instrument Ownership for Firm: Rite Technical Services, Inc.

Date: 05/02/2026

	FUNCTION	MINIMUM RANGE	MINIMUM ACCURACY	MINIMUM RESOLUTION	INSTRUMENT INFORMATION	CALIBRATION INTERVAL
A,H	**Rotation Measurement**	60 to 5000 rpm	± 2% of reading ± 2 rpm	± 1 rpm	Mfr. / Model Number: EXTECH/461920 Serial Number: 130723148	12 Months F Date: 05/02/2026
	Temperature Measurement					
A	Air	-0 to 200 deg. F (US) -20 to 100 deg. C (SI)	± 0.5% of reading ± 2 deg. F (US) ± 1 deg. C (SI)	0.1 deg. F (US) 0.1 deg. C (SI)	Mfr. / Model Number: SHORTRIDGE/ADM870C Serial Number: M13148	12 Months B Date: 05/02/2026
H	Immersion	-0 to 200 deg. F (US) -20 to 100 deg. C (SI)	± 0.5% of reading ± 2 deg. F (US) ± 1 deg. C (SI)	0.1 deg. F (US) 0.1 deg. C (SI)	Mfr. / Model Number: SHORTRIDGE/ADT442 Serial Number: M06306-2	12 Months D Date: 05/02/2026
H	Contact	-0 to 200 deg. F (US) -20 to 100 deg. C (SI)	± 0.5% of reading ± 2 deg. F (US) ± 1 deg. C (SI)	0.1 deg. F (US) 0.1 deg. C (SI)	Mfr. / Model Number: SHORTRIDGE/ADT444 Serial Number: 122611	12 Months E Date: 05/02/2026
	Electrical Measurement CAT III True RMS					
A,H	Volts	1 to 600 VAC	± 2% of reading	1.0 Volt	Mfr. / Model Number: FLUKE / 323	12 Months G
A,H	Amperes	0.1 to 100 Amps	± 2% of reading	0.1 Ampere	Serial Number: 51427508MV	Date: 05/02/2026
A	**Air Pressure Measurement**	0 to 10.00 in.w.g. (US) 0 to 2500 Pascals (SI)	± 2% of reading ± 0.001 in. w.g. (US) ± 0.25 Pa (SI)	0.001 in. w.g. ≤ 1 in. w.g. (US) 0.10 Pa ≤ 250 Pa (SI) 0.01 in. w.g. > 1 in. w.g. (US) 1.0 Pa > 250 Pa (SI)	Mfr. / Model Number: SHORTRIDGE/ADM870C Serial Number: M13148	12 Months B Date: 05/02/2026

Instrument Ownership for Firm: Rite Technical Services, Inc.

Date: 05/02/2026

	FUNCTION	MINIMUM RANGE	MINIMUM ACCURACY	MINIMUM RESOLUTION	INSTRUMENT INFORMATION	CALIBRATION INTERVAL
A	**Air Velocity Measurement Hot Wire Anemometer OR Airfoil with Digital Meter**	**100 to 3500 fpm**	**±5% of reading, ± 7 fpm**	**1.0 fpm**	Mfr. / Model Number: SHORTRIDGE/ADM870C Serial Number: M13148	12 Months B Date: 05/02/2026
A	**Air Velocity Measurement Rotating Vane**	**50 to 2500 fpm**	**± 2% of reading ± ± 4 fpm**	**1.0 fpm**	Mfr. / Model Number: TSI/8322 Serial Number: 55060516	12 Months A Date: 05/02/2026
A	**Humidity Measurement**	10 to 90% RH	3% of reading	1.0%	Mfr. / Model Number: EXTECH/RH300 Serial Number: 10386511	12 Months H Date: 05/02/2026
A	**Direct Reading Hood**	100 to 2000 cfm (US) 50 to 944 l/s (SI)	± 5% of reading ± 7 cfm (US) ± 4 l/s (SI)	Digital 1.0 cfm (US) Digital 1.0 l/s (SI) Analog - Not Applicable	Mfr. / Model Number: SHORTRIDGE/8400 Serial Number: M06306-1	12 Months C Date: 05/02/2026

Instrument Ownership for Firm: Rite Technical Services, Inc.

Date: 05/02/2026

	FUNCTION	MINIMUM RANGE	MINIMUM ACCURACY	MINIMUM RESOLUTION	INSTRUMENT INFORMATION	CALIBRATION INTERVAL
H						
	Hydronic Pressure Measurement	0.4 to 200 psi (US) 3 to 1400 kPa (SI)	± 2% of reading ± 1 psi (US) ± 7 kPa (SI)	0.1 psi (US) 1.0 kPa (SI)	Mfr. / Model Number: ALNOR/HM680 Serial Number: 70552168	12 Months I Date: 05/02/2026
H						
	Hydronic Differential Pressure Measurement	0.4 to 75 psi (US) 3 to 500 kPa (SI)	± 2% of reading ± 0.5 psi (US) ± 3.5 kPa (SI)	0.01 psi (US) 0.1 kPa (SI)	Mfr. / Model Number: ALNOR/HM680 Serial Number: 70552168	12 Months I Date: 05/02/2026

CONTENTS

PROJECT: SADDLE RIVER DAY SCHOOL

LOCATION: 147 CHESTNUT RIDGE ROAD, SADDLE RIVER, NJ 07458

S. NO.	DESCRIPTION	PAGE
1	SUMMARY	1.1
2	PUMP & BALANCING VALVE TEST REPORT	2.1 – 2.4
3	ABBREVIATIONS & DEFINITIONS	APPENDIX

Rite Technical Services, Inc.
183 Broadway, Ste 216
Hicksville, NY 11801
T: (718) 576 1786

07/14/2026

SUMMARY

TESTING AND BALANCING

Northern Wolves Inc
55 9th Street, Unit 55A-2
Brooklyn, NY 11215

Ref: Saddle River Day School

Location: 147 Chestnut Ridge Road, Saddle River, NJ 07458

Attn: Ruslan Zhdamarov,

Our firm performed testing and balancing at the above referenced project. The measured results are listed in the attached detailed report.

Should you have any questions regarding the information in the report, please do not hesitate to call our office.

Yours truly,



Rohit Arora

Rite T & B

HYDRONIC PUMP TEST REPORT

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM / UNIT: P-1, P-2

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 07/14/2026

UNIT DATA	UNIT NO.		UNIT NO.		UNIT NO.	
UNIT DESIGNATION	P-1		P-2			
TYPE OF SERVICE	SECONDARY HOT WATER		SECONDARY HOT WATER			
MANUFACTURER	BELL & GOSSETT		BELL & GOSSETT			
MODEL NUMBER	E-90 2AAB BF 4"		E-90 2AAB BF 4"			
DESIGN FLOW GPM	100		100			
DESIGN HEAD - FT	60		60			
IMPELLER SIZE - INCH	4.000		4.000			
SERIAL NUMBER	9003580-2		9003580B52-1			
MOTOR MANUFACTURER	NIDEC		NIDEC			
TEST DATA	**DESIGN**	**ACTUAL**	**DESIGN**	**ACTUAL**	**DESIGN**	**ACTUAL**
MOTOR HP	-	5	-	5		
PUMP/MOTOR SPEED RPM	-	3450	-	3450		
NO FLOW SUCTION PRESSURE FT	-	69	-	70		
NO FLOW DISCHARGE PRESSURE FT	-	136	-	137		
NO FLOW DIFFERENTIAL PRESSURE FT	-	67	-	67		
ACTUAL IMPELLER SIZE	-	4.0"	-	4.0"		
FINAL SUCTION PRESSURE FT	-	93	-	93		
FINAL DISCHARGE PRESSURE FT	-	121	-	120		
TOTAL DYNAMIC HEAD FT	60	28	60	27		
FINAL FLOW GPM	100	66*	100	67*		
MOTOR RATED AMPERAGE	-	13.7	-	13.7		
MOTOR RATED PHASE	-	3	-	3		
MOTOR RATED Hz	-	60	-	60		
MOTOR RATED VOLTS	-	208	-	208		
MOTOR FRAME	-	56J	-	56J		
FINAL OPERATING VOLTAGES	208	209/210/210	208	209/210/210		
FINAL OPERATING AMPERAGES T1/T2/T3	13.7	5.1/5.2/5.2	13.7	5.2/5.2/5.3		
FINAL VFD OPERATING Hz	60	42	60	42		
*NOTE: FLOW ADJUSTED AS PER TOTAL REQUIRED AT TERMINALS/OPERATING LOAD. DP SET POINT AT BMS: 1.6 PSI.						

Rite T & B

BALANCING VALVE TEST REPORT

(Fixed or Adjustable Orifice)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: SECONDARY HOT WATER

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 07/14/2026

UNIT DESIGNATION	SERVICE	MANUFACTURER	MODEL NUMBER	SIZE	DESIGN FLOW GPM	VALVE SETTING/ POSITION	FINAL FLOW GPM	REMARKS
P-1 TDV	HOT WATER	B&G	3DS-3B	3"	100	100	66	FO-100, FC-0
P-2 TDV	HOT WATER	B&G	3DS-3B	3"	100	100	67	FO-100, FC-0
VAV-1-1	HOT WATER	B&G	CB-3/4	3/4"	1.40	20	1.45	FO-0-50-FC
VAV-1-2	HOT WATER	B&G	CB-3/4	3/4"	1.45	20	1.45	FO-0-50-FC
VAV-1-3	HOT WATER	B&G	CB-3/4	3/4"	2.53	5	2.55	FO-0-50-FC
VAV-1-4	HOT WATER	B&G	CB-3/4	3/4"	0.39	40	0.42	FO-0-50-FC
VAV-1-5	HOT WATER	B&G	CB-3/4	3/4"	0.11	45	0.14	FO-0-50-FC
VAV-1-6	HOT WATER	B&G	CB-3/4	3/4"	0.17	44	0.16	FO-0-50-FC
VAV-1-7	HOT WATER	B&G	CB-3/4	3/4"	0.11	45	0.13	FO-0-50-FC
VAV-1-8	HOT WATER	B&G	CB-3/4	3/4"	0.26	42	0.30	FO-0-50-FC
VAV-1-9	HOT WATER	B&G	CB-3/4	3/4"	0.60	35	0.65	FO-0-50-FC
VAV-2-1	HOT WATER	B&G	CB-3/4	3/4"	1.93	18	2.00	FO-0-50-FC
VAV-2-2	HOT WATER	B&G	CB-3/4	3/4"	3.17	0	3.20	FO-0-50-FC
VAV-2-3	HOT WATER	B&G	CB-3/4	3/4"	1.23	20	1.30	FO-0-50-FC
VAV-2-4	HOT WATER	B&G	CB-3/4	3/4"	1.93	18	2.00	FO-0-50-FC
VAV-2-5	HOT WATER	B&G	CB-3/4	3/4"	1.93	20	2.00	FO-0-50-FC
VAV-2-6	HOT WATER	B&G	CB-3/4	3/4"	0.37	42	0.40	FO-0-50-FC
VAV-2-7	HOT WATER	B&G	CB-3/4	3/4"	0.19	46	0.20	FO-0-50-FC
VAV-2-8	HOT WATER	B&G	CB-3/4	3/4"	0.37	40	0.40	FO-0-50-FC
VAV-2-9	HOT WATER	B&G	CB-3/4	3/4"	0.46	40	0.50	FO-0-50-FC

Rite T & B

BALANCING VALVE TEST REPORT

(Fixed or Adjustable Orifice)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: SECONDARY HOT WATER

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 07/14/2026

UNIT DESIGNATION	SERVICE	MANUFACTURER	MODEL NUMBER	SIZE	DESIGN FLOW GPM	VALVE SETTING/ POSITION	FINAL FLOW GPM	REMARKS
VAV-2-10	HOT WATER	B&G	CB-3/4	3/4"	0.46	40	0.50	FO-0-50-FC
VAV-2-11	HOT WATER	B&G	CB-3/4	3/4"	0.55	38	0.60	FO-0-50-FC
VAV-2-12	HOT WATER	B&G	CB-3/4	3/4"	1.56	20	1.60	FO-0-50-FC
VAV-2-13	HOT WATER	B&G	CB-3/4	3/4"	0.73	35	0.80	FO-0-50-FC
VAV-2-14	HOT WATER	B&G	CB-3/4	3/4"	0.64	38	0.70	FO-0-50-FC
VAV-2-15	HOT WATER	B&G	CB-3/4	3/4"	0.55	40	0.60	FO-0-50-FC
VAV-2-16	HOT WATER	B&G	CB-3/4	3/4"	0.57	40	0.60	FO-0-50-FC
VAV-2-17	HOT WATER	B&G	CB-3/4	3/4"	1.28	25	1.35	FO-0-50-FC
VAV-2-18	HOT WATER	B&G	CB-3/4	3/4"	0.32	45	0.40	FO-0-50-FC
VAV-2-19	HOT WATER	B&G	CB-3/4	3/4"	0.32	45	0.40	FO-0-50-FC
VAV-2-20	HOT WATER	B&G	CB-3/4	3/4"	0.37	45	0.40	FO-0-50-FC
VAV-2-21	HOT WATER	B&G	CB-3/4	3/4"	0.32	45	0.40	FO-0-50-FC
VAV-2-22	HOT WATER	B&G	CB-3/4	3/4"	2.55	15	2.60	FO-0-50-FC
VAV-3-1	HOT WATER	B&G	CB-3/4	3/4"	1.05	25	1.10	FO-0-50-FC
VAV-3-2	HOT WATER	TA	STAD-3/4	3/4"	0.37	10	0.42	FO-40,FC-00
VAV-3-3	HOT WATER	B&G	CB-3/4	3/4"	2.36	15	2.40	FO-0-50-FC
VAV-3-4	HOT WATER	TA	STAD-3/4	3/4"	2.36	35	2.40	FO-40,FC-00
VAV-3-5	HOT WATER	B&G	CB-3/4	3/4"	0.17	50	0.20	FO-0-50-FC
VAV-3-6	HOT WATER	B&G	CB-3/4	3/4"	0.37	45	0.40	FO-0-50-FC
VAV-3-7	HOT WATER	TA	STAD-3/4	3/4"	2.06	32	2.11	FO-40,FC-00

Rite T & B

BALANCING VALVE TEST REPORT

(Fixed or Adjustable Orifice)

PROJECT: SADDLE RIVER DAY SCHOOL

SYSTEM DESIGNATION: SECONDARY HOT WATER

LOCATION: 147 CHESTNUT RIDGE ROAD
SADDLE RIVER, NJ 07458

DATE: 07/14/2026

UNIT DESIGNATION	SERVICE	MANUFACTURER	MODEL NUMBER	SIZE	DESIGN FLOW GPM	VALVE SETTING/ POSITION	FINAL FLOW GPM	REMARKS
VAV-3-8	HOT WATER	B&G	CB-3/4	3/4"	2.45	10	2.50	FO-0-50-FC
VAV-3-9	HOT WATER	B&G	CB-3/4	3/4"	2.00	20	2.10	FO-0-50-FC
VAV-3-10	HOT WATER	B&G	CB-3/4	3/4"	0.62	40	0.65	FO-0-50-FC
VAV-3-11	HOT WATER	B&G	CB-3/4	3/4"	0.62	40	0.65	FO-0-50-FC
VAV-3-12	HOT WATER	B&G	CB-3/4	3/4"	1.34	25	1.40	FO-0-50-FC
VAV-3-13	HOT WATER	B&G	CB-3/4	3/4"	0.17	50	0.20	FO-0-50-FC
VAV-3-14	HOT WATER	B&G	CB-3/4	3/4"	0.32	45	0.38	FO-0-50-FC
VAV-3-15	HOT WATER	B&G	CB-3/4	3/4"	0.32	45	0.36	FO-0-50-FC
UH-1	HOT WATER	TA	STAD-3/4	3/4"	2.06	32	2.11	FO-40,FC-00
UH-3	HOT WATER	TA	STAD-3/4	3/4"	2.06	32	2.11	FO-40,FC-00
UH-4	HOT WATER	TA	STAD-3/4	3/4"	2.06	32	2.11	FO-40,FC-00
RP-A TOI. A-200A	HOT WATER	B&G	CB-3/4	3/4"	0.25	50	0.30	FO-0-50-FC
RP-A TOI. A-200B	HOT WATER	B&G	CB-3/4	3/4"	0.25	50	0.30	FO-0-50-FC
RP-A TOI. RM. 214	HOT WATER	B&G	CB-3/4	3/4"	0.25	50	0.30	FO-0-50-FC
RP-A TOI. G-100B	HOT WATER	B&G	CB-3/4	3/4"	0.25	50	0.30	FO-0-50-FC
RP-A TOI. G-100B	HOT WATER	B&G	CB-3/4	3/4"	0.25	48	0.28	FO-0-50-FC
RP-A TOI. G-100C	HOT WATER	B&G	CB-3/4	3/4"	0.25	50	0.30	FO-0-50-FC
RP-A TOI. G-100C	HOT WATER	B&G	CB-3/4	3/4"	0.25	50	0.29	FO-0-50-FC

ABBREVIATIONS AND DEFINITIONS

- 1WCD ONE WAY BLOW PATTERN CEILING DIFFUSER
- 2WCD TWO WAY BLOW PATTERN CEILING DIFFUSER
- 3WCD THREE WAY BLOW PATTERN CEILING DIFFUSER
- 4WCD FOUR WAY BLOW PATTERN CEILING DIFFUSER
- BHP BRAKE HORSEPOWER
- CAV CONSTANT AIR VOLUME
- CFM CUBIC FEET PER MINUTE AIR FLOW
- CG, CR CEILING GRILL, CELING REGISTER
- CC COOLING COIL
- DIA DIAMETER
- DNL DATA NOT LEGIBLE OR AVAILABLE ON EQUIPMENT
- DPR DAMPER
- EA EXHAUST AIR
- EFF EFFICIENCY
- EG, ER EXHAUST GRILLE, EXHAUST REGISTER
- E.S.P. EXTERNAL STATIC PRESSURE
- EXIST EXISTING
- FF FINAL FILTER
- FPM FEET PER MINUTE AIR VELOCITY
- FPS FEET PER SECOND WATER VELOCITY
- FT FOOT (FEET) LENGTH
- GPM GALLONS PER MINUTE FLOW
- HC HEATING COIL
- HF HEPA FILTER
- HP HORSEPOWER
- HRC, HRW HEAT RECOVERY CORE, HEAT RECOVERY WHEEL
- IN. WC INCHES WATER COLUMN PRESSURE
- LBG LINEAR BAR GRILL
- LD LINEAR DIFFUSER
- N.A., N.APP. DEVICE NOT ACCESSIBLE, NOT APPLICABLE
- N.I., N.S. NOT INSTALLED, NOT SPECIFIED
- OA OUTSIDE AIR
- OED OPEN ENDED DUCT
- PFAC POWER FACTOR
- PF PREFILTER
- PSI POUNDS PER SQUARE INCH PRESSURE
- PSID POUNDS PER SQUARE INCH DIFFERENTIAL PERSSURE
- PSIG POUNDS PER SQUARE INCH GAUGE PRESSURE
- RA RETURN AIR
- RG, RR, RCD RETURN GRILLE, RETURN REGISTER, ROUND CEILING DIFFUSER
- RND ROUND
- RPM REVOLUTIONS PER MINUTE ROTATIONAL SPEED
- SA SUPPLY AIR
- SG, SR SUPPLY GRILL, SUPPLY REGISTER
- SQFT SQUARE FEET AREA
- S.P. STATIC PRESSURE
- T.S.P. TOTAL STATIC PRESSURE
- VAV VARIABLE AIR VOLUME BOX
- V.P. VELOCITY PRESSURE
- VD VOLUME DAMPER
- WMS WIRE MESH SCREEN

EXHIBIT 8

HVAC owner training confirmation, training of 8/31/2026 (sent to March 10/6/2026)

NORTHERN WOLVES
AIR CONDITIONING

Northern Wolves Inc.
55 9th Street, Unit 55A-2, Brooklyn, NY 11215
(347) 463-9248 | hello@northernwolvesac.com | northernwolvesac.com

October 5, 2026

March Associates Construction, Inc.
Attn: Gabriel Miani, P.E., Senior Project Manager
Project: Saddle River Day School, 147 Chestnut Ridge Rd, Saddle River, NJ 07458

Re: Certification of HVAC Owner Training

Northern Wolves Inc. hereby confirms that on Monday, August 31, 2026, we provided on-site operation and maintenance training to the Saddle River Day School maintenance team on the HVAC equipment installed under our subcontract. The training consisted of a walkthrough of the building and roof, with a review at each equipment type.

Topics Covered

- **Maintenance points:** filters, screens and strainers that must be changed or monitored, and recommended service intervals.
- **Critical valves and shutoffs:** location and operation of isolation valves, control valves and make-up water.
- **Emergency shutdown:** boiler emergency shutoff, equipment disconnects and kill switches.
- **Troubleshooting:** reading unit alarms and trouble codes, basic checks, and who to contact for service.

Equipment Covered

- **Boiler room:** condensing boilers, pumps and VFDs, emergency shutoffs, valving, make-up water, chemical feeder, strainers, air separator and expansion tank.
- **Rooftop units (RTUs):** filters, valving, trouble codes, ductwork and dampers.
- **Split systems:** indoor units and rooftop condensing units.
- **VAV boxes:** hot water reheat coils and valving.
- **Cabinet and electric unit heaters (CUH/EUH):** maintenance and valving.
- **Fin tube radiation and radiant ceiling panels:** maintenance and valving.
- **Exhaust fans:** lab hood exhaust fans and toilet exhaust fans.
- **Destratification fans.**

Building Management System (BMS) training was provided separately by AME, Inc., the controls subcontractor, in accordance with Section 23 09 23.

Sincerely,

Andrei Kastanyan,
09/01/2026

Northern Wolves Inc.
